

# Aggregate Optimization Chart

MIX ID'S: DDD0K7E7, DDD0K7E8 and DDD0K7E9

Production Gradation Report

**PLANT #:** **P-102**

Sample Date: 7/16/18

Concrete Grade: DM

Contractor: \_\_\_\_\_

Dates Test Represents: 7/17/2018 through 7/23/2018

MDOT No.: \_\_\_\_\_

Agg. Class	Pit #	Source	Weight (SSD)	ft <sup>3</sup>	Specific Gravity	% Contribution
6AA	58-003	Stoneco	1475	8.79	2.69	49.2
26A	58-003	Stoneco	370	2.20	2.69	12.4
2NS	38-046	Chelsea	1150	6.95	2.65	38.4
<b>Total Wt</b>			<b>2995</b>	<b>17.95</b>		<b>100.0</b>

<----- Verify this number is 100%



**Superior Materials, LLC**  
 30701 W. 10 Mile Rd.  
 Suite 500  
 Farmington Hills, MI 48336

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	99.6	100.0	100.0	99.8	0.2	0.2
3/4"	77.1	100.0	100.0	88.7	11.1	11.3
1/2"	36.8	99.6	100.0	68.8	19.9	31.2
3/8"	16.4	83.8	100.0	56.8	12.0	43.2
#4	2.8	21.2	100.0	42.4	14.4	57.6
#8	1.3	6.5	87.0	34.8	7.5	65.2
#16	0.8	2.8	62.0	24.5	10.3	75.5
#30	0.6	1.8	42.0	16.6	7.9	83.4
#50	0.6	1.6	21.0	8.6	8.1	91.4
#100	0.4	1.5	5.0	2.3	6.3	97.7
LBW	0.7	1.2	0.8	0.8	1.5	99.2


\*Maximum % Retained must be above the 3/8" sieve.  
 \*Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation  Batch Plant Gradations  Aggregate Supplier Gradations

Adjusted WF Initial Production Sample (IPS)

<b>Coarseness Factor:</b>	<b>66</b>	<b>Workability Factor:</b>	<b>35</b>	<b>37.3</b>	<b>Coarseness Factor:</b>	<b>61</b>
---------------------------	-----------	----------------------------	-----------	-------------	---------------------------	-----------

<b>Workability Factor:</b>	<b>36</b>
----------------------------	-----------

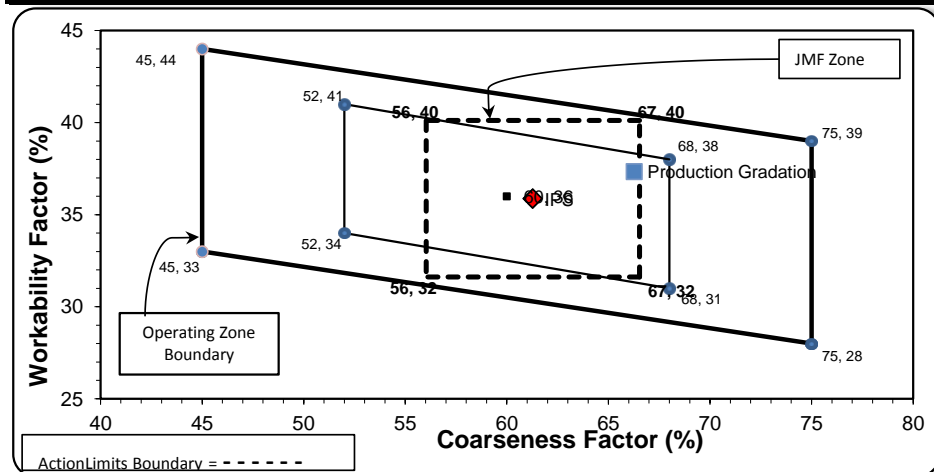

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	99.3	0.7	0.7
3/4"	89.2	10.1	10.8
1/2"	70.7	18.5	29.3
3/8"	60.7	10.0	39.3
#4	44.4	16.3	55.6
#8	35.9	8.5	64.1
#16	27.3	8.6	72.7
#30	19.1	8.2	80.9
#50	7.4	11.7	92.6
#100	1.9	5.6	98.1
LBW	0.7	1.2	99.3

PREPARED BY:  
 SM, LLC Technical Service

Approved By:

# Aggregate Optimization Chart

MIX ID'S: DDD0K7E7, DDD0K7E8 and DDD0K7E9

Production Gradation Report

**PLANT #:** **P-103**

Sample Date: 7/16/18

Concrete Grade: DM

Contractor: \_\_\_\_\_

Dates Test Represents: 7/17/2018 through 7/23/2018

MDOT No.: \_\_\_\_\_

Agg. Class	Pit #	Source	Weight (SSD)	ft <sup>3</sup>	Specific Gravity	% Contribution
6AA	58-003	Stoneco	1475	8.79	2.69	49.2
26A	58-003	Stoneco	370	2.20	2.69	12.4
2NS	38-046	Chelsea	1150	6.95	2.65	38.4
<b>Total Wt</b>			<b>2995</b>	<b>17.95</b>		<b>100.0</b>

<----- Verify this number is 100%



**Superior Materials, LLC**  
 30701 W. 10 Mile Rd.  
 Suite 500  
 Farmington Hills, MI 48336

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	99.6	100.0	100.0	99.8	0.2	0.2
3/4"	77.1	100.0	100.0	88.7	11.1	11.3
1/2"	36.8	99.6	100.0	68.8	19.9	31.2
3/8"	16.4	83.8	100.0	56.8	12.0	43.2
#4	2.8	21.2	100.0	42.4	14.4	57.6
#8	1.3	6.5	87.0	34.8	7.5	65.2
#16	0.8	2.8	62.0	24.5	10.3	75.5
#30	0.6	1.8	42.0	16.6	7.9	83.4
#50	0.6	1.6	21.0	8.6	8.1	91.4
#100	0.4	1.5	5.0	2.3	6.3	97.7
LBW	0.7	1.2	0.8	0.8	1.5	99.2


\*Maximum % Retained must be above the 3/8" sieve.  
 \*Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation  Batch Plant Gradations  Aggregate Supplier Gradations

Adjusted WF Initial Production Sample (IPS)

<b>Coarseness Factor:</b>	<b>66</b>	<b>Workability Factor:</b>	<b>35</b>	<b>37.3</b>	<b>Coarseness Factor:</b>	<b>61</b>
---------------------------	-----------	----------------------------	-----------	-------------	---------------------------	-----------

<b>Workability Factor:</b>	<b>36</b>
----------------------------	-----------

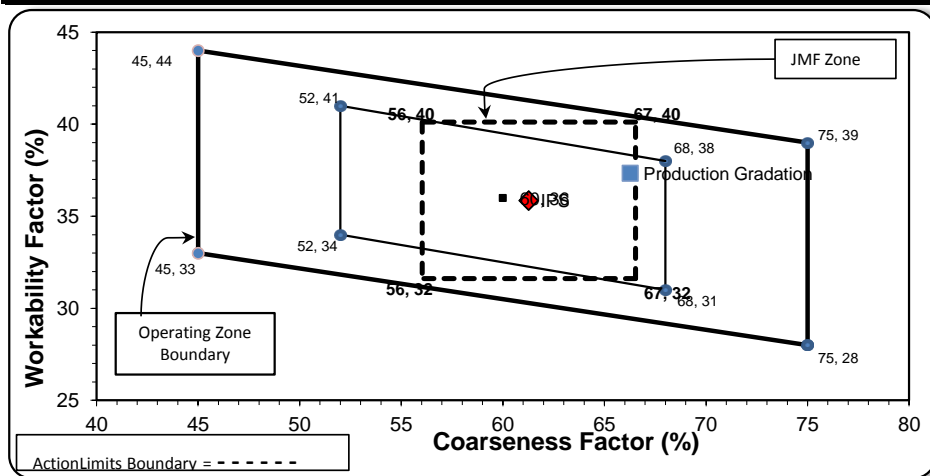

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	99.3	0.7	0.7
3/4"	89.2	10.1	10.8
1/2"	70.7	18.5	29.3
3/8"	60.7	10.0	39.3
#4	44.4	16.3	55.6
#8	35.9	8.5	64.1
#16	27.3	8.6	72.7
#30	19.1	8.2	80.9
#50	7.4	11.7	92.6
#100	1.9	5.6	98.1
LBW	0.7	1.2	99.3

PREPARED BY:  
 SM, LLC Technical Service

Approved BY:

# Aggregate Optimization Chart

MIX ID'S: DDD0K7E7, DDD0K7E8 and DDD0K7E9

Production Gradation Report

**PLANT #:** **P-32**

Sample Date: 7/16/18

Concrete Grade: **DM**

Contractor: \_\_\_\_\_

Dates Test Represents: 7/17/2018 through 7/23/2018

MDOT No.: \_\_\_\_\_

Agg. Class	Pit #	Source	Weight (SSD)	ft <sup>3</sup>	Specific Gravity	% Contribution
6AA	71-47	Presque Isle	1448	8.86	2.62	49.1
26A	71-47	Presque Isle	300	1.83	2.62	10.2
2NS	95-13	Smelter Bay	1200	7.26	2.65	40.7
<b>Total Wt</b>			<b>2948</b>	<b>17.95</b>		<b>100.0</b>

<----- Verify this number is 100%



**Superior Materials, LLC**  
 30701 W. 10 Mile Rd.  
 Suite 500  
 Farmington Hills, MI 48336

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	100.0	100.0	100.0	100.0	0.0	0.0
3/4"	91.9	100.0	100.0	96.0	4.0	4.0
1/2"	48.6	95.6	100.0	74.3	21.7	25.7
3/8"	23.4	83.1	100.0	60.7	13.6	39.3
#4	2.6	21.0	97.2	43.0	17.7	57.0
#8	1.6	6.4	84.4	35.8	7.2	64.2
#16	1.4	3.6	67.3	28.4	7.3	71.6
#30	1.4	2.9	47.2	20.2	8.3	79.8
#50	1.3	2.7	21.6	9.7	10.5	90.3
#100	1.3	2.4	6.6	3.6	6.1	96.4
LBW	1.0	2.0	1.2	1.2	2.4	98.8


\*Maximum % Retained must be above the 3/8" sieve.  
 \*Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation  Batch Plant Gradations  Aggregate Supplier Gradations

Adjusted WF Initial Production Sample (IPS)

<b>Coarseness Factor:</b>	<b>61</b>	<b>Workability Factor:</b>	<b>36</b>	<b>38.3</b>	<b>Coarseness Factor:</b>	<b>62</b>
---------------------------	-----------	----------------------------	-----------	-------------	---------------------------	-----------

<b>Workability Factor:</b>	<b>36</b>
----------------------------	-----------

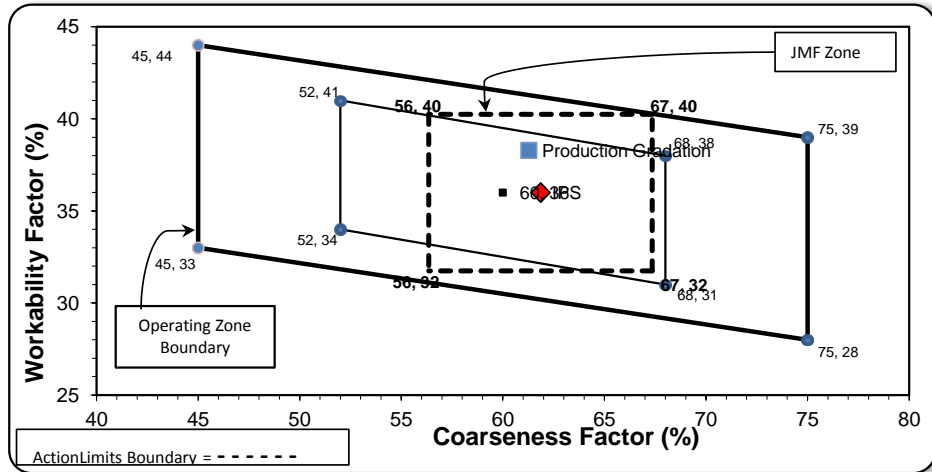

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	100.0	0.0	0.0
3/4"	95.0	5.0	5.0
1/2"	72.3	22.8	27.7
3/8"	60.4	11.8	39.6
#4	42.6	17.8	57.4
#8	36.0	6.6	64.0
#16	29.5	6.5	70.5
#30	20.3	9.2	79.7
#50	9.5	10.8	90.5
#100	3.4	6.1	96.6
LBW	1.3	2.1	98.7

PREPARED BY:  
 SM, LLC Technical Service

Approved By:

# Aggregate Optimization Chart

MIX ID'S: DDD0K7E7, DDD0K7E8 and DDD0K7E9

Production Gradation Report

**PLANT #:** **P-35**

Sample Date: 7/16/18

Concrete Grade: **DM**

Contractor: \_\_\_\_\_

Dates Test Represents: 7/17/2018 through 7/23/2018

MDOT No.: \_\_\_\_\_

Agg. Class	Pit #	Source	Weight (SSD)	ft <sup>3</sup>	Specific Gravity	% Contribution
6AA	58-003	Stoneco	1490	8.88	2.69	49.8
26A	58-003	Stoneco	250	1.49	2.69	8.4
2NS	81-93	Burmeister	1250	7.59	2.64	41.8
<b>Total Wt</b>			<b>2990</b>	<b>17.95</b>		<b>100.0</b>

<----- Verify this number is 100%



**Superior Materials, LLC**  
 30701 W. 10 Mile Rd.  
 Suite 500  
 Farmington Hills, MI 48336

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	99.6	100.0	100.0	99.8	0.2	0.2
3/4"	77.1	100.0	100.0	88.6	11.2	11.4
1/2"	36.8	99.6	100.0	68.5	20.1	31.5
3/8"	16.4	83.8	100.0	57.0	11.5	43.0
#4	2.8	21.2	95.4	43.1	13.9	56.9
#8	1.3	6.5	80.6	34.9	8.2	65.1
#16	0.8	2.8	63.9	27.3	7.5	72.7
#30	0.6	1.8	45.8	19.6	7.8	80.4
#50	0.6	1.6	22.2	9.7	9.9	90.3
#100	0.4	1.5	5.0	2.4	7.3	97.6
LBW	0.7	1.2	1.3	1.0	1.4	99.0


\*Maximum % Retained must be above the 3/8" sieve.  
 \*Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation  Batch Plant Gradations  Aggregate Supplier Gradations

Adjusted WF Initial Production Sample (IPS)

<b>Coarseness Factor:</b>	<b>66</b>	<b>Workability Factor:</b>	<b>35</b>	<b>37.4</b>	<b>Coarseness Factor:</b>	<b>61</b>
---------------------------	-----------	----------------------------	-----------	-------------	---------------------------	-----------

<b>Workability Factor:</b>	<b>36</b>
----------------------------	-----------

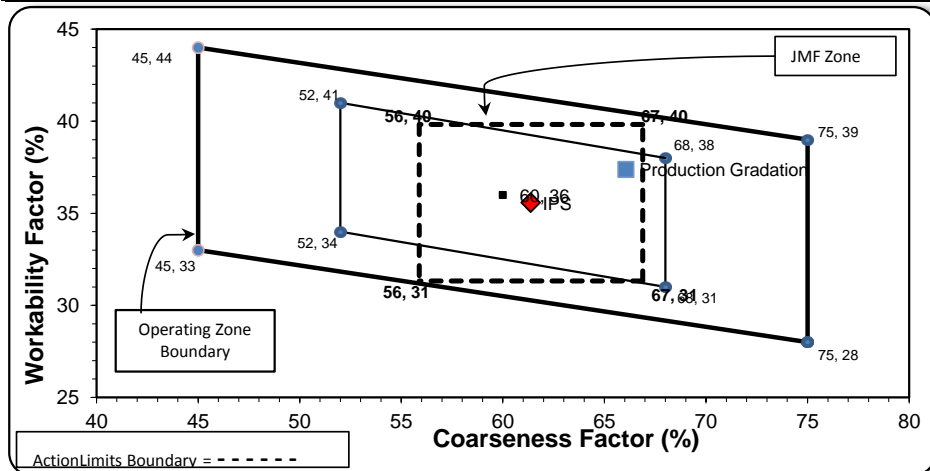

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	99.3	0.7	0.7
3/4"	89.1	10.2	10.9
1/2"	70.5	18.6	29.5
3/8"	60.5	10.0	39.5
#4	44.1	16.4	55.9
#8	35.6	8.5	64.4
#16	27.7	7.9	72.3
#30	20.6	7.1	79.4
#50	8.7	11.8	91.3
#100	1.6	7.1	98.4
LBW	1.1	0.6	98.9

PREPARED BY:  
 SM, LLC Technical Service

Approved By:

# Aggregate Optimization Chart

MIX ID'S: DDD0K7E7, DDD0K7E8 and DDD0K7E9

Production Gradation Report

**PLANT #:** **P-36**

Sample Date: 7/16/18

Concrete Grade: **DM**

Contractor: \_\_\_\_\_

Dates Test Represents: 7/17/2018 through 7/23/2018

MDOT No.: \_\_\_\_\_

Agg. Class	Pit #	Source	Weight (SSD)	ft <sup>3</sup>	Specific Gravity	% Contribution
6AA	71-47	Presque Isle	1300	7.95	2.62	44.1
26A	71-47	Presque Isle	500	3.06	2.62	16.9
2NS	63-92	AA Grange Hall	1150	6.95	2.65	39.0
<b>Total Wt</b>			<b>2950</b>	<b>17.96</b>		<b>100.0</b>

<----- Verify this number is 100%



**Superior Materials, LLC**  
 30701 W. 10 Mile Rd.  
 Suite 500  
 Farmington Hills, MI 48336

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	100.0	100.0	100.0	100.0	0.0	0.0
3/4"	84.5	100.0	100.0	93.2	6.8	6.8
1/2"	36.2	95.6	100.0	71.1	22.0	28.9
3/8"	14.1	83.1	100.0	59.3	11.9	40.7
#4	1.9	21.0	97.0	42.2	17.1	57.8
#8	1.3	6.4	83.8	34.3	7.9	65.7
#16	1.2	3.6	69.3	28.2	6.2	71.8
#30	1.2	2.9	52.9	21.6	6.5	78.4
#50	1.1	2.7	26.6	11.3	10.3	88.7
#100	1.1	2.4	4.5	2.6	8.7	97.4
LBW	1.0	2.0	0.2	0.9	1.8	99.1


\*Maximum % Retained must be above the 3/8" sieve.  
 \*Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation  Batch Plant Gradations  Aggregate Supplier Gradations

Adjusted WF Initial Production Sample (IPS)

<b>Coarseness Factor:</b>	<b>62</b>	<b>Workability Factor:</b>	<b>34</b>	<b>Adjusted WF</b>	<b>36.8</b>
---------------------------	-----------	----------------------------	-----------	--------------------	-------------

<b>Coarseness Factor:</b>	<b>63</b>
<b>Workability Factor:</b>	<b>35</b>

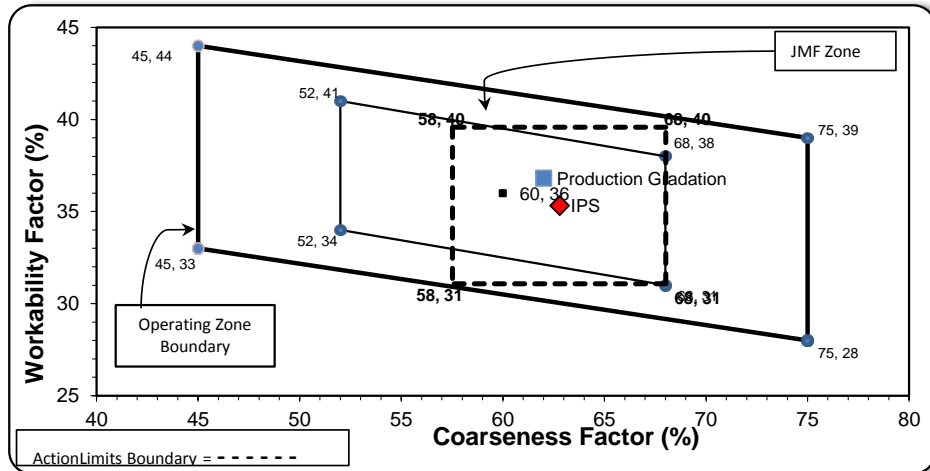

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	99.9	0.1	0.1
3/4"	89.1	10.8	10.9
1/2"	71.3	17.8	28.7
3/8"	59.4	11.9	40.6
#4	42.6	16.8	57.4
#8	35.3	7.3	64.7
#16	28.5	6.8	71.5
#30	20.9	7.6	79.1
#50	9.0	12.0	91.0
#100	1.7	7.3	98.3
LBW	0.7	1.0	99.3

PREPARED BY:  
 SM, LLC Technical Service

Approved By:

# Aggregate Optimization Chart

MIX ID'S: DDD0K7E7, DDD0K7E8 and DDD0K7E9

Production Gradation Report

**PLANT #:** **P-02**

Sample Date: 7/16/18

Concrete Grade: **DM**

Contractor: \_\_\_\_\_

Dates Test Represents: 7/17/2018 through 7/23/2018

MDOT No.: \_\_\_\_\_

Agg. Class	Pit #	Source	Weight (SSD)	ft <sup>3</sup>	Specific Gravity	% Contribution
6AA	71-47	Presque Isle	1300	7.95	2.62	44.1
26A	71-47	Presque Isle	500	3.06	2.62	16.9
2NS	47-16	Buno Road	1150	6.95	2.65	39.0
<b>Total Wt</b>			<b>2950</b>	<b>17.96</b>		<b>100.0</b>

<----- Verify this number is 100%



**Superior Materials, LLC**  
 30701 W. 10 Mile Rd.  
 Suite 500  
 Farmington Hills, MI 48336

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	100.0	100.0	100.0	100.0	0.0	0.0
3/4"	84.5	100.0	100.0	93.2	6.8	6.8
1/2"	36.2	95.6	100.0	71.1	22.0	28.9
3/8"	14.1	83.1	100.0	59.3	11.9	40.7
#4	1.9	21.0	96.3	41.9	17.3	58.1
#8	1.3	6.4	85.8	35.1	6.8	64.9
#16	1.2	3.6	72.1	29.2	5.9	70.8
#30	1.2	2.9	52.4	21.4	7.8	78.6
#50	1.1	2.7	18.6	8.2	13.3	91.8
#100	1.1	2.4	2.4	1.8	6.4	98.2
LBW	1.0	2.0	0.4	0.9	0.9	99.1


\*Maximum % Retained must be above the 3/8" sieve.  
 \*Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation  Batch Plant Gradations  Aggregate Supplier Gradations

Adjusted WF Initial Production Sample (IPS)

<b>Coarseness Factor:</b>	<b>63</b>	<b>Workability Factor:</b>	<b>35</b>	<b>Adjusted WF</b>	<b>37.6</b>
---------------------------	-----------	----------------------------	-----------	--------------------	-------------

<b>Coarseness Factor:</b>	<b>63</b>
<b>Workability Factor:</b>	<b>35</b>

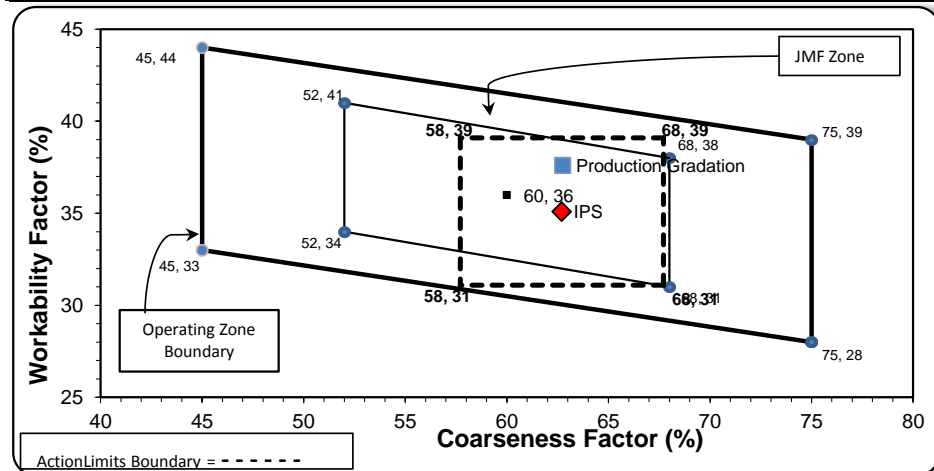

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	100.0	0.0	0.0
3/4"	95.1	4.9	4.9
1/2"	74.6	20.5	25.4
3/8"	59.3	15.3	40.7
#4	42.1	17.2	57.9
#8	35.1	7.1	64.9
#16	29.2	5.9	70.8
#30	21.9	7.3	78.1
#50	9.6	12.4	90.4
#100	2.4	7.2	97.6
LBW	0.9	1.5	99.1

PREPARED BY:  
 SM, LLC Technical Service

Approved By:
