

# Aggregate Optimization Chart

MIX ID'S: DDD0K7E7, DDD0K7E8 and DDD0K7E9

Production Gradation Report

**PLANT #:** **P-102**

Sample Date: 7/30/18

Concrete Grade: DM

Contractor: \_\_\_\_\_

Dates Test Represents: 7/31/2018 through 8/6/2018

MDOT No.: \_\_\_\_\_

Agg. Class	Pit #	Source	Weight (SSD)	ft <sup>3</sup>	Specific Gravity	% Contribution
6AA	58-003	Stoneco	1475	8.79	2.69	49.2
26A	58-003	Stoneco	370	2.20	2.69	12.4
2NS	38-046	Chelsea	1150	6.95	2.65	38.4
<b>Total Wt</b>			<b>2995</b>	<b>17.95</b>		<b>100.0</b>

<----- Verify this number is 100%

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	99.2	100.0	100.0	99.6	0.4	0.4
3/4"	77.2	100.0	100.0	88.8	10.8	11.2
1/2"	43.0	99.6	100.0	71.9	16.9	28.1
3/8"	19.0	90.0	100.0	58.9	13.0	41.1
#4	3.8	22.8	100.0	43.1	15.8	56.9
#8	1.2	8.5	89.0	35.8	7.3	64.2
#16	0.8	3.9	65.0	25.8	10.0	74.2
#30	0.6	2.5	46.0	18.3	7.6	81.7
#50	0.6	2.2	27.0	10.9	7.3	89.1
#100	0.4	2.0	7.0	3.1	7.8	96.9
LBW	0.5	1.8	1.2	0.9	2.2	99.1



**Superior Materials, LLC**  
 30701 W. 10 Mile Rd.  
 Suite 500  
 Farmington Hills, MI 48336


\*Maximum % Retained must be above the 3/8" sieve.  
 \*Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation  Batch Plant Gradations  Aggregate Supplier Gradations

Adjusted WF Initial Production Sample (IPS)

<b>Coarseness Factor:</b>	<b>64</b>	<b>Workability Factor:</b>	<b>36</b>
---------------------------	-----------	----------------------------	-----------

<b>Coarseness Factor:</b>	<b>61</b>
<b>Workability Factor:</b>	<b>36</b>

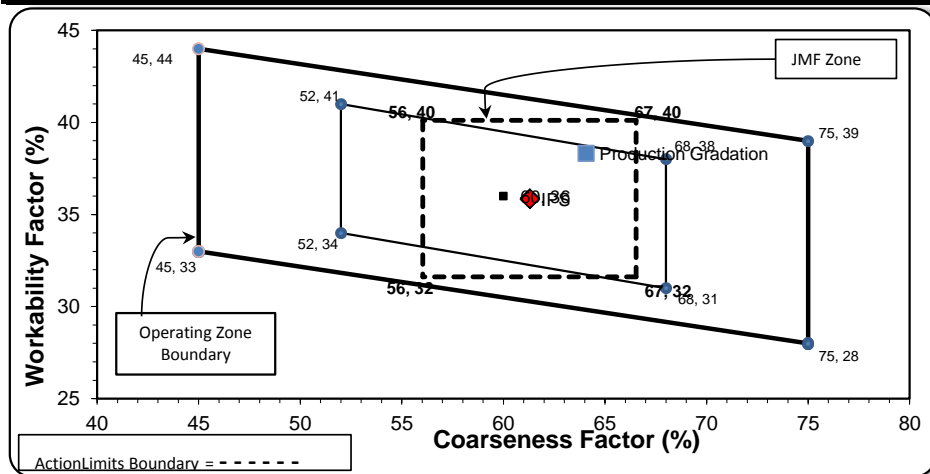

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	99.3	0.7	0.7
3/4"	89.2	10.1	10.8
1/2"	70.7	18.5	29.3
3/8"	60.7	10.0	39.3
#4	44.4	16.3	55.6
#8	35.9	8.5	64.1
#16	27.3	8.6	72.7
#30	19.1	8.2	80.9
#50	7.4	11.7	92.6
#100	1.9	5.6	98.1
LBW	0.7	1.2	99.3

PREPARED BY:  
 SM, LLC Technical Service

Approved By:

# Aggregate Optimization Chart

MIX ID'S: DDD0K7E7, DDD0K7E8 and DDD0K7E9

Production Gradation Report

**PLANT #:** **P-32**

Sample Date: 7/30/18

Concrete Grade: DM

Contractor: \_\_\_\_\_

Dates Test Represents: 7/31/2018 through 8/6/2018

MDOT No.: \_\_\_\_\_

Agg. Class	Pit #	Source	Weight (SSD)	ft <sup>3</sup>	Specific Gravity	% Contribution
6AA	71-47	Presque Isle	1525	9.33	2.62	51.7
26A	71-47	Presque Isle	250	1.53	2.62	8.5
2NS	95-13	Smelter Bay	1175	7.11	2.65	39.8
<b>Total Wt</b>			<b>2950</b>	<b>17.96</b>		<b>100.0</b>

<----- Verify this number is 100%

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	100.0	100.0	100.0	100.0	0.0	0.0
3/4"	90.2	100.0	100.0	94.9	5.1	5.1
1/2"	47.9	96.6	100.0	72.8	22.2	27.2
3/8"	21.3	86.1	100.0	58.1	14.6	41.9
#4	1.5	26.5	96.9	41.6	16.5	58.4
#8	0.5	9.6	83.4	34.3	7.3	65.7
#16	0.4	4.8	66.3	27.0	7.3	73.0
#30	0.3	3.6	45.3	18.5	8.5	81.5
#50	0.3	3.1	18.6	7.8	10.7	92.2
#100	0.2	2.8	4.2	2.0	5.8	98.0
LBW	0.1	2.2	0.8	0.6	1.5	99.4



**Superior Materials, LLC**  
 30701 W. 10 Mile Rd.  
 Suite 500  
 Farmington Hills, MI 48336


\*Maximum % Retained must be above the 3/8" sieve.  
 \*Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation  Batch Plant Gradations  Aggregate Supplier Gradations

Adjusted WF Initial Production Sample (IPS)

<b>Coarseness Factor:</b>	<b>64</b>	<b>Workability Factor:</b>	<b>34</b>	<b>Adjusted WF</b>	<b>36.8</b>
---------------------------	-----------	----------------------------	-----------	--------------------	-------------

<b>Coarseness Factor:</b>	<b>62</b>
<b>Workability Factor:</b>	<b>36</b>

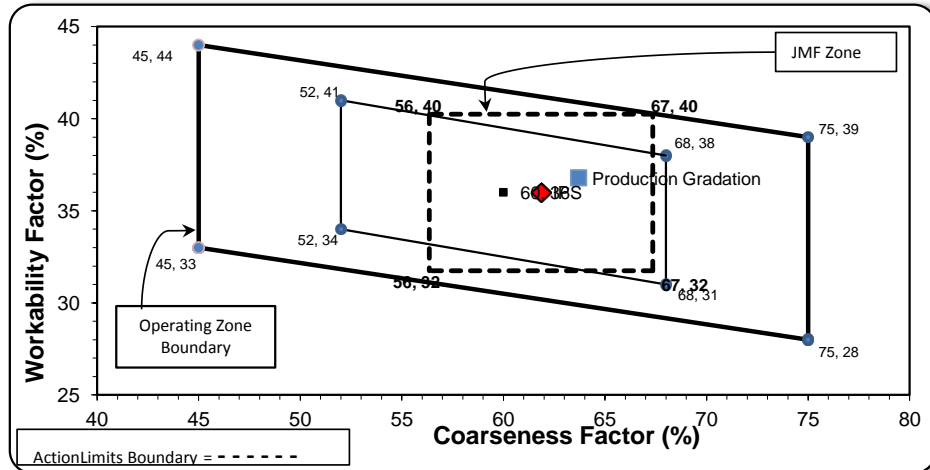

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	100.0	0.0	0.0
3/4"	95.0	5.0	5.0
1/2"	72.3	22.8	27.7
3/8"	60.4	11.8	39.6
#4	42.6	17.8	57.4
#8	36.0	6.6	64.0
#16	29.5	6.5	70.5
#30	20.3	9.2	79.7
#50	9.5	10.8	90.5
#100	3.4	6.1	96.6
LBW	1.3	2.1	98.7

PREPARED BY:  
 SM, LLC Technical Service

Approved By:

# Aggregate Optimization Chart

MIX ID'S: DDD0K7E7, DDD0K7E8 and DDD0K7E9

Production Gradation Report

**PLANT #:** **P-35**

Sample Date: 7/30/18

Concrete Grade: DM

Contractor: \_\_\_\_\_

Dates Test Represents: 7/31/2018 through 8/6/2018

MDOT No.: \_\_\_\_\_

Agg. Class	Pit #	Source	Weight (SSD)	ft <sup>3</sup>	Specific Gravity	% Contribution
6AA	58-003	Stoneco	1490	8.88	2.69	49.8
26A	58-003	Stoneco	250	1.49	2.69	8.4
2NS	81-93	Burmeister	1250	7.59	2.64	41.8
<b>Total Wt</b>			<b>2990</b>	<b>17.95</b>		<b>100.0</b>

<----- Verify this number is 100%



**Superior Materials, LLC**  
 30701 W. 10 Mile Rd.  
 Suite 500  
 Farmington Hills, MI 48336

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	99.2	100.0	100.0	99.6	0.4	0.4
3/4"	77.2	100.0	100.0	88.6	11.0	11.4
1/2"	43.0	99.6	100.0	71.6	17.1	28.4
3/8"	19.0	90.0	100.0	58.8	12.8	41.2
#4	3.8	22.8	95.3	43.6	15.2	56.4
#8	1.2	8.5	79.2	34.4	9.2	65.6
#16	0.8	3.9	61.3	26.4	8.1	73.6
#30	0.6	2.5	42.3	18.2	8.2	81.8
#50	0.6	2.2	16.8	7.5	10.7	92.5
#100	0.4	2.0	3.9	2.0	5.5	98.0
LBW	0.5	1.8	1.2	0.9	1.1	99.1

\*Maximum % Retained must be above the 3/8" sieve.  
 \*Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.


Production Gradation  Batch Plant Gradations  Aggregate Supplier Gradations

Adjusted WF Initial Production Sample (IPS)

<b>Coarseness Factor:</b>	<b>63</b>	<b>Workability Factor:</b>	<b>34</b>
---------------------------	-----------	----------------------------	-----------

<b>Coarseness Factor:</b>	<b>61</b>
<b>Workability Factor:</b>	<b>36</b>

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	99.3	0.7	0.7
3/4"	89.1	10.2	10.9
1/2"	70.5	18.6	29.5
3/8"	60.5	10.0	39.5
#4	44.1	16.4	55.9
#8	35.6	8.5	64.4
#16	27.7	7.9	72.3
#30	20.6	7.1	79.4
#50	8.7	11.8	91.3
#100	1.6	7.1	98.4
LBW	1.1	0.6	98.9

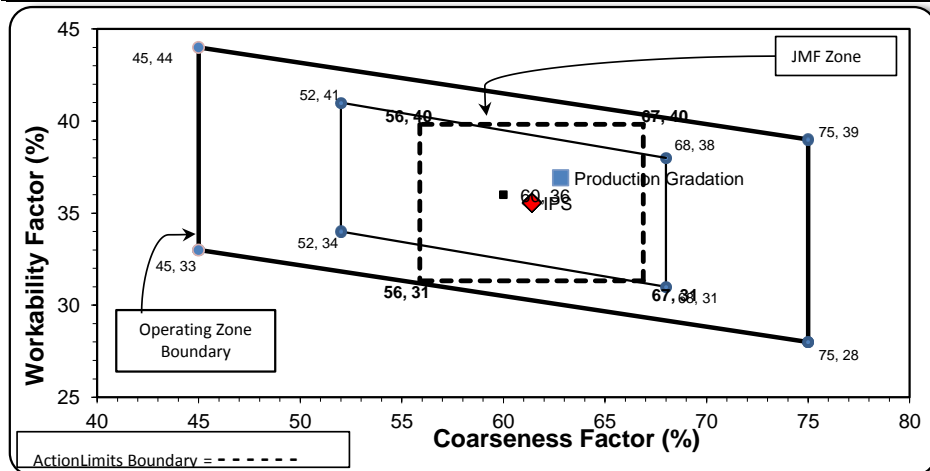

PREPARED BY:  
 SM, LLC Technical Service

Approved By:

# Aggregate Optimization Chart

MIX ID'S: DDD0K7E7, DDD0K7E8 and DDD0K7E9

Production Gradation Report

**PLANT #:** **P-36**

Sample Date: 7/30/18

Concrete Grade: DM

Contractor: \_\_\_\_\_

Dates Test Represents: 7/31/2018 through 8/6/2018

MDOT No.: \_\_\_\_\_

Agg. Class	Pit #	Source	Weight (SSD)	ft <sup>3</sup>	Specific Gravity	% Contribution
6AA	71-47	Presque Isle	1500	9.17	2.62	50.8
26A	71-47	Presque Isle	300	1.83	2.62	10.2
2NS	63-92	AA Grange Hall	1150	6.95	2.65	39.0
<b>Total Wt</b>			<b>2950</b>	<b>17.96</b>		<b>100.0</b>

<----- Verify this number is 100%

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	100.0	100.0	100.0	100.0	0.0	0.0
3/4"	91.4	100.0	100.0	95.6	4.4	4.4
1/2"	47.2	96.6	100.0	72.8	22.8	27.2
3/8"	19.4	86.1	100.0	57.6	15.2	42.4
#4	2.0	26.5	97.4	41.7	15.9	58.3
#8	1.3	9.6	84.7	34.7	7.0	65.3
#16	1.2	4.8	69.8	28.3	6.3	71.7
#30	1.1	3.6	52.3	21.3	7.0	78.7
#50	1.1	3.1	24.6	10.5	10.8	89.5
#100	1.0	2.8	3.8	2.3	8.2	97.7
LBW	0.9	2.2	0.3	0.8	1.5	99.2



**Superior Materials, LLC**  
 30701 W. 10 Mile Rd.  
 Suite 500  
 Farmington Hills, MI 48336

\*Maximum % Retained must be above the 3/8" sieve.  
 \*Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.


Production Gradation  Batch Plant Gradations  Aggregate Supplier Gradations

Adjusted WF Initial Production Sample (IPS)

<b>Coarseness Factor:</b>	<b>65</b>	<b>Workability Factor:</b>	<b>35</b>	<b>Adjusted WF</b>	<b>37.2</b>
---------------------------	-----------	----------------------------	-----------	--------------------	-------------

<b>Coarseness Factor:</b>	<b>63</b>
<b>Workability Factor:</b>	<b>35</b>

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	99.9	0.1	0.1
3/4"	89.1	10.8	10.9
1/2"	71.3	17.8	28.7
3/8"	59.4	11.9	40.6
#4	42.6	16.8	57.4
#8	35.3	7.3	64.7
#16	28.5	6.8	71.5
#30	20.9	7.6	79.1
#50	9.0	12.0	91.0
#100	1.7	7.3	98.3
LBW	0.7	1.0	99.3

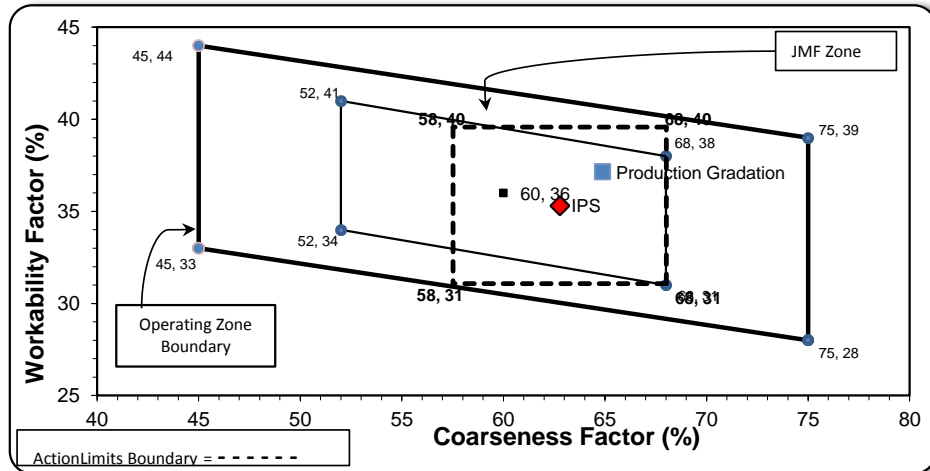

PREPARED BY:  
 SM, LLC Technical Service

Approved By:

# Aggregate Optimization Chart

MIX ID'S: DDD0K7E7, DDD0K7E8 and DDD0K7E9

Production Gradation Report

**PLANT #:** P-02

Sample Date: 7/30/18

Concrete Grade: DM

Contractor: \_\_\_\_\_

Dates Test Represents: 7/31/2018 through 8/6/2018

MDOT No.: \_\_\_\_\_

Agg. Class	Pit #	Source	Weight (SSD)	ft <sup>3</sup>	Specific Gravity	% Contribution
6AA	71-47	Presque Isle	1500	9.17	2.62	50.8
26A	71-47	Presque Isle	300	1.83	2.62	10.2
2NS	47-16	Buno Road	1150	6.95	2.65	39.0
<b>Total Wt</b>			<b>2950</b>	<b>17.96</b>		<b>100.0</b>

<----- Verify this number is 100%

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	100.0	100.0	100.0	100.0	0.0	0.0
3/4"	91.4	100.0	100.0	95.6	4.4	4.4
1/2"	47.2	96.6	100.0	72.8	22.8	27.2
3/8"	19.4	86.1	100.0	57.6	15.2	42.4
#4	2.0	26.5	96.3	41.3	16.4	58.7
#8	1.3	9.6	85.8	35.1	6.2	64.9
#16	1.2	4.8	71.8	29.1	6.0	70.9
#30	1.1	3.6	52.5	21.4	7.7	78.6
#50	1.1	3.1	20.8	9.0	12.4	91.0
#100	1.0	2.8	3.0	2.0	7.0	98.0
LBW	0.9	2.2	0.4	0.8	1.1	99.2



**Superior Materials, LLC**  
 30701 W. 10 Mile Rd.  
 Suite 500  
 Farmington Hills, MI 48336


\*Maximum % Retained must be above the 3/8" sieve.  
 \*Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation  Batch Plant Gradations  Aggregate Supplier Gradations

Adjusted WF Initial Production Sample (IPS)

<b>Coarseness Factor:</b>	<b>65</b>	<b>Workability Factor:</b>	<b>35</b>
---------------------------	-----------	----------------------------	-----------

<b>Coarseness Factor:</b>	<b>63</b>
<b>Workability Factor:</b>	<b>35</b>

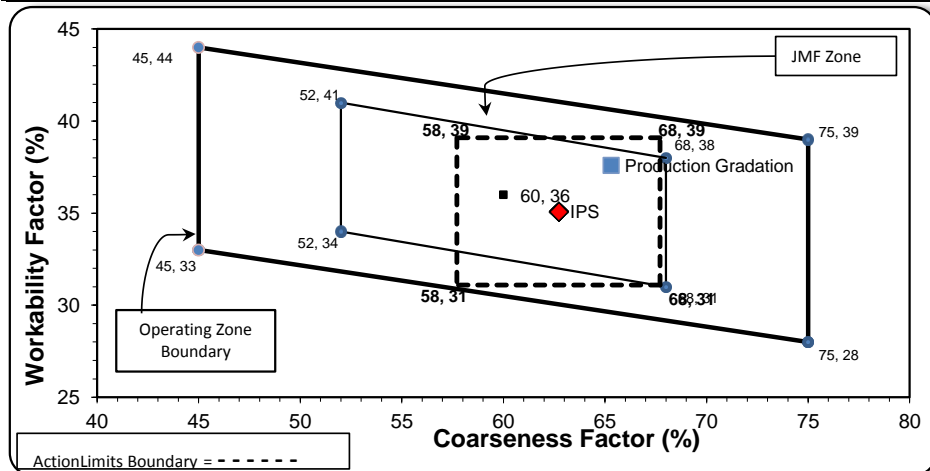

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	100.0	0.0	0.0
3/4"	95.1	4.9	4.9
1/2"	74.6	20.5	25.4
3/8"	59.3	15.3	40.7
#4	42.1	17.2	57.9
#8	35.1	7.1	64.9
#16	29.2	5.9	70.8
#30	21.9	7.3	78.1
#50	9.6	12.4	90.4
#100	2.4	7.2	97.6
LBW	0.9	1.5	99.1

PREPARED BY:  
 SM, LLC Technical Service

Approved By:
