

# Aggregate Optimization Chart

MIX ID'S: DDS257E7, DDS257E5 and DDS257E8

Production Gradation Report

**PLANT #:** **P-103**

Sample Date: 7/10/17

Concrete Grade: **S2M**

Contractor: \_\_\_\_\_

Dates Test Represents: 7/10/2017 to 7/16/2017

MDOT No.: \_\_\_\_\_

Agg. Class	Pit #	Source	Weight (SSD)	ft <sup>3</sup>	Specific Gravity	% Contribution
6AA	58-003	Stoneco	1655	9.86	2.69	52.5
26A	58-003	Stoneco	200	1.19	2.69	6.3
2NS	81-93	Burmeister	1300	7.89	2.64	41.2
<b>Total Wt</b>			<b>3155</b>	<b>18.94</b>		<b>100.0</b>

<----- Verify this number is 100%




**Superior Materials, LLC**  
 30701 W. 10 Mile Rd.  
 Suite 500  
 Farmington Hills, MI 48336

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	98.8	100.0	100.0	99.4	0.6	0.6
3/4"	79.9	100.0	100.0	89.5	9.9	10.5
1/2"	48.6	99.8	100.0	73.0	16.4	27.0
3/8"	20.9	86.1	100.0	57.6	15.4	42.4
#4	3.0	28.9	99.1	44.2	13.4	55.8
#8	1.0	6.2	85.4	36.1	8.1	63.9
#16	1.3	2.9	70.2	29.8	6.3	70.2
#30	1.0	2.3	50.2	21.4	8.4	78.6
#50	0.8	2.0	24.6	10.7	10.7	89.3
#100	0.7	1.9	5.9	2.9	7.8	97.1
LBW	0.5	1.6	1.4	0.9	2.0	99.1

\*Maximum % Retained must be above the 3/8" sieve.  
 \*Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation  Batch Plant Gradations  Aggregate Supplier Gradations

<b>Coarseness Factor:</b>	<b>66</b>	<b>Workability Factor:</b>	<b>36</b>
---------------------------	-----------	----------------------------	-----------

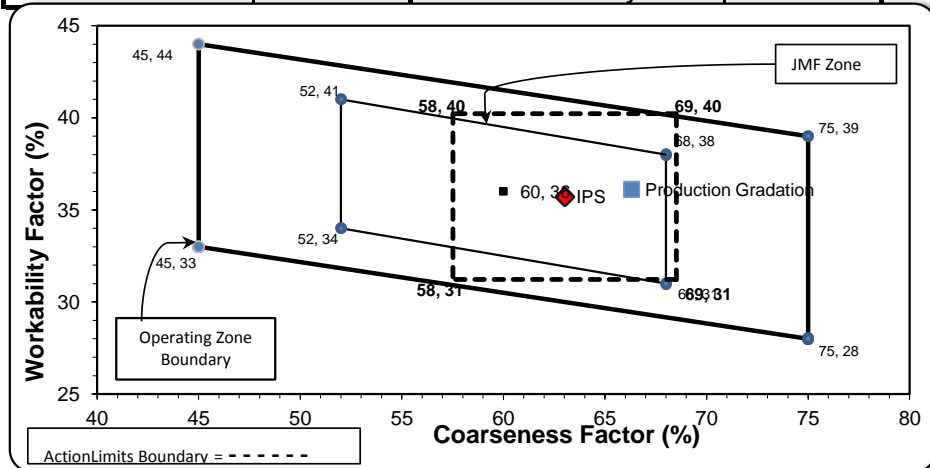

Initial Production Sample (IPS)

<b>Coarseness Factor:</b>	<b>63</b>		
<b>Workability Factor:</b>	<b>36</b>		
Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	99.2	0.8	0.8
3/4"	90.9	8.3	9.1
1/2"	71.3	19.6	28.7
3/8"	59.5	11.8	40.5
#4	43.8	15.7	56.2
#8	35.7	8.1	64.3
#16	27.0	8.7	73.0
#30	18.6	8.4	81.4
#50	6.8	11.8	93.2
#100	1.4	5.4	98.6
LBW	0.6	0.8	99.4

PREPARED BY:  
 SM, LLC Technical Service

Approved BY:

# Aggregate Optimization Chart

MIX ID'S: WSN175E9

Production Gradation Report

**PLANT #:** **P-36**

Sample Date: 7/10/17

Dates Test Represents: 7/10/2017 to 7/16/2017

Concrete Grade: **S2M (SPECIAL, 5000 PSI)**

Contractor: \_\_\_\_\_

MDOT No.: \_\_\_\_\_

Agg. Class	Pit #	Source	Weight (SSD)	ft <sup>3</sup>	Specific Gravity	% Contribution
6AA	58-003	Stoneco	1580	9.41	2.69	52.8
26A	71-47	Presque Isle	200	1.22	2.62	6.7
2NS	63-92	AA Grange Hall	1210	7.32	2.65	40.5
<b>Total Wt</b>			<b>2990</b>	<b>17.95</b>		<b>100.0</b>

<----- Verify this number is 100%

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	98.8	100.0	100.0	99.4	0.6	0.6
3/4"	79.9	100.0	100.0	89.4	10.0	10.6
1/2"	48.6	98.4	100.0	72.7	16.6	27.3
3/8"	20.9	86.4	100.0	57.3	15.4	42.7
#4	3.0	13.5	98.3	42.3	15.0	57.7
#8	1.0	2.8	86.7	35.8	6.5	64.2
#16	1.3	1.8	68.8	28.6	7.2	71.4
#30	1.0	1.6	46.7	19.5	9.1	80.5
#50	0.8	1.6	16.8	7.3	12.2	92.7
#100	0.7	1.4	2.6	1.5	5.8	98.5
LBW	0.5	1.4	0.3	0.5	1.0	99.5


\*Maximum % Retained must be above the 3/8" sieve.  
 \*Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.



**Superior Materials, LLC**  
 30701 W. 10 Mile Rd.  
 Suite 500  
 Farmington Hills, MI 48336

Production Gradation  Batch Plant Gradations  Aggregate Supplier Gradations

<b>Coarseness Factor:</b>	<b>67</b>	<b>Workability Factor:</b>	<b>36</b>
---------------------------	-----------	----------------------------	-----------

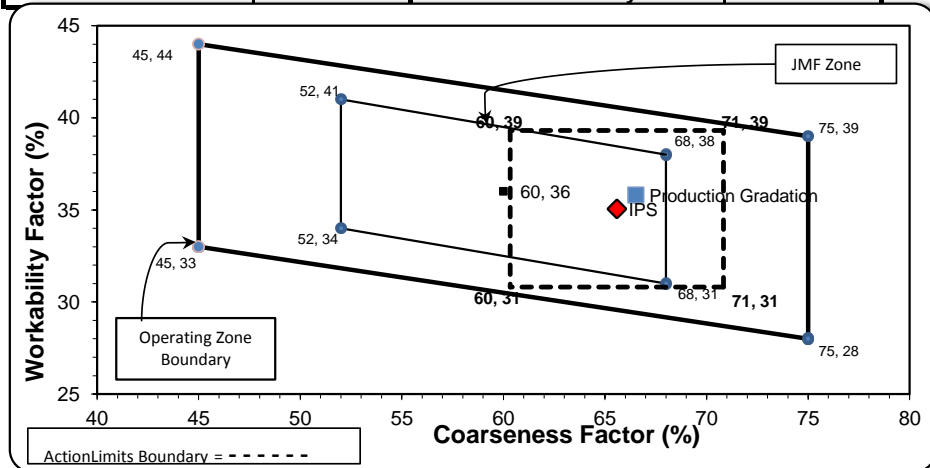

Initial Production Sample (IPS)

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	100.0	0.0	0.0
3/4"	91.7	8.3	8.3
1/2"	66.8	24.8	33.2
3/8"	57.4	9.4	42.6
#4	43.0	14.4	57.0
#8	35.1	7.9	64.9
#16	28.0	7.1	72.0
#30	19.5	8.5	80.5
#50	8.1	11.4	91.9
#100	2.0	6.1	98.0
LBW	0.7	1.3	99.3

PREPARED BY:  
 SM, LLC Technical Service

Approved By:

# Aggregate Optimization Chart

MIX ID'S: DDS257E7, DDS257E5 and DDS257E8

Production Gradation Report

**PLANT #:** **P-38**

Sample Date: 7/10/17

Concrete Grade: **S2M**

Contractor: \_\_\_\_\_

Dates Test Represents: 7/10/2017 to 7/16/2017

MDOT No.: \_\_\_\_\_

Agg. Class	Pit #	Source	Weight (SSD)	ft <sup>3</sup>	Specific Gravity	% Contribution
6AA	58-003	Stoneco	1655	9.86	2.69	52.5
26A	58-003	Stoneco	200	1.19	2.69	6.3
2NS	81-93	Burmeister	1300	7.89	2.64	41.2
<b>Total Wt</b>			<b>3155</b>	<b>18.94</b>		<b>100.0</b>

<----- Verify this number is 100%

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	98.8	100.0	100.0	99.4	0.6	0.6
3/4"	79.9	100.0	100.0	89.5	9.9	10.5
1/2"	48.6	99.8	100.0	73.0	16.4	27.0
3/8"	20.9	86.1	100.0	57.6	15.4	42.4
#4	3.0	28.9	99.1	44.2	13.4	55.8
#8	1.0	6.2	85.4	36.1	8.1	63.9
#16	1.3	2.9	70.2	29.8	6.3	70.2
#30	1.0	2.3	50.2	21.4	8.4	78.6
#50	0.8	2.0	24.6	10.7	10.7	89.3
#100	0.7	1.9	5.9	2.9	7.8	97.1
LBW	0.5	1.6	1.4	0.9	2.0	99.1




**Superior Materials, LLC**  
 30701 W. 10 Mile Rd.  
 Suite 500  
 Farmington Hills, MI 48336

\*Maximum % Retained must be above the 3/8" sieve.  
 \*Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation  Batch Plant Gradations  Aggregate Supplier Gradations

**Coarseness Factor: 66**      **Workability Factor: 36**

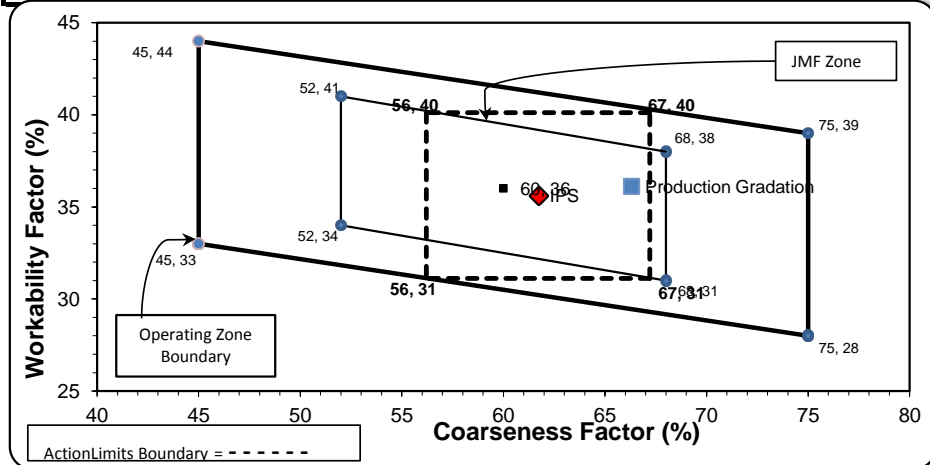

Initial Production Sample (IPS)

Coarseness Factor: 62		Workability Factor: 36	
Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	99.2	0.8	0.8
3/4"	91.1	8.1	8.9
1/2"	72.0	19.1	28.0
3/8"	60.3	11.7	39.7
#4	43.4	16.9	56.6
#8	35.6	7.8	64.4
#16	28.4	7.2	71.6
#30	21.8	6.7	78.2
#50	9.1	12.6	90.9
#100	1.7	7.4	98.3
LBW	1.1	0.6	98.9

PREPARED BY:  
 SM, LLC Technical Service

Approved By:
