

# Aggregate Optimization Chart

MIX ID'S: DDS257E7 and DDS257E8

Production Gradation Report

**PLANT #:** **P-102**

Sample Date: 9/24/18

Concrete Grade: **S2M**

Contractor: \_\_\_\_\_

Dates Test Represents: 9/25/2018 through 10/1/2018

MDOT No.: \_\_\_\_\_

Agg. Class	Pit #	Source	Weight (SSD)	ft <sup>3</sup>	Specific Gravity	% Contribution
6AA	58-003	Stoneco	1500	8.94	2.69	47.5
26A	58-003	Stoneco	400	2.38	2.69	12.7
2NS	38-046	Chelsea	1260	7.62	2.65	39.9
<b>Total Wt</b>			<b>3160</b>	<b>18.94</b>		<b>100.0</b>

<----- Verify this number is 100%




**Superior Materials, LLC**  
 30701 W. 10 Mile Rd.  
 Suite 500  
 Farmington Hills, MI 48336

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	99.5	100.0	100.0	99.8	0.2	0.2
3/4"	82.1	100.0	100.0	91.5	8.3	8.5
1/2"	41.4	99.8	100.0	72.2	19.3	27.8
3/8"	17.2	89.7	100.0	59.4	12.8	40.6
#4	2.0	20.9	100.0	43.5	15.9	56.5
#8	1.0	4.3	88.0	36.1	7.4	63.9
#16	0.8	1.4	65.0	26.5	9.6	73.5
#30	0.7	0.9	46.0	18.8	7.7	81.2
#50	0.7	0.8	25.0	10.4	8.4	89.6
#100	0.5	0.7	6.0	2.7	7.7	97.3
LBW	0.5	0.5	1.0	0.7	2.0	99.3

\*Maximum % Retained must be above the 3/8" sieve.  
 \*Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation  Batch Plant Gradations  Aggregate Supplier Gradations

<b>Coarseness Factor:</b>	<b>64</b>	<b>Workability Factor:</b>	<b>36</b>
---------------------------	-----------	----------------------------	-----------

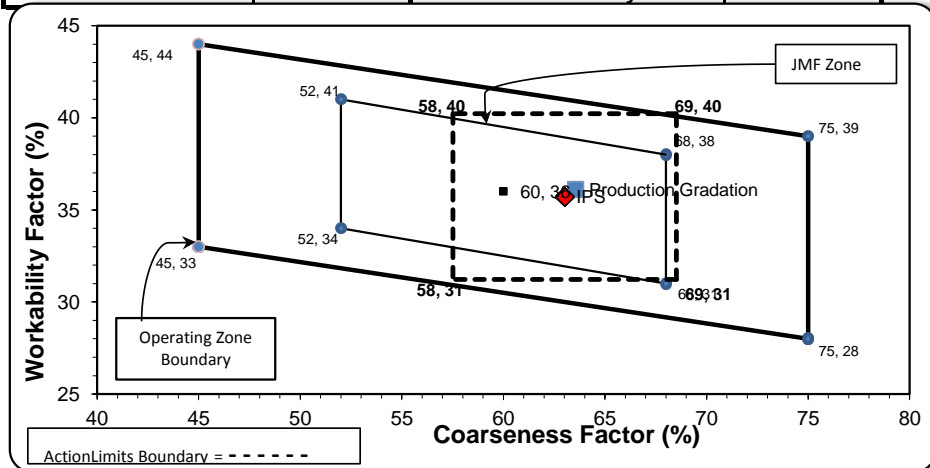

Initial Production Sample (IPS)

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	99.2	0.8	0.8
3/4"	90.9	8.3	9.1
1/2"	71.3	19.6	28.7
3/8"	59.5	11.8	40.5
#4	43.8	15.7	56.2
#8	35.7	8.1	64.3
#16	27.0	8.7	73.0
#30	18.6	8.4	81.4
#50	6.8	11.8	93.2
#100	1.4	5.4	98.6
LBW	0.6	0.8	99.4

PREPARED BY:  
 SM, LLC Technical Service

Approved By:

# Aggregate Optimization Chart

MIX ID'S: DDS257E7 and DDS257E8

Production Gradation Report

**PLANT #:** P-32

Sample Date: 9/24/18

Concrete Grade: S2M

Contractor: \_\_\_\_\_

Dates Test Represents: 9/25/2018 through 10/1/2018

MDOT No.: \_\_\_\_\_

Agg. Class	Pit #	Source	Weight (SSD)	ft <sup>3</sup>	Specific Gravity	% Contribution
6AA	71-47	Presque Isle	1600	9.79	2.62	51.4
26A	71-47	Presque Isle	230	1.41	2.62	7.4
2NS	95-13	Smelter Bay	1280	7.74	2.65	41.2
<b>Total Wt</b>			<b>3110</b>	<b>18.93</b>		<b>100.0</b>

<----- Verify this number is 100%




**Superior Materials, LLC**  
 30701 W. 10 Mile Rd.  
 Suite 500  
 Farmington Hills, MI 48336

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	98.0	100.0	100.0	99.0	1.0	1.0
3/4"	77.4	100.0	100.0	88.4	10.6	11.6
1/2"	42.9	95.8	100.0	70.3	18.1	29.7
3/8"	21.1	81.7	100.0	58.1	12.3	41.9
#4	3.1	21.3	97.7	43.4	14.7	56.6
#8	1.8	7.2	86.1	36.9	6.5	63.1
#16	1.6	4.0	68.8	29.4	7.5	70.6
#30	1.5	3.2	46.6	20.2	9.2	79.8
#50	1.5	2.9	19.4	9.0	11.2	91.0
#100	1.4	2.6	4.2	2.6	6.3	97.4
LBW	1.1	2.0	1.0	1.1	1.5	98.9

\*Maximum % Retained must be above the 3/8" sieve.  
 \*Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation  Batch Plant Gradations  Aggregate Supplier Gradations

<b>Coarseness Factor:</b>	<b>66</b>	<b>Workability Factor:</b>	<b>37</b>
---------------------------	-----------	----------------------------	-----------

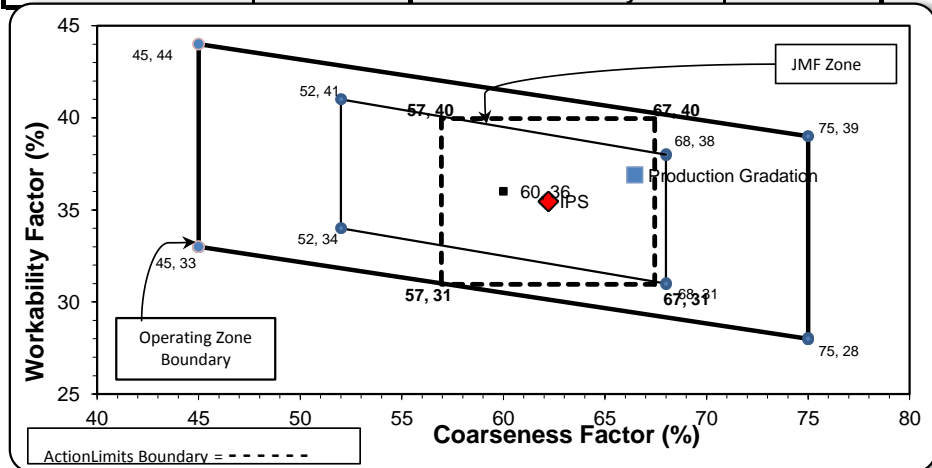

Initial Production Sample (IPS)

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	100.0	0.0	0.0
3/4"	94.0	6.0	6.0
1/2"	70.2	23.7	29.8
3/8"	59.9	10.4	40.1
#4	42.7	17.2	57.3
#8	35.5	7.2	64.5
#16	28.4	7.0	71.6
#30	19.2	9.2	80.8
#50	8.9	10.3	91.1
#100	3.1	5.9	96.9
LBW	1.4	1.7	98.6

PREPARED BY:  
 SM, LLC Technical Service

Approved By:

# Aggregate Optimization Chart

MIX ID'S: DDS257E7 and DDS257E8

Production Gradation Report

**PLANT #:** **P-36**

Sample Date: 9/24/18

Concrete Grade: **S2M**

Contractor: \_\_\_\_\_

Dates Test Represents: 9/25/2018 through 10/1/2018

MDOT No.: \_\_\_\_\_

Agg. Class	Pit #	Source	Weight (SSD)	ft <sup>3</sup>	Specific Gravity	% Contribution
6AA	71-47	Presque Isle	1630	9.97	2.62	52.4
26A	71-47	Presque Isle	200	1.22	2.62	6.4
2NS	63-92	AA Grange Hall	1280	7.74	2.65	41.2
<b>Total Wt</b>			<b>3110</b>	<b>18.93</b>		<b>100.0</b>

<----- Verify this number is 100%

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	100.0	100.0	100.0	100.0	0.0	0.0
3/4"	83.9	100.0	100.0	91.6	8.4	8.4
1/2"	41.8	95.8	100.0	69.2	22.3	30.8
3/8"	23.1	81.7	100.0	58.5	10.7	41.5
#4	4.7	21.3	97.4	43.9	14.6	56.1
#8	2.5	7.2	83.7	36.2	7.7	63.8
#16	2.2	4.0	68.0	29.4	6.8	70.6
#30	2.1	3.2	50.8	22.2	7.2	77.8
#50	2.0	2.9	24.1	11.2	11.1	88.8
#100	1.9	2.6	4.1	2.9	8.3	97.1
LBW	1.5	2.0	0.3	1.0	1.8	99.0




**Superior Materials, LLC**  
 30701 W. 10 Mile Rd.  
 Suite 500  
 Farmington Hills, MI 48336

\*Maximum % Retained must be above the 3/8" sieve.  
 \*Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation  Batch Plant Gradations  Aggregate Supplier Gradations

**Coarseness Factor:** **65**      **Workability Factor:** **36**

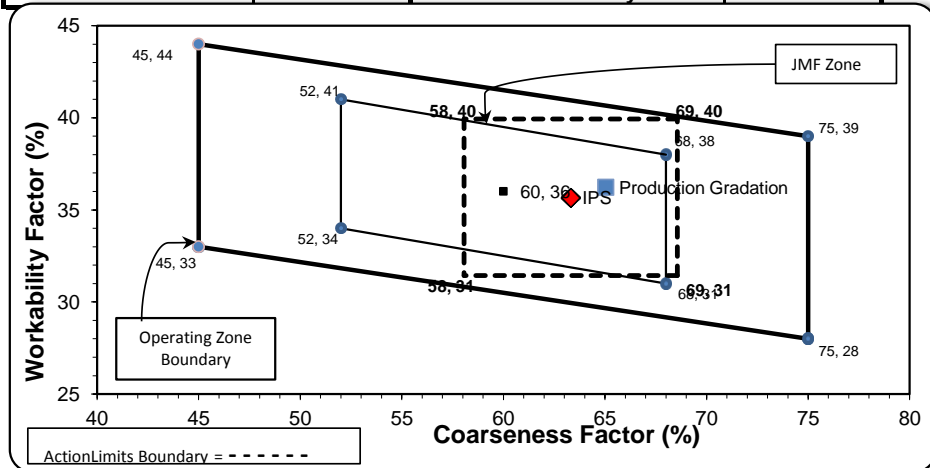

Initial Production Sample (IPS)

Coarseness Factor:		63	
Workability Factor:		36	
Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	100.0	0.0	0.0
3/4"	95.6	4.4	4.4
1/2"	73.1	22.6	26.9
3/8"	59.3	13.8	40.7
#4	42.8	16.5	57.2
#8	35.7	7.1	64.3
#16	28.9	6.8	71.1
#30	20.7	8.2	79.3
#50	9.9	10.8	90.1
#100	2.1	7.8	97.9
LBW	0.9	1.2	99.1

PREPARED BY:  
 SM, LLC Technical Service

Approved By:

# Aggregate Optimization Chart

MIX ID'S: DDS257E7 and DDS257E8

Production Gradation Report

**PLANT #:** **P-02**

Sample Date: 9/24/18

Concrete Grade: **S2M**

Contractor: \_\_\_\_\_

Dates Test Represents: 9/25/2018 through 10/1/2018

MDOT No.: \_\_\_\_\_

Agg. Class	Pit #	Source	Weight (SSD)	ft <sup>3</sup>	Specific Gravity	% Contribution
6AA	71-47	Presque Isle	1630	9.97	2.62	52.4
26A	71-47	Presque Isle	200	1.22	2.62	6.4
2NS	63-92	AA Grange Hall	1280	7.74	2.65	41.2
<b>Total Wt</b>			<b>3110</b>	<b>18.93</b>		<b>100.0</b>

<----- Verify this number is 100%

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	100.0	100.0	100.0	100.0	0.0	0.0
3/4"	83.9	100.0	100.0	91.6	8.4	8.4
1/2"	41.8	95.8	100.0	69.2	22.3	30.8
3/8"	23.1	81.7	100.0	58.5	10.7	41.5
#4	4.7	21.3	97.4	43.9	14.6	56.1
#8	2.5	7.2	83.7	36.2	7.7	63.8
#16	2.2	4.0	68.0	29.4	6.8	70.6
#30	2.1	3.2	50.8	22.2	7.2	77.8
#50	2.0	2.9	24.1	11.2	11.1	88.8
#100	1.9	2.6	4.1	2.9	8.3	97.1
LBW	1.5	2.0	0.3	1.0	1.8	99.0




**Superior Materials, LLC**  
 30701 W. 10 Mile Rd.  
 Suite 500  
 Farmington Hills, MI 48336

\*Maximum % Retained must be above the 3/8" sieve.  
 \*Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation  Batch Plant Gradations  Aggregate Supplier Gradations

**Coarseness Factor:** **65**      **Workability Factor:** **36**

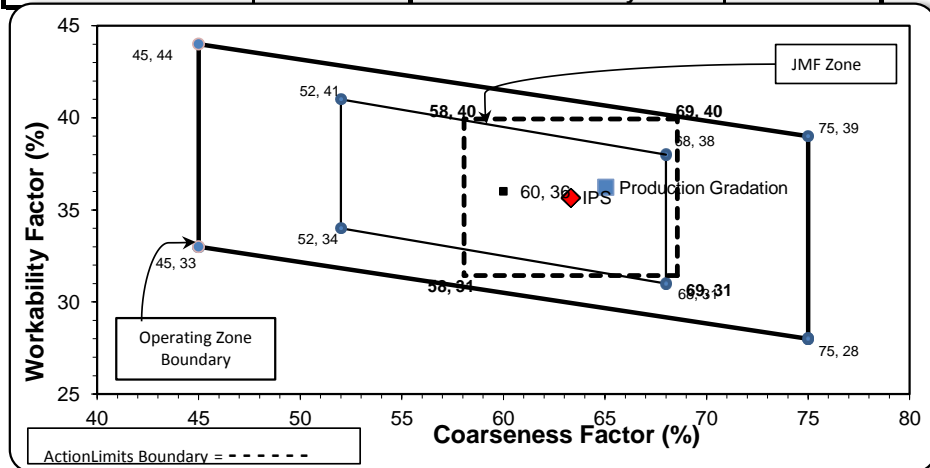

Initial Production Sample (IPS)

**Coarseness Factor:** **63**  
**Workability Factor:** **36**

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	100.0	0.0	0.0
3/4"	95.6	4.4	4.4
1/2"	73.1	22.6	26.9
3/8"	59.3	13.8	40.7
#4	42.8	16.5	57.2
#8	35.7	7.1	64.3
#16	28.9	6.8	71.1
#30	20.7	8.2	79.3
#50	9.9	10.8	90.1
#100	2.1	7.8	97.9
LBW	0.9	1.2	99.1

PREPARED BY:  
 SM, LLC Technical Service

Approved By:
