

Aggregate Optimization Chart

PLANT #: **P-32**

Sample Date: 1/25/21 Concrete Grade: **DM**
 Dates Test Represents: 1/26/2021 through 2/1/2021

Contractor: _____

MDOT No.: _____

Agg. Class	Pit #	Source	Weight (SSD)	ft ³	Specific Gravity	% Contribution
6AA	71-47	Presque Isle	1455	8.90	2.62	50.1
26A	71-47	Presque Isle	300	1.83	2.62	10.3
2NS	95-013	Smelter Bay	1150	6.95	2.65	39.6
Total Wt			2905	17.69		100.0

<----- Verify this number is 100%



Superior Materials, LLC
 30701 W. 10 Mile Rd.
 Suite 500
 Farmington Hills, MI 48336


Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	98.1	100.0	100.0	99.0	1.0	1.0
3/4"	71.8	100.0	100.0	85.9	13.2	14.1
1/2"	30.9	98.4	100.0	65.2	20.7	34.8
3/8"	15.2	85.4	100.0	56.0	9.2	44.0
#4	2.6	13.4	96.6	40.9	15.1	59.1
#8	1.5	2.8	82.8	33.8	7.1	66.2
#16	1.3	1.5	66.7	27.2	6.6	72.8
#30	1.2	1.3	43.3	17.9	9.3	82.1
#50	1.0	1.2	18.0	7.8	10.1	92.2
#100	0.9	1.1	4.4	2.3	5.4	97.7
LBW	0.6	0.8	1.1	0.8	1.5	99.2

*Maximum % Retained must be above the 3/8" sieve.
 *Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation Batch Plant Gradations Aggregate Supplier Gradations Adjusted WF Initial Production Sample (IPS)

Coarseness Factor:	66	Workability Factor:	34	Adjusted WF	36.3
---------------------------	-----------	----------------------------	-----------	--------------------	-------------

Coarseness Factor:	62
Workability Factor:	36

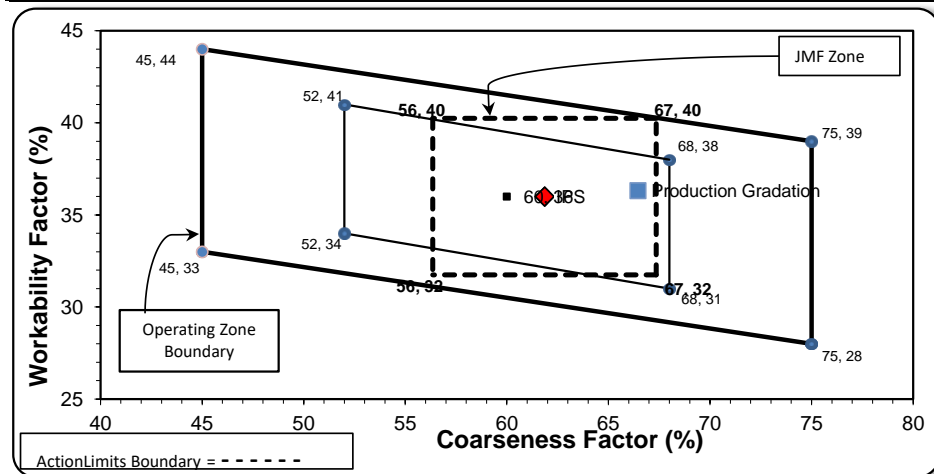

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	100.0	0.0	0.0
3/4"	95.0	5.0	5.0
1/2"	72.3	22.8	27.7
3/8"	60.4	11.8	39.6
#4	42.6	17.8	57.4
#8	36.0	6.6	64.0
#16	29.5	6.5	70.5
#30	20.3	9.2	79.7
#50	9.5	10.8	90.5
#100	3.4	6.1	96.6
LBW	1.3	2.1	98.7

PREPARED BY:
 SM, LLC Technical Service

Approved By:

Aggregate Optimization Chart

PLANT #: **P-36**

Sample Date: 1/25/21 Concrete Grade: DM
 Dates Test Represents: 1/26/2021 through 2/1/2021

Contractor: _____

MDOT No.: _____

Agg. Class	Pit #	Source	Weight (SSD)	ft ³	Specific Gravity	% Contribution
6AA	71-47	Presque Isle	1505	9.21	2.62	51.8
26A	71-47	Presque Isle	300	1.83	2.62	10.3
2NS	63-92	Grange Hall	1100	6.65	2.65	37.9
Total Wt			2905	17.69		100.0

<----- Verify this number is 100%



Superior Materials, LLC
 30701 W. 10 Mile Rd.
 Suite 500
 Farmington Hills, MI 48336


Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	99.0	100.0	100.0	99.5	0.5	0.5
3/4"	83.1	100.0	100.0	91.2	8.2	8.8
1/2"	38.3	98.4	100.0	67.9	23.4	32.1
3/8"	19.6	85.4	100.0	56.8	11.0	43.2
#4	3.6	13.4	97.3	40.1	16.7	59.9
#8	2.4	2.8	84.1	33.4	6.7	66.6
#16	2.0	1.5	69.2	27.4	6.0	72.6
#30	2.0	1.3	48.6	19.6	7.8	80.4
#50	2.0	1.2	19.5	8.5	11.0	91.5
#100	1.8	1.1	2.4	2.0	6.6	98.0
LBW	1.4	0.8	0.4	1.0	1.0	99.0

*Maximum % Retained must be above the 3/8" sieve.
 *Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation Batch Plant Gradations Aggregate Supplier Gradations Adjusted WF Initial Production Sample (IPS)

Coarseness Factor:	65	Workability Factor:	33	Adjusted WF	35.9
---------------------------	-----------	----------------------------	-----------	--------------------	-------------

Coarseness Factor:	63
Workability Factor:	35

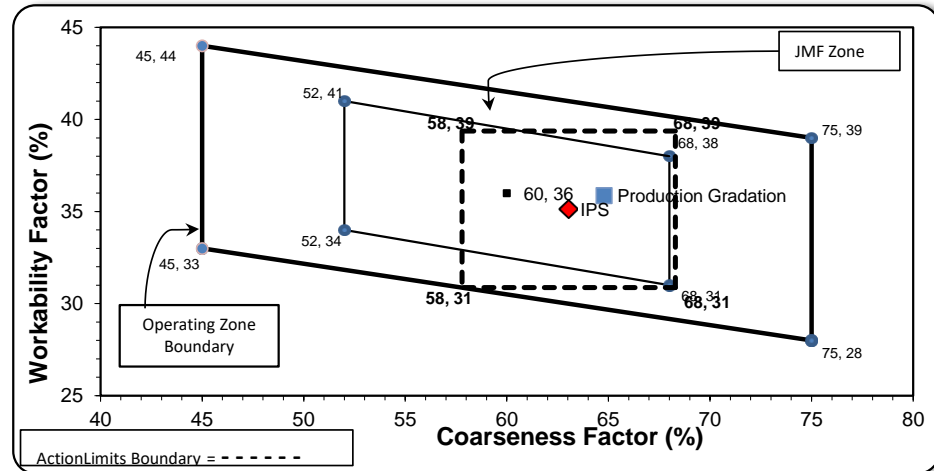

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	99.1	0.9	0.9
3/4"	90.3	8.8	9.7
1/2"	69.2	21.1	30.8
3/8"	59.1	10.1	40.9
#4	41.8	17.3	58.2
#8	35.1	6.6	64.9
#16	28.5	6.6	71.5
#30	21.2	7.3	78.8
#50	8.7	12.5	91.3
#100	1.8	7.0	98.2
LBW	0.7	1.0	99.3

PREPARED BY:
 SM, LLC Technical Service

Approved By:

Aggregate Optimization Chart

PLANT #: **P-39**

Sample Date: 1/25/21 Concrete Grade: **DM**
 Dates Test Represents: 1/26/2021 through 2/1/2021

Contractor: _____

MDOT No.: _____

Agg. Class	Pit #	Source	Weight (SSD)	ft ³	Specific Gravity	% Contribution
6AA	71-47	Presque Isle	1555	9.51	2.62	53.5
26A	71-47	Presque Isle	250	1.53	2.62	8.6
2NS	63-92	Grange Hall	1100	6.65	2.65	37.9
Total Wt			2905	17.69		100.0

<----- Verify this number is 100%



Superior Materials, LLC
 30701 W. 10 Mile Rd.
 Suite 500
 Farmington Hills, MI 48336

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	99.2	100.0	100.0	99.6	0.4	0.4
3/4"	89.0	100.0	100.0	94.1	5.5	5.9
1/2"	45.8	97.2	100.0	70.7	23.4	29.3
3/8"	25.4	88.9	100.0	59.1	11.6	40.9
#4	3.1	16.3	97.3	39.9	19.2	60.1
#8	1.7	4.0	84.1	33.1	6.8	66.9
#16	1.5	2.4	69.2	27.2	5.9	72.8
#30	1.4	2.0	48.6	19.3	7.9	80.7
#50	1.3	1.9	19.5	8.2	11.1	91.8
#100	1.3	1.8	2.4	1.8	6.5	98.2
LBW	1.2	1.6	0.4	0.9	0.8	99.1


*Maximum % Retained must be above the 3/8" sieve.
 *Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation Batch Plant Gradations Aggregate Supplier Gradations

Adjusted WF Initial Production Sample (IPS)

Coarseness Factor:	61	Workability Factor:	33	Adjusted WF	35.6
---------------------------	-----------	----------------------------	-----------	--------------------	-------------

Coarseness Factor:	63
Workability Factor:	36

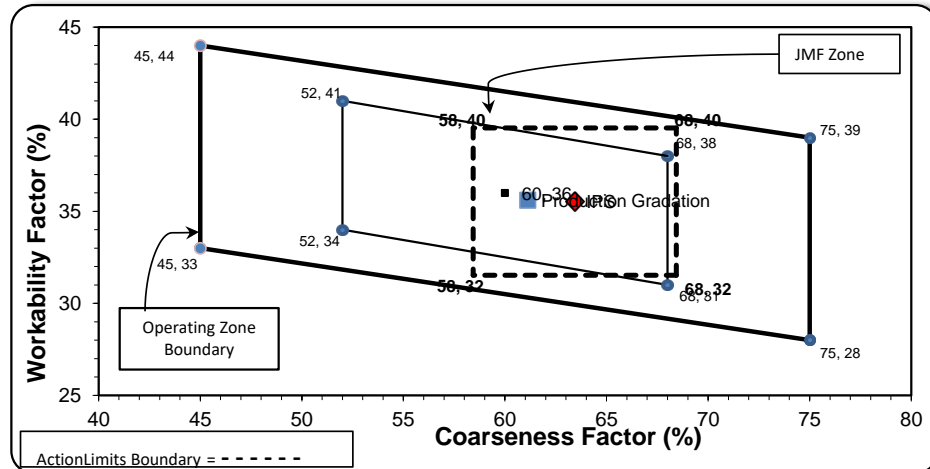

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	100.0	0.0	0.0
3/4"	89.7	10.3	10.3
1/2"	70.3	19.4	29.7
3/8"	59.1	11.2	40.9
#4	42.8	16.3	57.2
#8	35.5	7.3	64.5
#16	29.0	6.5	71.0
#30	21.2	7.7	78.8
#50	9.8	11.5	90.2
#100	3.7	6.1	96.3
LBW	1.2	2.5	98.8

PREPARED BY:
 SM, LLC Technical Service

Approved By:

Aggregate Optimization Chart

PLANT #: **P-02**

Sample Date: 1/25/21 Concrete Grade: **DM**
 Dates Test Represents: 1/26/2021 through 2/1/2021

Contractor: _____

MDOT No.: _____

Agg. Class	Pit #	Source	Weight (SSD)	ft ³	Specific Gravity	% Contribution
6AA	71-47	Presque Isle	1455	8.90	2.62	50.1
26A	71-47	Presque Isle	300	1.83	2.62	10.3
2NS	63-115	Ray Rd	1150	6.95	2.65	39.6
Total Wt			2905	17.69		100.0

<----- Verify this number is 100%



Superior Materials, LLC
 30701 W. 10 Mile Rd.
 Suite 500
 Farmington Hills, MI 48336

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	99.0	100.0	100.0	99.5	0.5	0.5
3/4"	83.1	100.0	100.0	91.5	8.0	8.5
1/2"	38.3	98.4	100.0	68.9	22.6	31.1
3/8"	19.6	85.4	100.0	58.2	10.7	41.8
#4	3.6	13.4	96.4	41.3	16.9	58.7
#8	2.4	2.8	77.4	32.1	9.2	67.9
#16	2.0	1.5	60.8	25.2	6.9	74.8
#30	2.0	1.3	45.3	19.1	6.2	80.9
#50	2.0	1.2	21.0	9.4	9.6	90.6
#100	1.8	1.1	3.4	2.4	7.1	97.6
LBW	1.4	0.8	0.3	0.9	1.5	99.1


*Maximum % Retained must be above the 3/8" sieve.
 *Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation Batch Plant Gradations Aggregate Supplier Gradations

Adjusted WF Initial Production Sample (IPS)

Coarseness Factor:	62	Workability Factor:	32	34.6	Coarseness Factor:	63
---------------------------	-----------	----------------------------	-----------	-------------	---------------------------	-----------

Workability Factor:	35
----------------------------	-----------

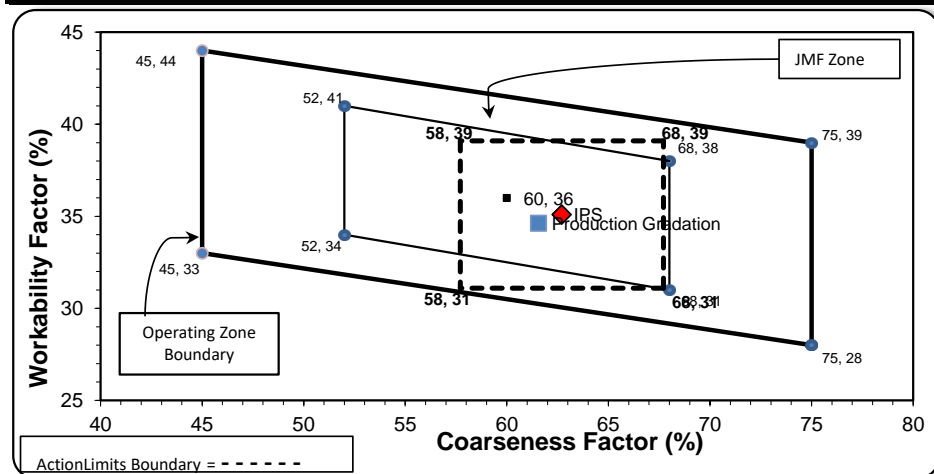

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	100.0	0.0	0.0
3/4"	95.1	4.9	4.9
1/2"	74.6	20.5	25.4
3/8"	59.3	15.3	40.7
#4	42.1	17.2	57.9
#8	35.1	7.1	64.9
#16	29.2	5.9	70.8
#30	21.9	7.3	78.1
#50	9.6	12.4	90.4
#100	2.4	7.2	97.6
LBW	0.9	1.5	99.1

PREPARED BY:
 SM, LLC Technical Service

Approved By:
