

# Aggregate Optimization Chart

**PLANT #:** **P-32**

Sample Date: 2/15/21 Concrete Grade: **DM**

Dates Test Represents: 2/16/2021 through 2/22/2021

Contractor: \_\_\_\_\_

MDOT No.: \_\_\_\_\_

Agg. Class	Pit #	Source	Weight (SSD)	ft <sup>3</sup>	Specific Gravity	% Contribution
6AA	71-47	Presque Isle	1400	8.56	2.62	48.2
26A	71-47	Presque Isle	355	2.17	2.62	12.2
2NS	95-013	Smelter Bay	1150	6.95	2.65	39.6
<b>Total Wt</b>			<b>2905</b>	<b>17.69</b>		<b>100.0</b>

<----- Verify this number is 100%

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	98.1	100.0	100.0	99.1	0.9	0.9
3/4"	71.8	100.0	100.0	86.4	12.7	13.6
1/2"	30.9	97.0	100.0	66.3	20.1	33.7
3/8"	15.2	77.4	100.0	56.4	10.0	43.6
#4	2.6	10.5	96.7	40.8	15.6	59.2
#8	1.5	3.8	84.7	34.7	6.1	65.3
#16	1.3	2.6	71.2	29.1	5.6	70.9
#30	1.2	2.2	50.1	20.7	8.4	79.3
#50	1.0	2.1	19.0	8.3	12.4	91.7
#100	0.9	1.9	4.5	2.4	5.8	97.6
LBW	0.6	1.7	1.3	1.0	1.4	99.0




**Superior Materials, LLC**  
 30701 W. 10 Mile Rd.  
 Suite 500  
 Farmington Hills, MI 48336

\*Maximum % Retained must be above the 3/8" sieve.  
 \*Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation  Batch Plant Gradations  Aggregate Supplier Gradations  Adjusted WF Initial Production Sample (IPS)

<b>Coarseness Factor:</b>	<b>67</b>	<b>Workability Factor:</b>	<b>35</b>	<b>Adjusted WF</b>	<b>37.2</b>
---------------------------	-----------	----------------------------	-----------	--------------------	-------------

<b>Coarseness Factor:</b>	<b>62</b>
<b>Workability Factor:</b>	<b>36</b>

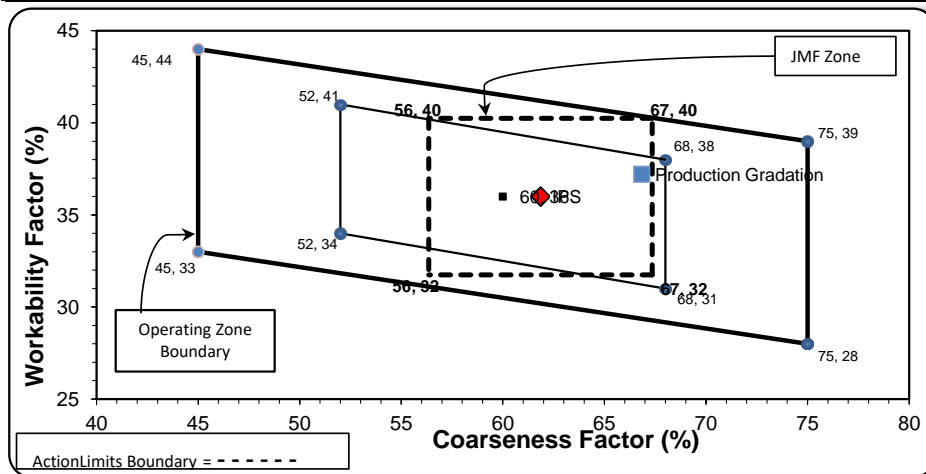

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	100.0	0.0	0.0
3/4"	95.0	5.0	5.0
1/2"	72.3	22.8	27.7
3/8"	60.4	11.8	39.6
#4	42.6	17.8	57.4
#8	36.0	6.6	64.0
#16	29.5	6.5	70.5
#30	20.3	9.2	79.7
#50	9.5	10.8	90.5
#100	3.4	6.1	96.6
LBW	1.3	2.1	98.7

PREPARED BY:  
 SM, LLC Technical Service

Approved By:

# Aggregate Optimization Chart

**PLANT #:** **P-36**

Sample Date: 2/15/21 Concrete Grade: **DM**

Dates Test Represents: 2/16/2021 through 2/22/2021

Contractor: \_\_\_\_\_

MDOT No.: \_\_\_\_\_



**Superior Materials, LLC**  
 30701 W. 10 Mile Rd.  
 Suite 500  
 Farmington Hills, MI 48336

Agg. Class	Pit #	Source	Weight (SSD)	ft <sup>3</sup>	Specific Gravity	% Contribution
6AA	71-47	Presque Isle	1455	8.90	2.62	50.1
26A	71-47	Presque Isle	350	2.14	2.62	12.0
2NS	63-92	Grange Hall	1100	6.65	2.65	37.9
<b>Total Wt</b>			<b>2905</b>	<b>17.69</b>		<b>100.0</b>

<----- Verify this number is 100%


Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	99.1	100.0	100.0	99.5	0.5	0.5
3/4"	80.3	100.0	100.0	90.1	9.4	9.9
1/2"	33.8	97.0	100.0	66.5	23.7	33.5
3/8"	15.2	77.4	100.0	54.8	11.7	45.2
#4	2.2	10.5	97.5	39.3	15.5	60.7
#8	1.8	3.8	85.3	33.7	5.6	66.3
#16	1.7	2.6	70.6	27.9	5.8	72.1
#30	1.7	2.2	49.2	19.7	8.2	80.3
#50	1.6	2.1	19.6	8.5	11.3	91.5
#100	1.5	1.9	2.3	1.9	6.6	98.1
LBW	1.3	1.7	0.5	1.0	0.8	99.0

\*Maximum % Retained must be above the 3/8" sieve.  
 \*Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation  Batch Plant Gradations  Aggregate Supplier Gradations  Adjusted WF Initial Production Sample (IPS)

<b>Coarseness Factor:</b>	<b>68</b>	<b>Workability Factor:</b>	<b>34</b>	<b>Adjusted WF</b>	<b>36.2</b>
---------------------------	-----------	----------------------------	-----------	--------------------	-------------

<b>Coarseness Factor:</b>	<b>63</b>
<b>Workability Factor:</b>	<b>35</b>

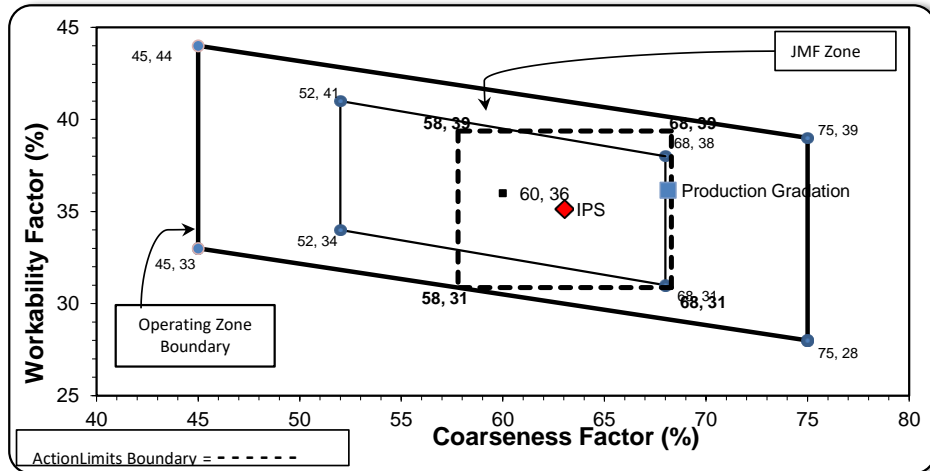

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	99.1	0.9	0.9
3/4"	90.3	8.8	9.7
1/2"	69.2	21.1	30.8
3/8"	59.1	10.1	40.9
#4	41.8	17.3	58.2
#8	35.1	6.6	64.9
#16	28.5	6.6	71.5
#30	21.2	7.3	78.8
#50	8.7	12.5	91.3
#100	1.8	7.0	98.2
LBW	0.7	1.0	99.3

PREPARED BY:  
 SM, LLC Technical Service

Approved By:

# Aggregate Optimization Chart

**PLANT #:** **P-39**

Sample Date: 2/15/21 Concrete Grade: **DM**

Dates Test Represents: 2/16/2021 through 2/22/2021

Contractor: \_\_\_\_\_

MDOT No.: \_\_\_\_\_

Agg. Class	Pit #	Source	Weight (SSD)	ft <sup>3</sup>	Specific Gravity	% Contribution
6AA	71-47	Presque Isle	1555	9.51	2.62	53.5
26A	71-47	Presque Isle	250	1.53	2.62	8.6
2NS	63-92	Grange Hall	1100	6.65	2.65	37.9
<b>Total Wt</b>			<b>2905</b>	<b>17.69</b>		<b>100.0</b>

<----- Verify this number is 100%



**Superior Materials, LLC**  
 30701 W. 10 Mile Rd.  
 Suite 500  
 Farmington Hills, MI 48336

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	96.6	100.0	100.0	98.2	1.8	1.8
3/4"	77.5	100.0	100.0	88.0	10.2	12.0
1/2"	39.8	98.8	100.0	67.7	20.3	32.3
3/8"	24.3	88.8	100.0	58.5	9.2	41.5
#4	4.8	18.6	97.5	41.1	17.4	58.9
#8	2.3	5.5	85.3	34.0	7.1	66.0
#16	1.8	2.7	70.6	27.9	6.1	72.1
#30	1.7	2.1	49.2	19.7	8.2	80.3
#50	1.6	1.9	19.6	8.4	11.3	91.6
#100	1.6	1.8	2.3	1.9	6.6	98.1
LBW	1.4	1.7	0.5	1.1	0.8	98.9


\*Maximum % Retained must be above the 3/8" sieve.  
 \*Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation  Batch Plant Gradations  Aggregate Supplier Gradations

Adjusted WF Initial Production Sample (IPS)

<b>Coarseness Factor:</b>	<b>63</b>	<b>Workability Factor:</b>	<b>34</b>	<b>Adjusted WF</b>	<b>36.5</b>
---------------------------	-----------	----------------------------	-----------	--------------------	-------------

<b>Coarseness Factor:</b>	<b>63</b>
<b>Workability Factor:</b>	<b>36</b>

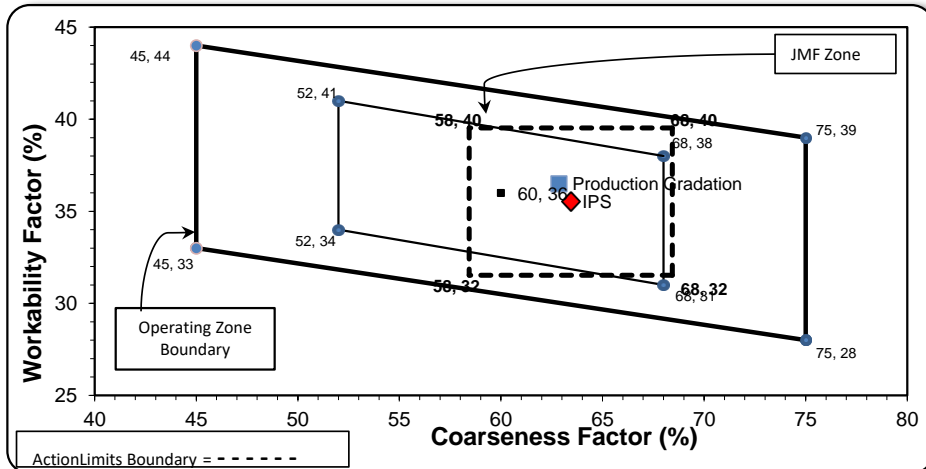

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	100.0	0.0	0.0
3/4"	89.7	10.3	10.3
1/2"	70.3	19.4	29.7
3/8"	59.1	11.2	40.9
#4	42.8	16.3	57.2
#8	35.5	7.3	64.5
#16	29.0	6.5	71.0
#30	21.2	7.7	78.8
#50	9.8	11.5	90.2
#100	3.7	6.1	96.3
LBW	1.2	2.5	98.8

PREPARED BY:  
 SM, LLC Technical Service

Approved By:

# Aggregate Optimization Chart

**PLANT #:** **P-02**

Sample Date: 2/15/21 Concrete Grade: DM  
 Dates Test Represents: 2/16/2021 through 2/22/2021

Contractor: \_\_\_\_\_

MDOT No.: \_\_\_\_\_

Agg. Class	Pit #	Source	Weight (SSD)	ft <sup>3</sup>	Specific Gravity	% Contribution
6AA	71-47	Presque Isle	1455	8.90	2.62	50.1
26A	71-47	Presque Isle	300	1.83	2.62	10.3
2NS	63-115	Ray Rd	1150	6.95	2.65	39.6
<b>Total Wt</b>			<b>2905</b>	<b>17.69</b>		<b>100.0</b>

<----- Verify this number is 100%



**Superior Materials, LLC**  
 30701 W. 10 Mile Rd.  
 Suite 500  
 Farmington Hills, MI 48336

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	99.1	100.0	100.0	99.5	0.5	0.5
3/4"	80.3	100.0	100.0	90.1	9.4	9.9
1/2"	33.8	97.0	100.0	66.5	23.6	33.5
3/8"	15.2	77.4	100.0	55.2	11.3	44.8
#4	2.2	10.5	97.5	40.8	14.4	59.2
#8	1.8	3.8	82.6	34.0	6.8	66.0
#16	1.7	2.6	67.6	27.9	6.1	72.1
#30	1.7	2.2	51.4	21.4	6.5	78.6
#50	1.6	2.1	24.7	10.8	10.6	89.2
#100	1.5	1.9	3.5	2.3	8.5	97.7
LBW	1.3	1.7	0.5	1.0	1.3	99.0


\*Maximum % Retained must be above the 3/8" sieve.  
 \*Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation  Batch Plant Gradations  Aggregate Supplier Gradations

Adjusted WF Initial Production Sample (IPS)

<b>Coarseness Factor:</b>	<b>68</b>	<b>Workability Factor:</b>	<b>34</b>	<b>Adjusted WF</b>	<b>36.5</b>
---------------------------	-----------	----------------------------	-----------	--------------------	-------------

<b>Coarseness Factor:</b>	<b>63</b>
<b>Workability Factor:</b>	<b>35</b>

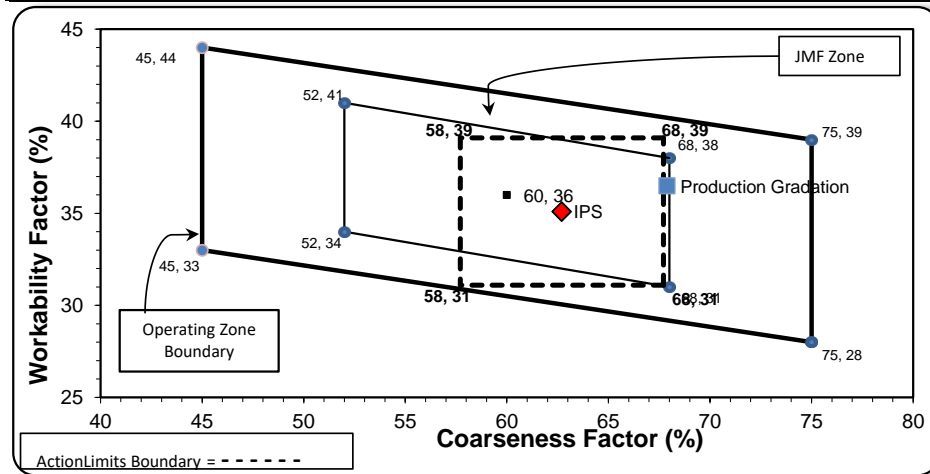

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	100.0	0.0	0.0
3/4"	95.1	4.9	4.9
1/2"	74.6	20.5	25.4
3/8"	59.3	15.3	40.7
#4	42.1	17.2	57.9
#8	35.1	7.1	64.9
#16	29.2	5.9	70.8
#30	21.9	7.3	78.1
#50	9.6	12.4	90.4
#100	2.4	7.2	97.6
LBW	0.9	1.5	99.1

PREPARED BY:  
 SM, LLC Technical Service

Approved By:
