

Aggregate Optimization Chart

PLANT #: **P-103**

Sample Date: 10/26/20

Concrete Grade: **DM**

Contractor: _____

Dates Test Represents: 10/27/2020 through 11/2/2020

MDOT No.: _____

Agg. Class	Pit #	Source	Weight (SSD)	ft ³	Specific Gravity	% Contribution
6AA	58-003	Stoneco	1500	8.94	2.69	50.8
26A	58-003	Stoneco	305	1.82	2.69	10.3
2NS	63-114	Highland	1150	6.95	2.65	38.9
Total Wt			2955	17.71		100.0

<----- Verify this number is 100%



Superior Materials, LLC
 30701 W. 10 Mile Rd.
 Suite 500
 Farmington Hills, MI 48336

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	100.0	100.0	100.0	100.0	0.0	0.0
3/4"	86.4	100.0	100.0	93.1	6.9	6.9
1/2"	47.2	99.6	100.0	73.2	19.9	26.8
3/8"	26.3	85.5	100.0	61.1	12.1	38.9
#4	5.2	19.0	98.9	43.1	18.0	56.9
#8	2.0	6.4	83.0	34.0	9.1	66.0
#16	1.4	3.4	65.1	26.4	7.6	73.6
#30	1.2	2.6	46.8	19.1	7.3	80.9
#50	1.0	2.3	19.2	8.2	10.9	91.8
#100	0.8	2.1	3.8	2.1	6.1	97.9
LBW	0.6	1.9	0.3	0.6	1.5	99.4


*Maximum % Retained must be above the 3/8" sieve.
 *Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation Batch Plant Gradations Aggregate Supplier Gradations

Adjusted WF Initial Production Sample (IPS)

Coarseness Factor:	59	Workability Factor:	34	36.5	Coarseness Factor:	61
---------------------------	-----------	----------------------------	-----------	-------------	---------------------------	-----------

Workability Factor:	36
----------------------------	-----------

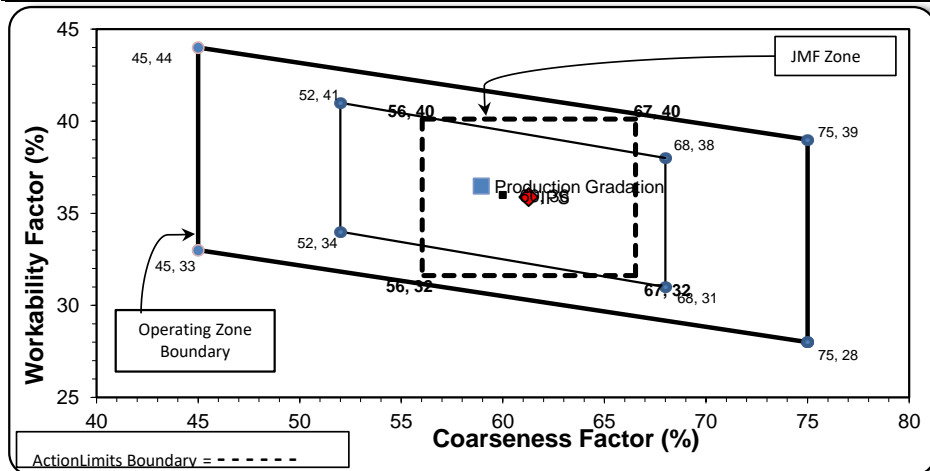

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	99.3	0.7	0.7
3/4"	89.2	10.1	10.8
1/2"	70.7	18.5	29.3
3/8"	60.7	10.0	39.3
#4	44.4	16.3	55.6
#8	35.9	8.5	64.1
#16	27.3	8.6	72.7
#30	19.1	8.2	80.9
#50	7.4	11.7	92.6
#100	1.9	5.6	98.1
LBW	0.7	1.2	99.3

PREPARED BY:
 SM, LLC Technical Service

Approved BY:

Aggregate Optimization Chart

PLANT #: **P-20**

Sample Date: 10/26/20

Concrete Grade: **DM**

Contractor: _____

Dates Test Represents: 10/27/2020 through 11/2/2020

MDOT No.: _____

Agg. Class	Pit #	Source	Weight (SSD)	ft ³	Specific Gravity	% Contribution
6AA	71-47	Presque Isle	1555	9.51	2.62	53.5
26A	71-47	Presque Isle	250	1.53	2.62	8.6
2NS	63-92	Grange Hall	1100	6.65	2.65	37.9
Total Wt			2905	17.69		100.0

<----- Verify this number is 100%



Superior Materials, LLC
 30701 W. 10 Mile Rd.
 Suite 500
 Farmington Hills, MI 48336

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	96.9	100.0	100.0	98.3	1.7	1.7
3/4"	76.4	100.0	100.0	87.4	11.0	12.6
1/2"	35.6	97.6	100.0	65.3	22.0	34.7
3/8"	21.5	91.2	100.0	57.2	8.1	42.8
#4	3.7	26.1	97.6	41.2	16.0	58.8
#8	2.1	7.2	85.8	34.2	7.0	65.8
#16	1.7	3.3	70.9	28.0	6.2	72.0
#30	1.6	2.4	48.8	19.5	8.5	80.5
#50	1.5	2.2	18.0	7.8	11.7	92.2
#100	1.5	2.0	2.5	1.9	5.9	98.1
LBW	1.4	1.8	0.4	1.1	0.9	98.9


*Maximum % Retained must be above the 3/8" sieve.
 *Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation Batch Plant Gradations Aggregate Supplier Gradations

Adjusted WF Initial Production Sample (IPS)

Coarseness Factor:	65	Workability Factor:	34	Adjusted WF	36.7
---------------------------	-----------	----------------------------	-----------	--------------------	-------------

Coarseness Factor:	63
Workability Factor:	36

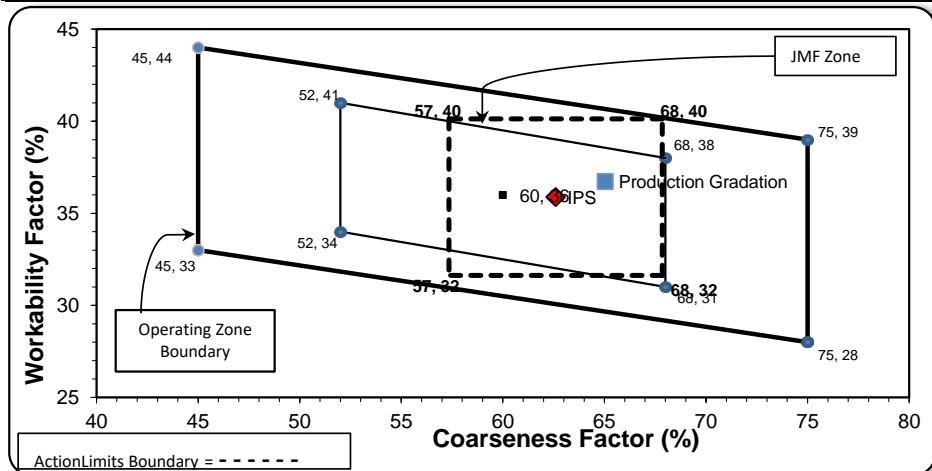

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	100.0	0.0	0.0
3/4"	89.2	10.8	10.8
1/2"	68.4	20.8	31.6
3/8"	59.9	8.6	40.1
#4	43.0	16.9	57.0
#8	35.9	7.1	64.1
#16	29.0	6.8	71.0
#30	21.3	7.7	78.7
#50	9.9	11.4	90.1
#100	2.4	7.5	97.6
LBW	1.2	1.2	98.8

PREPARED BY:
 SM, LLC Technical Service

Approved By:

Aggregate Optimization Chart

PLANT #: **P-32**

Sample Date: 10/26/20

Concrete Grade: **DM**

Contractor: _____

Dates Test Represents: 10/27/2020 through 11/2/2020

MDOT No.: _____

Agg. Class	Pit #	Source	Weight (SSD)	ft ³	Specific Gravity	% Contribution
6AA	71-47	Presque Isle	1605	9.82	2.62	55.2
26A	71-47	Presque Isle	150	0.92	2.62	5.2
2NS	95-013	Smelter Bay	1150	6.95	2.65	39.6
Total Wt			2905	17.69		100.0

<----- Verify this number is 100%



Superior Materials, LLC
 30701 W. 10 Mile Rd.
 Suite 500
 Farmington Hills, MI 48336

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	98.7	100.0	100.0	99.3	0.7	0.7
3/4"	84.4	100.0	100.0	91.4	7.9	8.6
1/2"	47.9	97.4	100.0	71.1	20.3	28.9
3/8"	31.3	89.6	100.0	61.5	9.6	38.5
#4	5.4	17.0	96.0	41.9	19.6	58.1
#8	3.6	4.8	83.3	35.2	6.7	64.8
#16	2.8	2.6	67.1	28.2	7.0	71.8
#30	2.6	2.3	46.7	20.0	8.2	80.0
#50	2.4	2.2	22.1	10.2	9.9	89.8
#100	2.2	2.1	6.1	3.7	6.4	96.3
LBW	1.7	1.9	1.0	1.4	2.3	98.6


*Maximum % Retained must be above the 3/8" sieve.
 *Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation Batch Plant Gradations Aggregate Supplier Gradations

Adjusted WF Initial Production Sample (IPS)

Coarseness Factor:	59	Workability Factor:	35	37.7	Coarseness Factor:	62
---------------------------	-----------	----------------------------	-----------	-------------	---------------------------	-----------

Workability Factor:	36
----------------------------	-----------

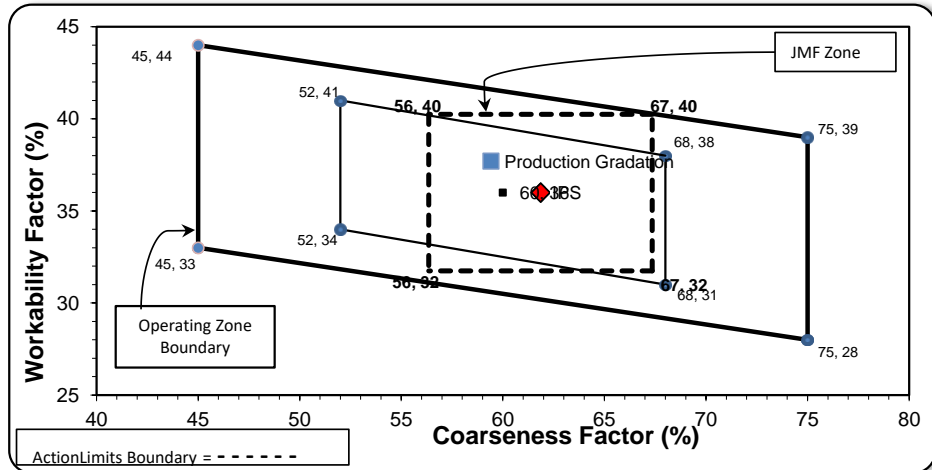

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	100.0	0.0	0.0
3/4"	95.0	5.0	5.0
1/2"	72.3	22.8	27.7
3/8"	60.4	11.8	39.6
#4	42.6	17.8	57.4
#8	36.0	6.6	64.0
#16	29.5	6.5	70.5
#30	20.3	9.2	79.7
#50	9.5	10.8	90.5
#100	3.4	6.1	96.6
LBW	1.3	2.1	98.7

PREPARED BY:
 SM, LLC Technical Service

Approved By:

Aggregate Optimization Chart

PLANT #: **P-36**

Sample Date: 10/26/20

Concrete Grade: **DM**

Contractor: _____

Dates Test Represents: 10/27/2020 through 11/2/2020

MDOT No.: _____

Agg. Class	Pit #	Source	Weight (SSD)	ft ³	Specific Gravity	% Contribution
6AA	71-47	Presque Isle	1605	9.82	2.62	55.2
26A	71-47	Presque Isle	200	1.22	2.62	6.9
2NS	63-92	Grange Hall	1100	6.65	2.65	37.9
Total Wt			2905	17.69		100.0

<----- Verify this number is 100%



Superior Materials, LLC
 30701 W. 10 Mile Rd.
 Suite 500
 Farmington Hills, MI 48336

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	96.6	100.0	100.0	98.1	1.9	1.9
3/4"	75.4	100.0	100.0	86.4	11.7	13.6
1/2"	37.4	97.4	100.0	65.2	21.2	34.8
3/8"	23.5	89.6	100.0	57.0	8.2	43.0
#4	5.4	17.0	97.6	41.1	15.9	58.9
#8	2.7	4.8	85.8	34.3	6.8	65.7
#16	2.2	2.6	70.9	28.2	6.1	71.8
#30	2.1	2.3	48.8	19.8	8.4	80.2
#50	2.0	2.2	18.0	8.1	11.7	91.9
#100	1.9	2.1	2.5	2.1	5.9	97.9
LBW	1.5	1.9	0.4	1.1	1.0	98.9


*Maximum % Retained must be above the 3/8" sieve.
 *Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation Batch Plant Gradations Aggregate Supplier Gradations

Adjusted WF Initial Production Sample (IPS)

Coarseness Factor:	65	Workability Factor:	34	Adjusted WF	36.8
---------------------------	-----------	----------------------------	-----------	--------------------	-------------

Coarseness Factor:	63
Workability Factor:	35

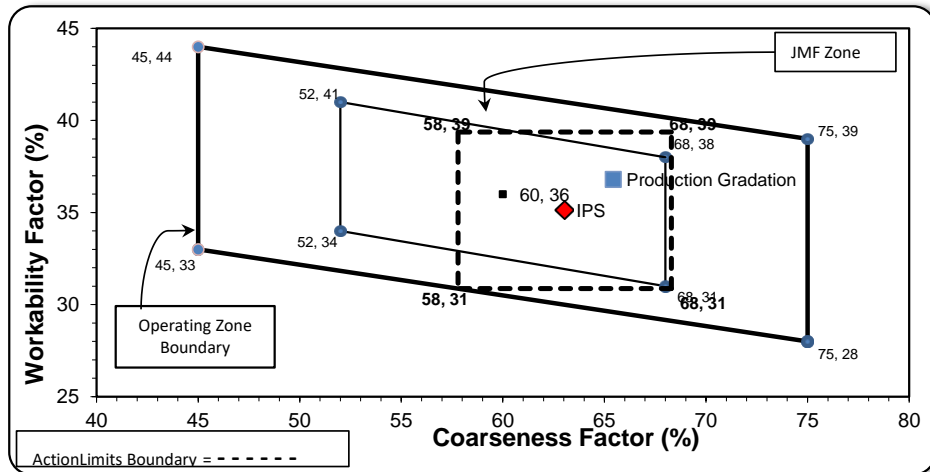

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	99.1	0.9	0.9
3/4"	90.3	8.8	9.7
1/2"	69.2	21.1	30.8
3/8"	59.1	10.1	40.9
#4	41.8	17.3	58.2
#8	35.1	6.6	64.9
#16	28.5	6.6	71.5
#30	21.2	7.3	78.8
#50	8.7	12.5	91.3
#100	1.8	7.0	98.2
LBW	0.7	1.0	99.3

PREPARED BY:
 SM, LLC Technical Service

Approved By:

Aggregate Optimization Chart

PLANT #: **P-39**

Sample Date: 10/26/20

Concrete Grade: **DM**

Contractor: _____

Dates Test Represents: 10/27/2020 through 11/2/2020

MDOT No.: _____

Agg. Class	Pit #	Source	Weight (SSD)	ft ³	Specific Gravity	% Contribution
6AA	71-47	Presque Isle	1605	9.82	2.62	55.2
26A	71-47	Presque Isle	150	0.92	2.62	5.2
2NS	44-051	Krake Willis Rd	1150	6.95	2.65	39.6
Total Wt			2905	17.69		100.0

<----- Verify this number is 100%



Superior Materials, LLC
 30701 W. 10 Mile Rd.
 Suite 500
 Farmington Hills, MI 48336

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	98.0	100.0	100.0	98.9	1.1	1.1
3/4"	81.5	100.0	100.0	89.8	9.1	10.2
1/2"	42.9	98.1	100.0	68.4	21.4	31.6
3/8"	25.1	91.0	100.0	58.2	10.2	41.8
#4	4.3	16.4	96.2	41.3	16.8	58.7
#8	2.0	4.5	82.2	33.9	7.4	66.1
#16	1.6	2.3	66.8	27.4	6.4	72.6
#30	1.5	1.8	52.2	21.6	5.9	78.4
#50	1.5	1.6	26.3	11.3	10.3	88.7
#100	1.4	1.6	7.1	3.7	7.7	96.3
LBW	1.3	1.4	0.8	1.1	2.6	98.9


*Maximum % Retained must be above the 3/8" sieve.
 *Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation Batch Plant Gradations Aggregate Supplier Gradations

Adjusted WF Initial Production Sample (IPS)

Coarseness Factor:	63	Workability Factor:	34	Adjusted WF	36.4
---------------------------	-----------	----------------------------	-----------	--------------------	-------------

Coarseness Factor:	63
Workability Factor:	36

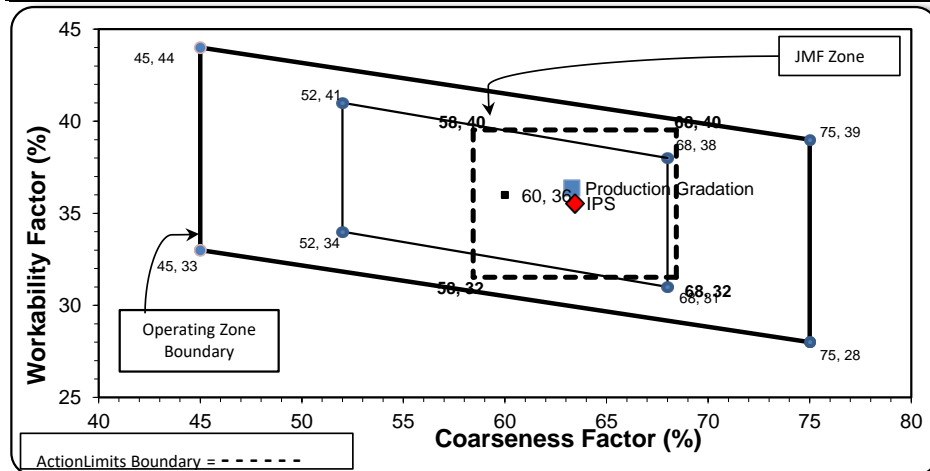

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	100.0	0.0	0.0
3/4"	89.7	10.3	10.3
1/2"	70.3	19.4	29.7
3/8"	59.1	11.2	40.9
#4	42.8	16.3	57.2
#8	35.5	7.3	64.5
#16	29.0	6.5	71.0
#30	21.2	7.7	78.8
#50	9.8	11.5	90.2
#100	3.7	6.1	96.3
LBW	1.2	2.5	98.8

PREPARED BY:
 SM, LLC Technical Service

Approved By:

Aggregate Optimization Chart

PLANT #: **P-02**

Sample Date: 10/26/20

Concrete Grade: **DM**

Contractor: _____

Dates Test Represents: 10/27/2020 through 11/2/2020

MDOT No.: _____

Agg. Class	Pit #	Source	Weight (SSD)	ft ³	Specific Gravity	% Contribution
6AA	71-47	Presque Isle	1655	10.12	2.62	57.0
26A	71-47	Presque Isle	100	0.61	2.62	3.4
2NS	63-115	Ray Rd	1150	6.95	2.65	39.6
Total Wt			2905	17.69		100.0

<----- Verify this number is 100%



Superior Materials, LLC
 30701 W. 10 Mile Rd.
 Suite 500
 Farmington Hills, MI 48336

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	96.6	100.0	100.0	98.1	1.9	1.9
3/4"	75.4	100.0	100.0	86.0	12.1	14.0
1/2"	37.4	97.4	100.0	64.2	21.7	35.8
3/8"	23.5	89.6	100.0	56.1	8.2	43.9
#4	5.4	17.0	98.0	42.5	13.6	57.5
#8	2.7	4.8	81.3	33.9	8.6	66.1
#16	2.2	2.6	64.6	26.9	7.0	73.1
#30	2.1	2.3	48.2	20.4	6.6	79.6
#50	2.0	2.2	21.8	9.8	10.5	90.2
#100	1.9	2.1	3.6	2.6	7.3	97.4
LBW	1.5	1.9	0.3	1.0	1.5	99.0


*Maximum % Retained must be above the 3/8" sieve.
 *Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation Batch Plant Gradations Aggregate Supplier Gradations

Adjusted WF Initial Production Sample (IPS)

Coarseness Factor:	66	Workability Factor:	34	Adjusted WF	36.4
---------------------------	-----------	----------------------------	-----------	--------------------	-------------

Coarseness Factor:	63
Workability Factor:	35

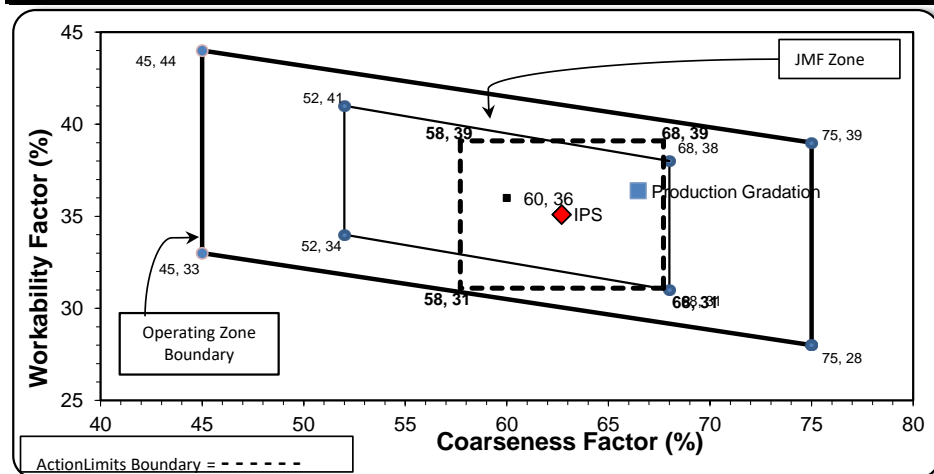

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	100.0	0.0	0.0
3/4"	95.1	4.9	4.9
1/2"	74.6	20.5	25.4
3/8"	59.3	15.3	40.7
#4	42.1	17.2	57.9
#8	35.1	7.1	64.9
#16	29.2	5.9	70.8
#30	21.9	7.3	78.1
#50	9.6	12.4	90.4
#100	2.4	7.2	97.6
LBW	0.9	1.5	99.1

PREPARED BY:
 SM, LLC Technical Service

Approved By:
