

# Aggregate Optimization Chart

## Production Gradation Report

**PLANT #:** **P-101**

Sample Date: 5/25/20

Concrete Grade: **DM**

Contractor: \_\_\_\_\_

Dates Test Represents: 5/26/2020 through 6/1/2020

MDOT No.: \_\_\_\_\_

Agg. Class	Pit #	Source	Weight (SSD)	ft <sup>3</sup>	Specific Gravity	% Contribution
6AA	71-47	Presque Isle	1660	10.15	2.62	57.0
26A	71-47	Presque Isle	100	0.61	2.62	3.4
2NS	75-051	Mid-Michigan	1150	6.93	2.66	39.5
<b>Total Wt</b>			<b>2910</b>	<b>17.69</b>		<b>100.0</b>

<----- Verify this number is 100%



**Superior Materials, LLC**  
 30701 W. 10 Mile Rd.  
 Suite 500  
 Farmington Hills, MI 48336

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	98.3	100.0	100.0	99.0	1.0	1.0
3/4"	82.2	100.0	100.0	89.8	9.2	10.2
1/2"	42.6	96.1	100.0	67.1	22.7	32.9
3/8"	26.5	87.3	100.0	57.6	9.5	42.4
#4	4.7	23.2	97.8	42.1	15.5	57.9
#8	2.3	6.6	81.2	33.6	8.5	66.4
#16	1.8	3.0	65.7	27.1	6.5	72.9
#30	1.7	2.3	49.6	20.7	6.4	79.3
#50	1.6	2.1	26.6	11.5	9.2	88.5
#100	1.5	2.0	5.6	3.1	8.4	96.9
LBW	1.4	1.9	0.8	1.2	2.0	98.8


\*Maximum % Retained must be above the 3/8" sieve.  
 \*Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation  Batch Plant Gradations  Aggregate Supplier Gradations

Adjusted WF Initial Production Sample (IPS)

<b>Coarseness Factor:</b>	<b>64</b>	<b>Workability Factor:</b>	<b>34</b>	<b>Adjusted WF</b>	<b>36.1</b>
---------------------------	-----------	----------------------------	-----------	--------------------	-------------

<b>Coarseness Factor:</b>	<b>62</b>
<b>Workability Factor:</b>	<b>35</b>

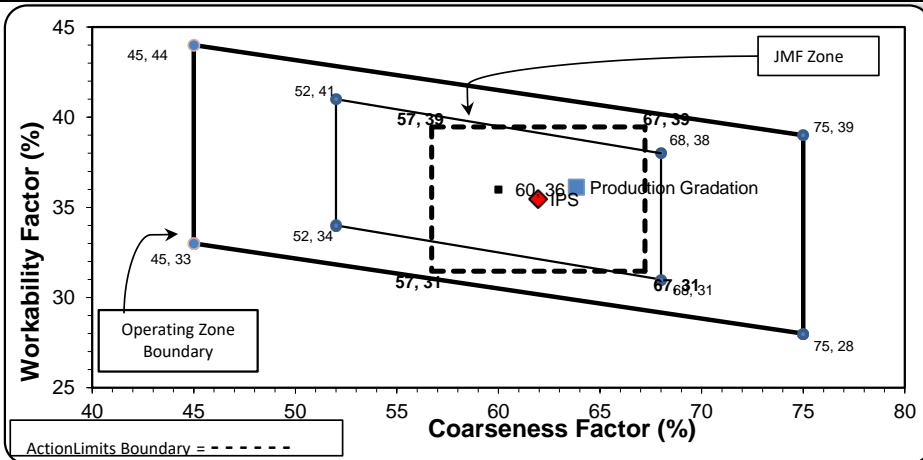

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	100.0	0.0	0.0
3/4"	95.0	5.0	5.0
1/2"	70.5	24.5	29.5
3/8"	60.0	10.5	40.0
#4	44.4	15.6	55.6
#8	35.5	9.0	64.5
#16	28.5	7.0	71.5
#30	21.5	7.0	78.5
#50	10.2	11.3	89.8
#100	3.1	7.1	96.9
LBW	1.3	1.8	98.7

PREPARED BY:  
 SM, LLC Technical Service

Approved By:

# Aggregate Optimization Chart

**PLANT #:** **P-102**

Sample Date: 5/25/20

Concrete Grade: **DM**

Contractor: \_\_\_\_\_

Dates Test Represents: 5/26/2020 through 6/1/2020

MDOT No.: \_\_\_\_\_

Agg. Class	Pit #	Source	Weight (SSD)	ft <sup>3</sup>	Specific Gravity	% Contribution
6AA	58-003	Stoneco	1500	8.94	2.69	50.8
26A	58-003	Stoneco	305	1.82	2.69	10.3
2NS	63-114	Highland	1150	6.95	2.65	38.9
<b>Total Wt</b>			<b>2955</b>	<b>17.71</b>		<b>100.0</b>

<----- Verify this number is 100%



**Superior Materials, LLC**  
 30701 W. 10 Mile Rd.  
 Suite 500  
 Farmington Hills, MI 48336

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	100.0	100.0	100.0	100.0	0.0	0.0
3/4"	83.4	100.0	100.0	91.6	8.4	8.4
1/2"	40.6	99.2	100.0	69.8	21.8	30.2
3/8"	18.8	89.5	100.0	57.7	12.1	42.3
#4	2.9	17.9	99.1	41.9	15.8	58.1
#8	1.5	3.5	83.8	33.7	8.2	66.3
#16	0.9	1.8	66.7	26.6	7.1	73.4
#30	0.8	1.4	49.9	20.0	6.6	80.0
#50	0.7	1.3	23.8	9.8	10.2	90.2
#100	0.6	1.2	4.8	2.3	7.5	97.7
LBW	0.6	1.0	0.4	0.6	1.7	99.4


\*Maximum % Retained must be above the 3/8" sieve.  
 \*Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation  Batch Plant Gradations  Aggregate Supplier Gradations

Adjusted WF Initial Production Sample (IPS)

<b>Coarseness Factor:</b>	<b>64</b>	<b>Workability Factor:</b>	<b>34</b>	<b>36.2</b>
---------------------------	-----------	----------------------------	-----------	-------------

<b>Coarseness Factor:</b>	<b>61</b>
<b>Workability Factor:</b>	<b>36</b>

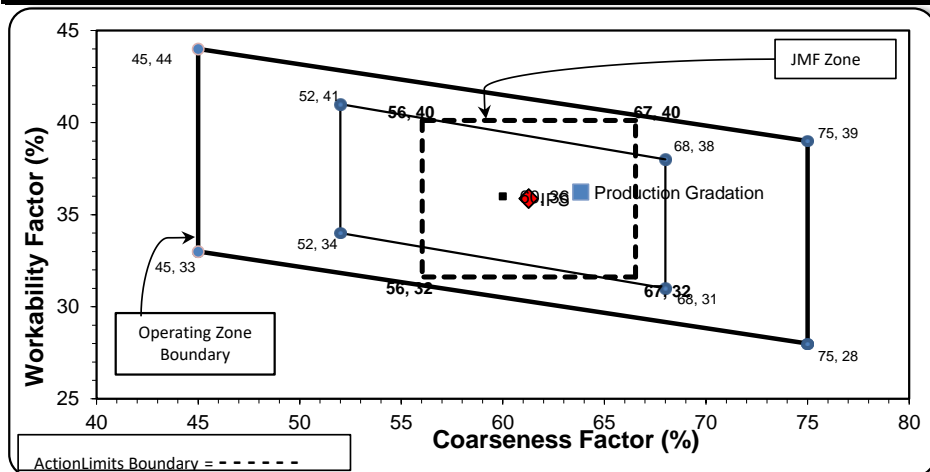

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	99.3	0.7	0.7
3/4"	89.2	10.1	10.8
1/2"	70.7	18.5	29.3
3/8"	60.7	10.0	39.3
#4	44.4	16.3	55.6
#8	35.9	8.5	64.1
#16	27.3	8.6	72.7
#30	19.1	8.2	80.9
#50	7.4	11.7	92.6
#100	1.9	5.6	98.1
LBW	0.7	1.2	99.3

PREPARED BY:  
 SM, LLC Technical Service

Approved By:

# Aggregate Optimization Chart

**PLANT #:** **P-12**

Sample Date: 5/25/20

Concrete Grade: **DM**

Contractor: \_\_\_\_\_

Dates Test Represents: 5/26/2020 through 6/1/2020

MDOT No.: \_\_\_\_\_

Agg. Class	Pit #	Source	Weight (SSD)	ft <sup>3</sup>	Specific Gravity	% Contribution
6AA	71-47	Presque Isle	1405	8.59	2.62	48.4
26A	71-47	Presque Isle	350	2.14	2.62	12.0
2NS	63-115	Ray Rd	1150	6.95	2.65	39.6
<b>Total Wt</b>			<b>2905</b>	<b>17.69</b>		<b>100.0</b>

<----- Verify this number is 100%



**Superior Materials, LLC**  
 30701 W. 10 Mile Rd.  
 Suite 500  
 Farmington Hills, MI 48336

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	99.0	100.0	100.0	99.5	0.5	0.5
3/4"	83.8	100.0	100.0	92.2	7.4	7.8
1/2"	39.0	96.3	100.0	70.1	22.1	29.9
3/8"	16.2	82.8	100.0	57.4	12.7	42.6
#4	3.4	24.4	98.3	43.5	13.9	56.5
#8	2.3	9.1	80.9	34.2	9.3	65.8
#16	1.9	5.3	64.3	27.0	7.2	73.0
#30	1.8	4.5	48.1	20.5	6.6	79.5
#50	1.6	4.1	24.3	10.9	9.6	89.1
#100	1.6	3.7	5.3	3.3	7.6	96.7
LBW	1.2	2.9	0.7	1.2	2.1	98.8


\*Maximum % Retained must be above the 3/8" sieve.  
 \*Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation  Batch Plant Gradations  Aggregate Supplier Gradations

Adjusted WF Initial Production Sample (IPS)

Coarseness Factor:	<b>65</b>	Workability Factor:	<b>34</b>	Adjusted WF	<b>36.7</b>
--------------------	-----------	---------------------	-----------	-------------	-------------

Coarseness Factor:	<b>63</b>
Workability Factor:	<b>36</b>

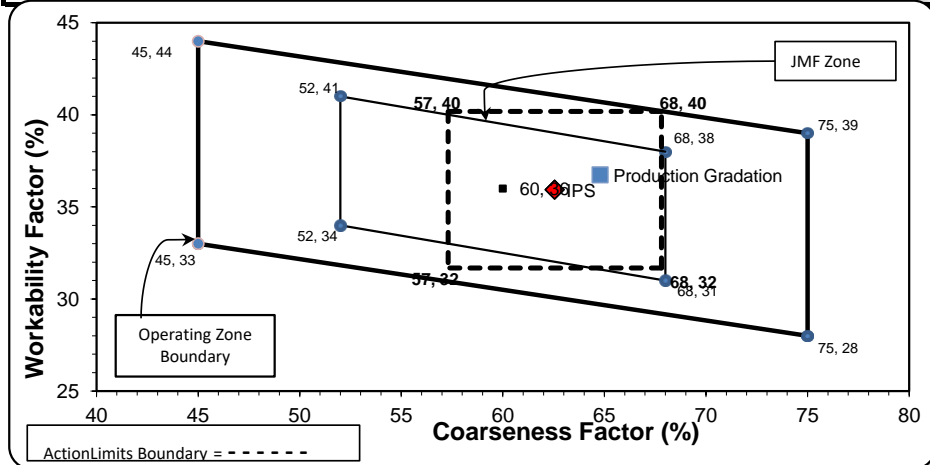

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	99.3	0.7	0.7
3/4"	89.0	10.3	11.0
1/2"	70.3	18.7	29.7
3/8"	59.9	10.4	40.1
#4	41.9	18.0	58.1
#8	35.9	6.0	64.1
#16	27.8	8.2	72.2
#30	18.9	8.8	81.1
#50	6.3	12.6	93.7
#100	1.7	4.6	98.3
LBW	1.0	0.7	99.0

PREPARED BY:  
 SM, LLC Technical Service

Approved By:

# Aggregate Optimization Chart

**PLANT #:** **P-32**

Sample Date: 5/25/20

Concrete Grade: DM

Contractor: \_\_\_\_\_

Dates Test Represents: 5/26/2020 through 6/1/2020

MDOT No.: \_\_\_\_\_

Agg. Class	Pit #	Source	Weight (SSD)	ft <sup>3</sup>	Specific Gravity	% Contribution
6AA	71-47	Presque Isle	1455	8.90	2.62	50.1
26A	71-47	Presque Isle	300	1.83	2.62	10.3
2NS	95-013	Smelter Bay	1150	6.95	2.65	39.6
<b>Total Wt</b>			<b>2905</b>	<b>17.69</b>		<b>100.0</b>

<----- Verify this number is 100%



**Superior Materials, LLC**  
 30701 W. 10 Mile Rd.  
 Suite 500  
 Farmington Hills, MI 48336

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	99.5	100.0	100.0	99.7	0.3	0.3
3/4"	77.8	100.0	100.0	88.9	10.9	11.1
1/2"	42.6	96.3	100.0	70.9	18.0	29.1
3/8"	22.6	82.8	100.0	59.5	11.4	40.5
#4	5.3	24.4	96.7	43.5	16.0	56.5
#8	2.6	9.1	84.1	35.5	7.9	64.5
#16	2.1	5.3	66.2	27.8	7.7	72.2
#30	2.0	4.5	42.6	18.3	9.5	81.7
#50	1.8	4.1	16.7	7.9	10.4	92.1
#100	1.6	3.7	3.6	2.6	5.3	97.4
LBW	1.2	2.9	0.7	1.2	1.4	98.8


\*Maximum % Retained must be above the 3/8" sieve.  
 \*Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation  Batch Plant Gradations  Aggregate Supplier Gradations

Adjusted WF Initial Production Sample (IPS)

<b>Coarseness Factor:</b>	<b>63</b>	<b>Workability Factor:</b>	<b>36</b>	<b>38.0</b>	<b>Coarseness Factor:</b>	<b>62</b>
---------------------------	-----------	----------------------------	-----------	-------------	---------------------------	-----------

<b>Workability Factor:</b>	<b>36</b>
----------------------------	-----------

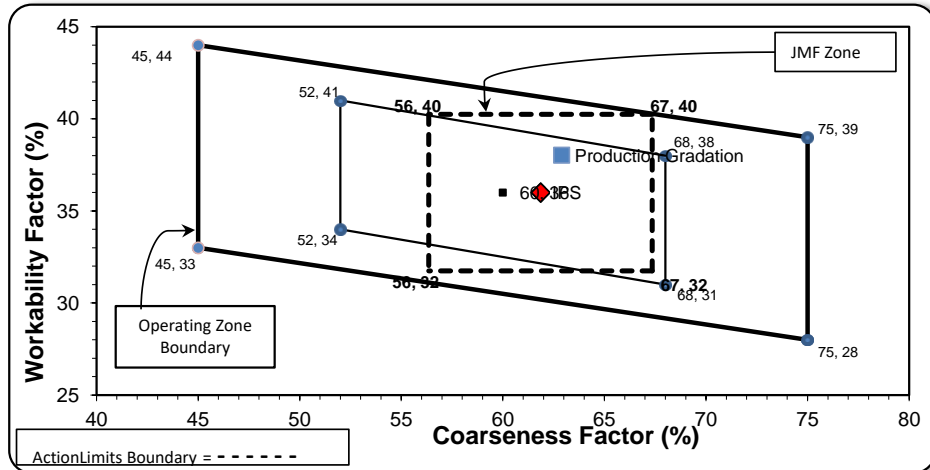

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	100.0	0.0	0.0
3/4"	95.0	5.0	5.0
1/2"	72.3	22.8	27.7
3/8"	60.4	11.8	39.6
#4	42.6	17.8	57.4
#8	36.0	6.6	64.0
#16	29.5	6.5	70.5
#30	20.3	9.2	79.7
#50	9.5	10.8	90.5
#100	3.4	6.1	96.6
LBW	1.3	2.1	98.7

PREPARED BY:  
 SM, LLC Technical Service

Approved By:

# Aggregate Optimization Chart

**PLANT #:** **P-35**

Sample Date: 5/25/20

Concrete Grade: **DM**

Contractor: \_\_\_\_\_

Dates Test Represents: 5/26/2020 through 6/1/2020

MDOT No.: \_\_\_\_\_

Agg. Class	Pit #	Source	Weight (SSD)	ft <sup>3</sup>	Specific Gravity	% Contribution
6AA	58-003	Stoneco	1400	8.34	2.69	47.4
26A	58-003	Stoneco	455	2.71	2.69	15.4
2NS	81-093	Burmeister	1100	6.65	2.65	37.2
<b>Total Wt</b>			<b>2955</b>	<b>17.70</b>		<b>100.0</b>

<----- Verify this number is 100%



**Superior Materials, LLC**  
 30701 W. 10 Mile Rd.  
 Suite 500  
 Farmington Hills, MI 48336

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	100.0	100.0	100.0	100.0	0.0	0.0
3/4"	83.4	100.0	100.0	92.1	7.9	7.9
1/2"	40.6	99.2	100.0	71.7	20.4	28.3
3/8"	18.8	89.5	100.0	59.9	11.8	40.1
#4	2.9	17.9	98.3	40.7	19.2	59.3
#8	1.5	3.5	90.1	34.8	5.9	65.2
#16	0.9	1.8	66.1	25.3	9.5	74.7
#30	0.8	1.4	47.8	18.4	6.9	81.6
#50	0.7	1.3	21.0	8.3	10.0	91.7
#100	0.6	1.2	4.0	2.0	6.4	98.0
LBW	0.6	1.0	1.1	0.8	1.1	99.2


\*Maximum % Retained must be above the 3/8" sieve.  
 \*Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation  Batch Plant Gradations  Aggregate Supplier Gradations

Adjusted WF Initial Production Sample (IPS)

<b>Coarseness Factor:</b>	<b>61</b>	<b>Workability Factor:</b>	<b>35</b>	<b>37.3</b>
---------------------------	-----------	----------------------------	-----------	-------------

<b>Coarseness Factor:</b>	<b>61</b>
<b>Workability Factor:</b>	<b>36</b>

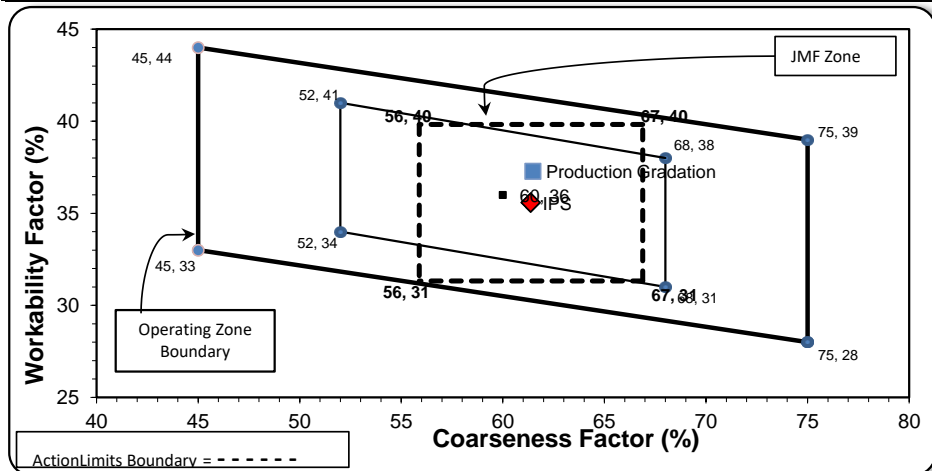

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	99.3	0.7	0.7
3/4"	89.1	10.2	10.9
1/2"	70.5	18.6	29.5
3/8"	60.5	10.0	39.5
#4	44.1	16.4	55.9
#8	35.6	8.5	64.4
#16	27.7	7.9	72.3
#30	20.6	7.1	79.4
#50	8.7	11.8	91.3
#100	1.6	7.1	98.4
LBW	1.1	0.6	98.9

PREPARED BY:  
 SM, LLC Technical Service

Approved By:

# Aggregate Optimization Chart

**PLANT #:** **P-36**

Sample Date: 5/25/20

Concrete Grade: **DM**

Contractor: \_\_\_\_\_

Dates Test Represents: 5/26/2020 through 6/1/2020

MDOT No.: \_\_\_\_\_

Agg. Class	Pit #	Source	Weight (SSD)	ft <sup>3</sup>	Specific Gravity	% Contribution
6AA	71-47	Presque Isle	1400	8.56	2.62	48.2
26A	71-47	Presque Isle	405	2.48	2.62	13.9
2NS	63-92	Grange Hall	1100	6.65	2.65	37.9
<b>Total Wt</b>			<b>2905</b>	<b>17.69</b>		<b>100.0</b>

<----- Verify this number is 100%



**Superior Materials, LLC**  
 30701 W. 10 Mile Rd.  
 Suite 500  
 Farmington Hills, MI 48336

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	99.0	100.0	100.0	99.5	0.5	0.5
3/4"	83.8	100.0	100.0	92.2	7.3	7.8
1/2"	39.0	96.3	100.0	70.1	22.1	29.9
3/8"	16.2	82.8	100.0	57.2	12.9	42.8
#4	3.4	24.4	97.6	42.0	15.2	58.0
#8	2.3	9.1	86.0	34.9	7.1	65.1
#16	1.9	5.3	72.0	28.9	6.0	71.1
#30	1.8	4.5	51.8	21.1	7.8	78.9
#50	1.6	4.1	22.9	10.0	11.1	90.0
#100	1.6	3.7	3.0	2.4	7.6	97.6
LBW	1.2	2.9	0.5	1.2	1.3	98.8


\*Maximum % Retained must be above the 3/8" sieve.  
 \*Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation  Batch Plant Gradations  Aggregate Supplier Gradations

Adjusted WF Initial Production Sample (IPS)

<b>Coarseness Factor:</b>	<b>66</b>	<b>Workability Factor:</b>	<b>35</b>	<b>Adjusted WF</b>	<b>37.4</b>
---------------------------	-----------	----------------------------	-----------	--------------------	-------------

<b>Coarseness Factor:</b>	<b>63</b>
<b>Workability Factor:</b>	<b>35</b>

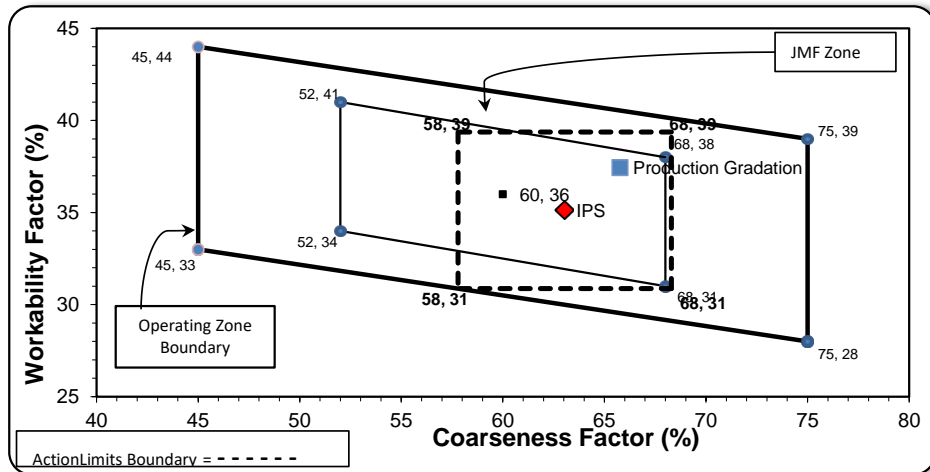

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	99.1	0.9	0.9
3/4"	90.3	8.8	9.7
1/2"	69.2	21.1	30.8
3/8"	59.1	10.1	40.9
#4	41.8	17.3	58.2
#8	35.1	6.6	64.9
#16	28.5	6.6	71.5
#30	21.2	7.3	78.8
#50	8.7	12.5	91.3
#100	1.8	7.0	98.2
LBW	0.7	1.0	99.3

PREPARED BY:  
 SM, LLC Technical Service

Approved By:

# Aggregate Optimization Chart

**PLANT #:** **P-39**

Sample Date: 5/25/20

Concrete Grade: **DM**

Contractor: \_\_\_\_\_

Dates Test Represents: 5/26/2020 through 6/1/2020

MDOT No.: \_\_\_\_\_

Agg. Class	Pit #	Source	Weight (SSD)	ft <sup>3</sup>	Specific Gravity	% Contribution
6AA	71-47	Presque Isle	1605	9.82	2.62	55.2
26A	71-47	Presque Isle	200	1.22	2.62	6.9
2NS	44-051	Krake Willis Rd	1100	6.65	2.65	37.9
<b>Total Wt</b>			<b>2905</b>	<b>17.69</b>		<b>100.0</b>

<----- Verify this number is 100%



**Superior Materials, LLC**  
 30701 W. 10 Mile Rd.  
 Suite 500  
 Farmington Hills, MI 48336

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	98.3	100.0	100.0	99.1	0.9	0.9
3/4"	82.2	100.0	100.0	90.2	8.9	9.8
1/2"	42.6	96.1	100.0	68.0	22.1	32.0
3/8"	26.5	87.3	100.0	58.5	9.5	41.5
#4	4.7	23.2	95.4	40.3	18.2	59.7
#8	2.3	6.6	81.2	32.5	7.8	67.5
#16	1.8	3.0	66.3	26.3	6.2	73.7
#30	1.7	2.3	50.6	20.3	6.0	79.7
#50	1.6	2.1	25.1	10.5	9.7	89.5
#100	1.5	2.0	7.5	3.8	6.7	96.2
LBW	1.4	1.9	0.8	1.2	2.6	98.8


\*Maximum % Retained must be above the 3/8" sieve.  
 \*Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation  Batch Plant Gradations  Aggregate Supplier Gradations

Adjusted WF Initial Production Sample (IPS)

<b>Coarseness Factor:</b>	<b>61</b>	<b>Workability Factor:</b>	<b>32</b>	<b>Adjusted WF</b>	<b>35.0</b>
---------------------------	-----------	----------------------------	-----------	--------------------	-------------

<b>Coarseness Factor:</b>	<b>63</b>
<b>Workability Factor:</b>	<b>36</b>

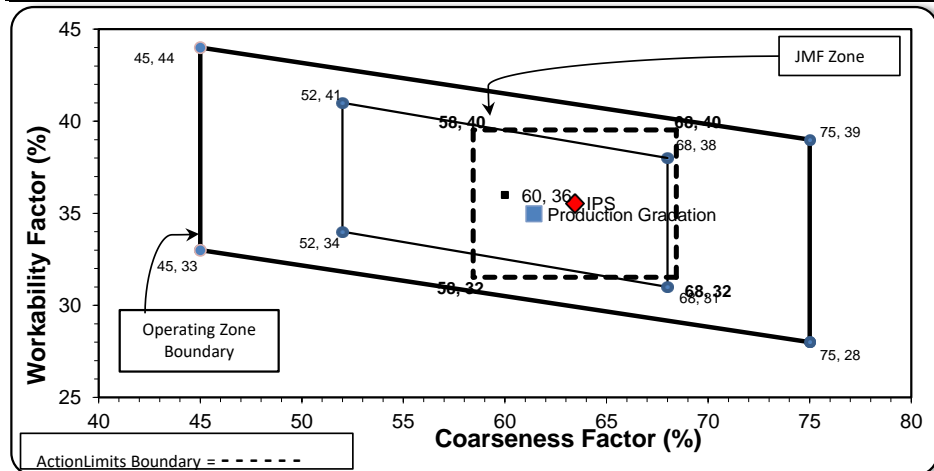

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	100.0	0.0	0.0
3/4"	89.7	10.3	10.3
1/2"	70.3	19.4	29.7
3/8"	59.1	11.2	40.9
#4	42.8	16.3	57.2
#8	35.5	7.3	64.5
#16	29.0	6.5	71.0
#30	21.2	7.7	78.8
#50	9.8	11.5	90.2
#100	3.7	6.1	96.3
LBW	1.2	2.5	98.8

PREPARED BY:  
 SM, LLC Technical Service

Approved By:

# Aggregate Optimization Chart

**PLANT #:** **P-02**

Sample Date: 5/25/20

Concrete Grade: **DM**

Contractor: \_\_\_\_\_

Dates Test Represents: 5/26/2020 through 6/1/2020

MDOT No.: \_\_\_\_\_

Agg. Class	Pit #	Source	Weight (SSD)	ft <sup>3</sup>	Specific Gravity	% Contribution
6AA	71-47	Presque Isle	1400	8.56	2.62	48.2
26A	71-47	Presque Isle	355	2.17	2.62	12.2
2NS	63-115	Ray Rd	1150	6.95	2.65	39.6
<b>Total Wt</b>			<b>2905</b>	<b>17.69</b>		<b>100.0</b>

<----- Verify this number is 100%



**Superior Materials, LLC**  
 30701 W. 10 Mile Rd.  
 Suite 500  
 Farmington Hills, MI 48336

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	99.0	100.0	100.0	99.5	0.5	0.5
3/4"	83.8	100.0	100.0	92.2	7.3	7.8
1/2"	39.0	96.3	100.0	70.2	22.0	29.8
3/8"	16.2	82.8	100.0	57.5	12.6	42.5
#4	3.4	24.4	98.3	43.5	14.0	56.5
#8	2.3	9.1	80.9	34.2	9.3	65.8
#16	1.9	5.3	64.3	27.0	7.2	73.0
#30	1.8	4.5	48.1	20.5	6.6	79.5
#50	1.6	4.1	24.3	10.9	9.6	89.1
#100	1.6	3.7	5.3	3.3	7.6	96.7
LBW	1.2	2.9	0.7	1.2	2.1	98.8


\*Maximum % Retained must be above the 3/8" sieve.  
 \*Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation  Batch Plant Gradations  Aggregate Supplier Gradations

Adjusted WF Initial Production Sample (IPS)

<b>Coarseness Factor:</b>	<b>65</b>	<b>Workability Factor:</b>	<b>34</b>	<b>Adjusted WF</b>	<b>36.7</b>
---------------------------	-----------	----------------------------	-----------	--------------------	-------------

<b>Coarseness Factor:</b>	<b>63</b>
<b>Workability Factor:</b>	<b>35</b>

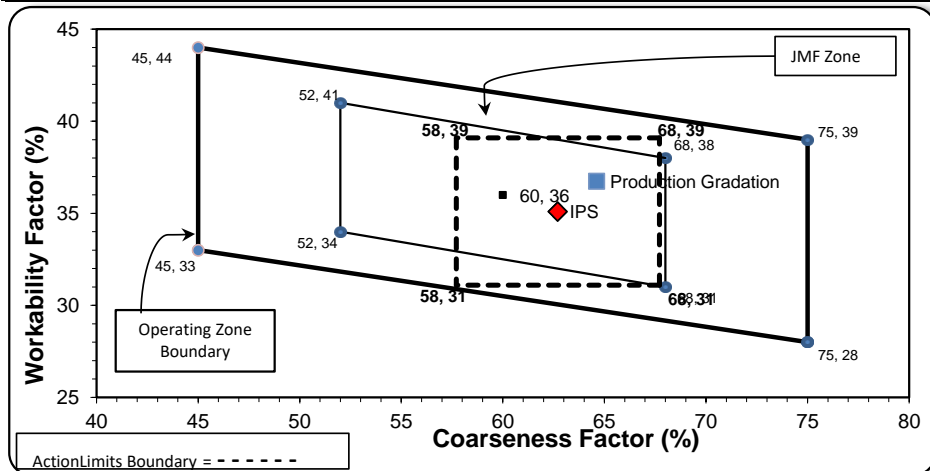

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	100.0	0.0	0.0
3/4"	95.1	4.9	4.9
1/2"	74.6	20.5	25.4
3/8"	59.3	15.3	40.7
#4	42.1	17.2	57.9
#8	35.1	7.1	64.9
#16	29.2	5.9	70.8
#30	21.9	7.3	78.1
#50	9.6	12.4	90.4
#100	2.4	7.2	97.6
LBW	0.9	1.5	99.1

PREPARED BY:  
 SM, LLC Technical Service

Approved By:
