

Aggregate Optimization Chart

Production Gradation Report

PLANT #: **P-101**

Sample Date: 6/29/20

Concrete Grade: **DM**

Contractor: _____

Dates Test Represents: 6/30/2020 through 7/6/2020

MDOT No.: _____

Agg. Class	Pit #	Source	Weight (SSD)	ft ³	Specific Gravity	% Contribution
6AA	71-47	Presque Isle	1560	9.54	2.62	53.6
26A	71-47	Presque Isle	200	1.22	2.62	6.9
2NS	75-051	Mid-Michigan	1150	6.93	2.66	39.5
Total Wt			2910	17.69		100.0

<----- Verify this number is 100%



Superior Materials, LLC
 30701 W. 10 Mile Rd.
 Suite 500
 Farmington Hills, MI 48336

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	98.6	100.0	100.0	99.2	0.8	0.8
3/4"	85.4	100.0	100.0	92.2	7.1	7.8
1/2"	47.6	96.3	100.0	71.7	20.5	28.3
3/8"	24.2	85.1	100.0	58.3	13.3	41.7
#4	4.4	21.7	98.1	42.6	15.7	57.4
#8	2.0	5.8	82.7	34.2	8.5	65.8
#16	1.6	2.8	67.7	27.8	6.3	72.2
#30	1.5	2.2	50.7	21.0	6.8	79.0
#50	1.4	2.0	26.2	11.2	9.7	88.8
#100	1.4	1.9	6.6	3.5	7.8	96.5
LBW	1.3	1.7	0.9	1.2	2.3	98.8


*Maximum % Retained must be above the 3/8" sieve.
 *Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation Batch Plant Gradations Aggregate Supplier Gradations

Adjusted WF Initial Production Sample (IPS)

Coarseness Factor:	63	Workability Factor:	34	Adjusted WF	36.7
---------------------------	-----------	----------------------------	-----------	--------------------	-------------

Coarseness Factor:	62
Workability Factor:	35

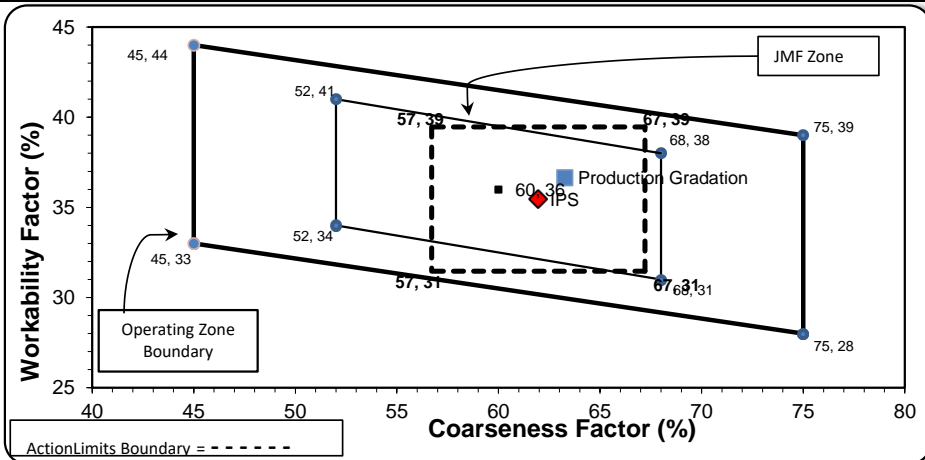

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	100.0	0.0	0.0
3/4"	95.0	5.0	5.0
1/2"	70.5	24.5	29.5
3/8"	60.0	10.5	40.0
#4	44.4	15.6	55.6
#8	35.5	9.0	64.5
#16	28.5	7.0	71.5
#30	21.5	7.0	78.5
#50	10.2	11.3	89.8
#100	3.1	7.1	96.9
LBW	1.3	1.8	98.7

PREPARED BY:
 SM, LLC Technical Service

Approved By:

Aggregate Optimization Chart

PLANT #: **P-102**

Sample Date: 6/29/20

Concrete Grade: DM

Contractor: _____

Dates Test Represents: 6/30/2020 through 7/6/2020

MDOT No.: _____

Agg. Class	Pit #	Source	Weight (SSD)	ft ³	Specific Gravity	% Contribution
6AA	58-003	Stoneco	1500	8.94	2.69	50.8
26A	58-003	Stoneco	305	1.82	2.69	10.3
2NS	63-114	Highland	1150	6.95	2.65	38.9
Total Wt			2955	17.71		100.0

<----- Verify this number is 100%



Superior Materials, LLC
 30701 W. 10 Mile Rd.
 Suite 500
 Farmington Hills, MI 48336

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	100.0	100.0	100.0	100.0	0.0	0.0
3/4"	86.4	100.0	100.0	93.1	6.9	6.9
1/2"	49.5	99.4	100.0	74.3	18.8	25.7
3/8"	24.2	80.7	100.0	59.5	14.8	40.5
#4	5.3	21.1	99.2	43.5	16.1	56.5
#8	1.8	5.5	83.9	34.1	9.3	65.9
#16	1.4	2.6	65.8	26.6	7.5	73.4
#30	1.2	2.0	48.5	19.7	6.9	80.3
#50	1.1	1.9	20.5	8.7	11.0	91.3
#100	1.0	1.8	3.8	2.2	6.6	97.8
LBW	0.7	1.5	0.3	0.6	1.5	99.4


*Maximum % Retained must be above the 3/8" sieve.
 *Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation Batch Plant Gradations Aggregate Supplier Gradations

Adjusted WF Initial Production Sample (IPS)

Coarseness Factor:	61	Workability Factor:	34	36.6
---------------------------	-----------	----------------------------	-----------	-------------

Coarseness Factor:	61
Workability Factor:	36

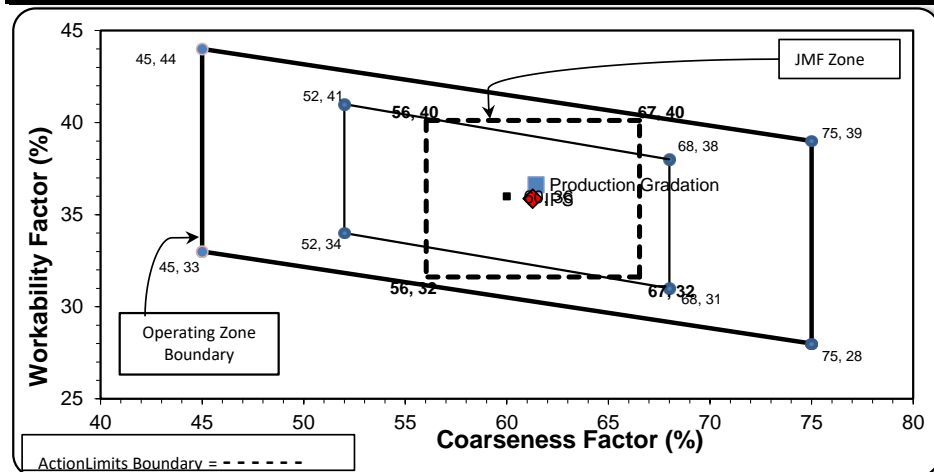

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	99.3	0.7	0.7
3/4"	89.2	10.1	10.8
1/2"	70.7	18.5	29.3
3/8"	60.7	10.0	39.3
#4	44.4	16.3	55.6
#8	35.9	8.5	64.1
#16	27.3	8.6	72.7
#30	19.1	8.2	80.9
#50	7.4	11.7	92.6
#100	1.9	5.6	98.1
LBW	0.7	1.2	99.3

PREPARED BY:
 SM, LLC Technical Service

Approved By:

Aggregate Optimization Chart

PLANT #: **P-12**

Sample Date: 6/29/20

Concrete Grade: **DM**

Contractor: _____

Dates Test Represents: 6/30/2020 through 7/6/2020

MDOT No.: _____

Agg. Class	Pit #	Source	Weight (SSD)	ft ³	Specific Gravity	% Contribution
6AA	71-47	Presque Isle	1505	9.21	2.62	51.8
26A	71-47	Presque Isle	250	1.53	2.62	8.6
2NS	63-115	Ray Rd	1150	6.95	2.65	39.6
Total Wt			2905	17.69		100.0

<----- Verify this number is 100%



Superior Materials, LLC
 30701 W. 10 Mile Rd.
 Suite 500
 Farmington Hills, MI 48336

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	98.2	100.0	100.0	99.1	0.9	0.9
3/4"	79.1	100.0	100.0	89.2	9.9	10.8
1/2"	41.9	97.1	100.0	69.7	19.5	30.3
3/8"	23.1	87.3	100.0	59.1	10.6	40.9
#4	4.6	27.8	98.1	43.6	15.5	56.4
#8	2.3	9.5	80.5	33.9	9.7	66.1
#16	2.0	4.6	63.4	26.5	7.3	73.5
#30	1.8	3.2	47.8	20.1	6.4	79.9
#50	1.7	2.7	25.0	11.0	9.1	89.0
#100	1.6	2.3	5.5	3.2	7.8	96.8
LBW	1.2	1.6	0.8	1.1	2.1	98.9


*Maximum % Retained must be above the 3/8" sieve.
 *Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation Batch Plant Gradations Aggregate Supplier Gradations

Adjusted WF Initial Production Sample (IPS)

Coarseness Factor: **62** Workability Factor: **34** Adjusted WF: **36.4**

Coarseness Factor: **63**
 Workability Factor: **36**

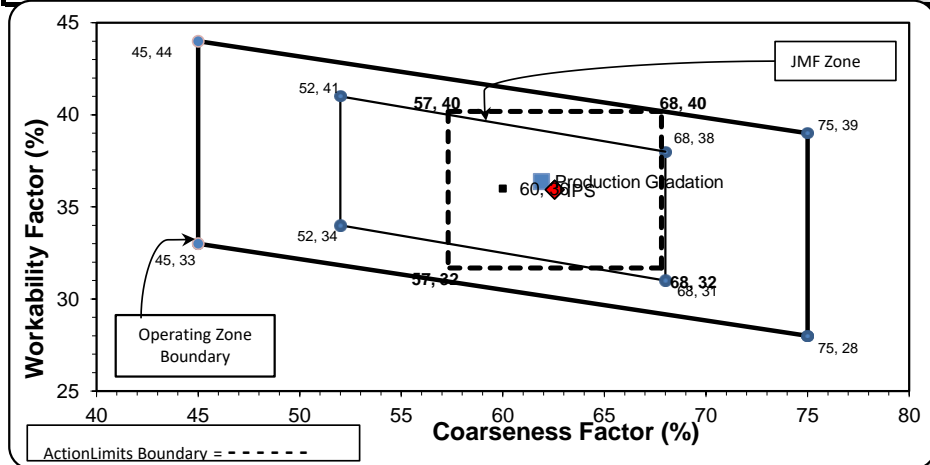

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	99.3	0.7	0.7
3/4"	89.0	10.3	11.0
1/2"	70.3	18.7	29.7
3/8"	59.9	10.4	40.1
#4	41.9	18.0	58.1
#8	35.9	6.0	64.1
#16	27.8	8.2	72.2
#30	18.9	8.8	81.1
#50	6.3	12.6	93.7
#100	1.7	4.6	98.3
LBW	1.0	0.7	99.0

PREPARED BY:
 SM, LLC Technical Service

Approved By:

Aggregate Optimization Chart

PLANT #: **P-32**

Sample Date: 6/29/20 Concrete Grade: DM
 Dates Test Represents: 6/30/2020 through 7/6/2020

Contractor: _____

MDOT No.: _____

Agg. Class	Pit #	Source	Weight (SSD)	ft ³	Specific Gravity	% Contribution
6AA	71-47	Presque Isle	1550	9.48	2.62	53.4
26A	71-47	Presque Isle	205	1.25	2.62	7.1
2NS	95-013	Smelter Bay	1150	6.95	2.65	39.6
Total Wt			2905	17.69		100.0

<----- Verify this number is 100%



Superior Materials, LLC
 30701 W. 10 Mile Rd.
 Suite 500
 Farmington Hills, MI 48336


Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	98.7	100.0	100.0	99.3	0.7	0.7
3/4"	78.8	100.0	100.0	88.7	10.6	11.3
1/2"	42.3	97.1	100.0	69.0	19.7	31.0
3/8"	25.4	87.3	100.0	59.3	9.7	40.7
#4	6.7	27.8	96.3	43.7	15.6	56.3
#8	3.3	9.5	82.1	34.9	8.7	65.1
#16	2.7	4.6	66.0	27.9	7.0	72.1
#30	2.5	3.2	46.5	20.0	7.9	80.0
#50	2.3	2.7	21.5	9.9	10.0	90.1
#100	2.1	2.3	5.7	3.5	6.4	96.5
LBW	1.6	1.6	1.1	1.4	2.1	98.6

*Maximum % Retained must be above the 3/8" sieve.
 *Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation Batch Plant Gradations Aggregate Supplier Gradations Adjusted WF Initial Production Sample (IPS)

Coarseness Factor:	63	Workability Factor:	35	Adjusted WF	37.4
---------------------------	-----------	----------------------------	-----------	--------------------	-------------

Coarseness Factor:	62
Workability Factor:	36

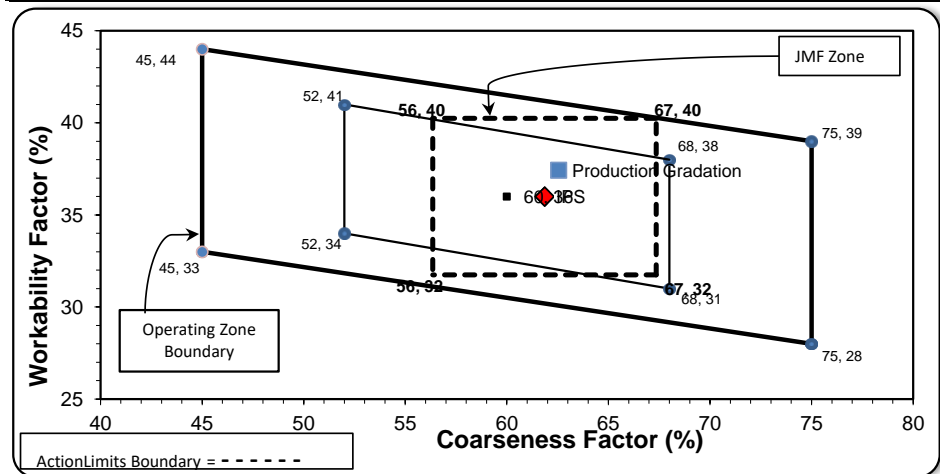

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	100.0	0.0	0.0
3/4"	95.0	5.0	5.0
1/2"	72.3	22.8	27.7
3/8"	60.4	11.8	39.6
#4	42.6	17.8	57.4
#8	36.0	6.6	64.0
#16	29.5	6.5	70.5
#30	20.3	9.2	79.7
#50	9.5	10.8	90.5
#100	3.4	6.1	96.6
LBW	1.3	2.1	98.7

PREPARED BY:
 SM, LLC Technical Service

Approved By:

Aggregate Optimization Chart

PLANT #: **P-35**

Sample Date: 6/29/20

Concrete Grade: **DM**

Contractor: _____

Dates Test Represents: 6/30/2020 through 7/6/2020

MDOT No.: _____

Agg. Class	Pit #	Source	Weight (SSD)	ft ³	Specific Gravity	% Contribution
6AA	58-003	Stoneco	1500	8.94	2.69	50.8
26A	58-003	Stoneco	355	2.11	2.69	12.0
2NS	81-093	Burmeister	1100	6.65	2.65	37.2
Total Wt			2955	17.70		100.0

<----- Verify this number is 100%



Superior Materials, LLC
 30701 W. 10 Mile Rd.
 Suite 500
 Farmington Hills, MI 48336

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	100.0	100.0	100.0	100.0	0.0	0.0
3/4"	86.4	100.0	100.0	93.1	6.9	6.9
1/2"	49.5	99.4	100.0	74.3	18.8	25.7
3/8"	24.2	80.7	100.0	59.2	15.1	40.8
#4	5.3	21.1	98.0	41.7	17.5	58.3
#8	1.8	5.5	89.7	35.0	6.7	65.0
#16	1.4	2.6	67.0	26.0	9.0	74.0
#30	1.2	2.0	47.8	18.6	7.3	81.4
#50	1.1	1.9	20.0	8.2	10.4	91.8
#100	1.0	1.8	4.0	2.2	6.0	97.8
LBW	0.7	1.5	1.2	1.0	1.2	99.0


*Maximum % Retained must be above the 3/8" sieve.
 *Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation Batch Plant Gradations Aggregate Supplier Gradations

Adjusted WF Initial Production Sample (IPS)

Coarseness Factor:	63	Workability Factor:	35	37.5
---------------------------	-----------	----------------------------	-----------	-------------

Coarseness Factor:	61
Workability Factor:	36

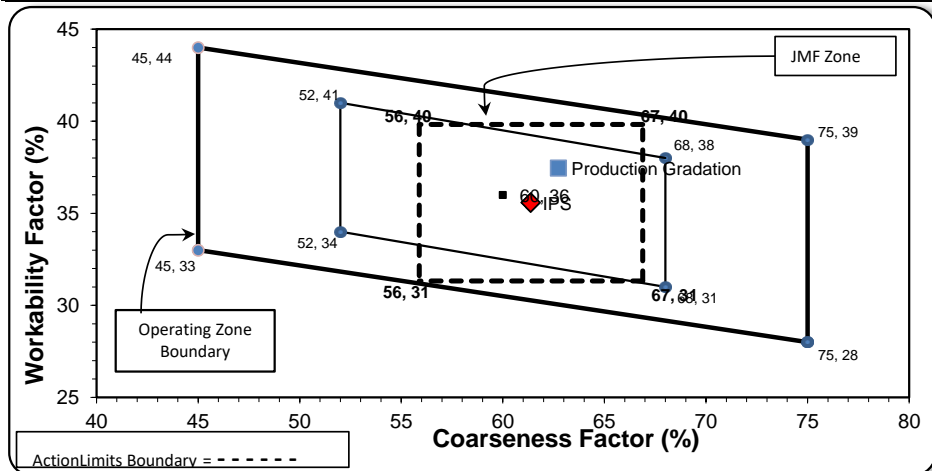

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	99.3	0.7	0.7
3/4"	89.1	10.2	10.9
1/2"	70.5	18.6	29.5
3/8"	60.5	10.0	39.5
#4	44.1	16.4	55.9
#8	35.6	8.5	64.4
#16	27.7	7.9	72.3
#30	20.6	7.1	79.4
#50	8.7	11.8	91.3
#100	1.6	7.1	98.4
LBW	1.1	0.6	98.9

PREPARED BY:
 SM, LLC Technical Service

Approved By:

Aggregate Optimization Chart

PLANT #: **P-36**

Sample Date: 6/29/20

Concrete Grade: DM

Contractor: _____

Dates Test Represents: 6/30/2020 through 7/6/2020

MDOT No.: _____

Agg. Class	Pit #	Source	Weight (SSD)	ft ³	Specific Gravity	% Contribution
6AA	71-47	Presque Isle	1555	9.51	2.62	53.5
26A	71-47	Presque Isle	250	1.53	2.62	8.6
2NS	63-92	Grange Hall	1100	6.65	2.65	37.9
Total Wt			2905	17.69		100.0

<----- Verify this number is 100%



Superior Materials, LLC
 30701 W. 10 Mile Rd.
 Suite 500
 Farmington Hills, MI 48336

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	98.2	100.0	100.0	99.0	1.0	1.0
3/4"	79.1	100.0	100.0	88.8	10.2	11.2
1/2"	41.9	97.1	100.0	68.7	20.2	31.3
3/8"	23.1	87.3	100.0	57.7	10.9	42.3
#4	4.6	27.8	97.4	41.7	16.0	58.3
#8	2.3	9.5	83.8	33.8	8.0	66.2
#16	2.0	4.6	67.9	27.2	6.6	72.8
#30	1.8	3.2	47.7	19.3	7.9	80.7
#50	1.7	2.7	20.4	8.9	10.4	91.1
#100	1.6	2.3	3.0	2.2	6.7	97.8
LBW	1.2	1.6	0.7	1.0	1.1	99.0


*Maximum % Retained must be above the 3/8" sieve.
 *Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation Batch Plant Gradations Aggregate Supplier Gradations

Adjusted WF Initial Production Sample (IPS)

Coarseness Factor:	64	Workability Factor:	34	Adjusted WF	36.3
---------------------------	-----------	----------------------------	-----------	--------------------	-------------

Coarseness Factor:	63
Workability Factor:	35

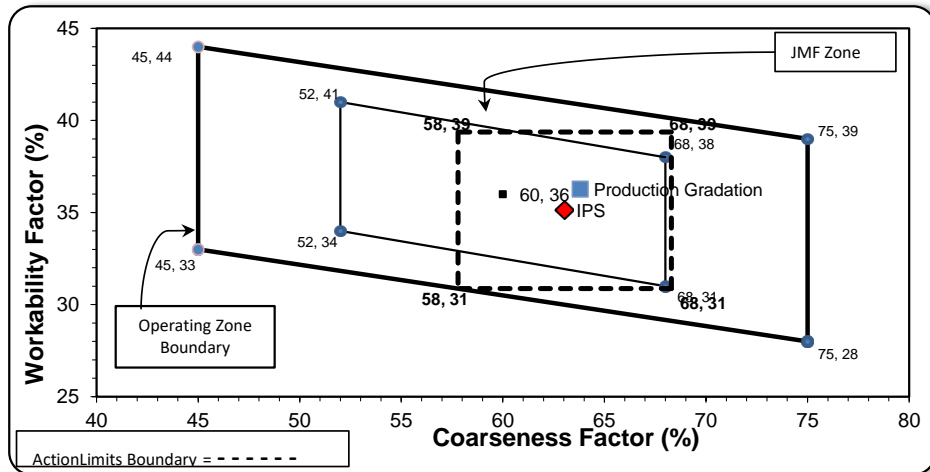

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	99.1	0.9	0.9
3/4"	90.3	8.8	9.7
1/2"	69.2	21.1	30.8
3/8"	59.1	10.1	40.9
#4	41.8	17.3	58.2
#8	35.1	6.6	64.9
#16	28.5	6.6	71.5
#30	21.2	7.3	78.8
#50	8.7	12.5	91.3
#100	1.8	7.0	98.2
LBW	0.7	1.0	99.3

PREPARED BY:
 SM, LLC Technical Service

Approved By:

Aggregate Optimization Chart

PLANT #: **P-39**

Sample Date: 6/29/20

Concrete Grade: **DM**

Contractor: _____

Dates Test Represents: 6/30/2020 through 7/6/2020

MDOT No.: _____

Agg. Class	Pit #	Source	Weight (SSD)	ft ³	Specific Gravity	% Contribution
6AA	71-47	Presque Isle	1705	10.43	2.62	58.7
26A	71-47	Presque Isle	100	0.61	2.62	3.4
2NS	44-051	Krake Willis Rd	1100	6.65	2.65	37.9
Total Wt			2905	17.69		100.0

<----- Verify this number is 100%



Superior Materials, LLC
 30701 W. 10 Mile Rd.
 Suite 500
 Farmington Hills, MI 48336

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	98.6	100.0	100.0	99.2	0.8	0.8
3/4"	85.4	100.0	100.0	91.4	7.7	8.6
1/2"	47.6	96.3	100.0	69.1	22.3	30.9
3/8"	24.2	85.1	100.0	55.0	14.1	45.0
#4	4.4	21.7	95.5	39.5	15.5	60.5
#8	2.0	5.8	80.6	31.9	7.6	68.1
#16	1.6	2.8	65.4	25.8	6.1	74.2
#30	1.5	2.2	50.2	20.0	5.8	80.0
#50	1.4	2.0	24.3	10.1	9.9	89.9
#100	1.4	1.9	7.5	3.7	6.4	96.3
LBW	1.3	1.7	1.2	1.3	2.5	98.7


*Maximum % Retained must be above the 3/8" sieve.
 *Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation Batch Plant Gradations Aggregate Supplier Gradations

Adjusted WF Initial Production Sample (IPS)

Coarseness Factor:	66	Workability Factor:	32	Adjusted WF	34.4
---------------------------	-----------	----------------------------	-----------	--------------------	-------------

Coarseness Factor:	63
Workability Factor:	36

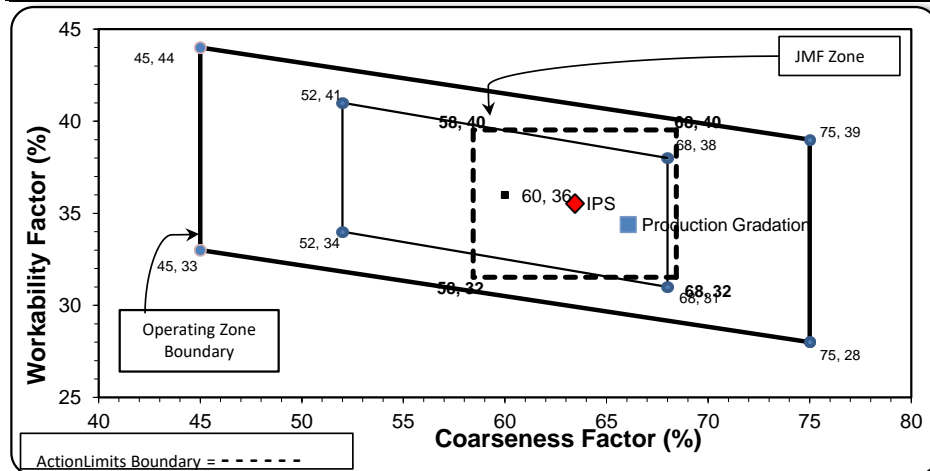

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	100.0	0.0	0.0
3/4"	89.7	10.3	10.3
1/2"	70.3	19.4	29.7
3/8"	59.1	11.2	40.9
#4	42.8	16.3	57.2
#8	35.5	7.3	64.5
#16	29.0	6.5	71.0
#30	21.2	7.7	78.8
#50	9.8	11.5	90.2
#100	3.7	6.1	96.3
LBW	1.2	2.5	98.8

PREPARED BY:
 SM, LLC Technical Service

Approved By:

Aggregate Optimization Chart

PLANT #: **P-02**

Sample Date: 6/29/20 Concrete Grade: DM
 Dates Test Represents: 6/30/2020 through 7/6/2020

Contractor: _____

MDOT No.: _____

Agg. Class	Pit #	Source	Weight (SSD)	ft ³	Specific Gravity	% Contribution
6AA	71-47	Presque Isle	1505	9.21	2.62	51.8
26A	71-47	Presque Isle	250	1.53	2.62	8.6
2NS	63-115	Ray Rd	1150	6.95	2.65	39.6
Total Wt			2905	17.69		100.0

<----- Verify this number is 100%



Superior Materials, LLC
 30701 W. 10 Mile Rd.
 Suite 500
 Farmington Hills, MI 48336

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	98.2	100.0	100.0	99.1	0.9	0.9
3/4"	79.1	100.0	100.0	89.2	9.9	10.8
1/2"	41.9	97.1	100.0	69.7	19.5	30.3
3/8"	23.1	87.3	100.0	59.1	10.6	40.9
#4	4.6	27.8	98.1	43.6	15.5	56.4
#8	2.3	9.5	80.5	33.9	9.7	66.1
#16	2.0	4.6	63.4	26.5	7.3	73.5
#30	1.8	3.2	47.8	20.1	6.4	79.9
#50	1.7	2.7	25.0	11.0	9.1	89.0
#100	1.6	2.3	5.5	3.2	7.8	96.8
LBW	1.2	1.6	0.8	1.1	2.1	98.9


*Maximum % Retained must be above the 3/8" sieve.
 *Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation Batch Plant Gradations Aggregate Supplier Gradations

Adjusted WF Initial Production Sample (IPS)

Coarseness Factor:	62	Workability Factor:	34	Adjusted WF	36.4
---------------------------	-----------	----------------------------	-----------	--------------------	-------------

Coarseness Factor:	63
Workability Factor:	35

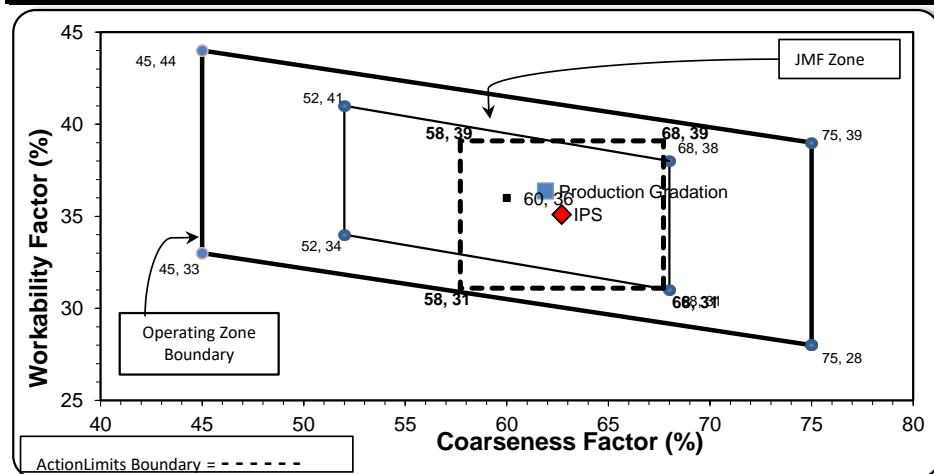

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	100.0	0.0	0.0
3/4"	95.1	4.9	4.9
1/2"	74.6	20.5	25.4
3/8"	59.3	15.3	40.7
#4	42.1	17.2	57.9
#8	35.1	7.1	64.9
#16	29.2	5.9	70.8
#30	21.9	7.3	78.1
#50	9.6	12.4	90.4
#100	2.4	7.2	97.6
LBW	0.9	1.5	99.1

PREPARED BY:
 SM, LLC Technical Service

Approved By:
