

# Aggregate Optimization Chart

## Production Gradation Report

**PLANT #:** **P-101**

Sample Date: 8/17/20

Concrete Grade: **DM**

Contractor: \_\_\_\_\_

Dates Test Represents: 8/18/2020 through 8/24/2020

MDOT No.: \_\_\_\_\_

Agg. Class	Pit #	Source	Weight (SSD)	ft <sup>3</sup>	Specific Gravity	% Contribution
6AA	71-47	Presque Isle	1460	8.93	2.62	50.2
26A	71-47	Presque Isle	300	1.83	2.62	10.3
2NS	75-051	Mid-Michigan	1150	6.93	2.66	39.5
<b>Total Wt</b>			<b>2910</b>	<b>17.69</b>		<b>100.0</b>

<----- Verify this number is 100%



**Superior Materials, LLC**  
 30701 W. 10 Mile Rd.  
 Suite 500  
 Farmington Hills, MI 48336

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	97.4	100.0	100.0	98.7	1.3	1.3
3/4"	80.2	100.0	100.0	90.1	8.6	9.9
1/2"	38.4	96.6	100.0	68.7	21.3	31.3
3/8"	21.6	88.1	100.0	59.4	9.3	40.6
#4	3.6	26.3	98.2	43.3	16.1	56.7
#8	1.8	7.2	80.9	33.6	9.7	66.4
#16	1.4	3.2	64.0	26.3	7.3	73.7
#30	1.4	2.4	47.8	19.8	6.5	80.2
#50	1.3	2.3	24.3	10.5	9.3	89.5
#100	1.2	2.2	5.8	3.1	7.4	96.9
LBW	1.1	2.1	0.8	1.1	2.0	98.9


\*Maximum % Retained must be above the 3/8" sieve.  
 \*Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation  Batch Plant Gradations  Aggregate Supplier Gradations

Adjusted WF Initial Production Sample (IPS)

<b>Coarseness Factor:</b>	<b>61</b>	<b>Workability Factor:</b>	<b>34</b>	<b>Adjusted WF</b>	<b>36.1</b>
---------------------------	-----------	----------------------------	-----------	--------------------	-------------

<b>Coarseness Factor:</b>	<b>62</b>
<b>Workability Factor:</b>	<b>35</b>

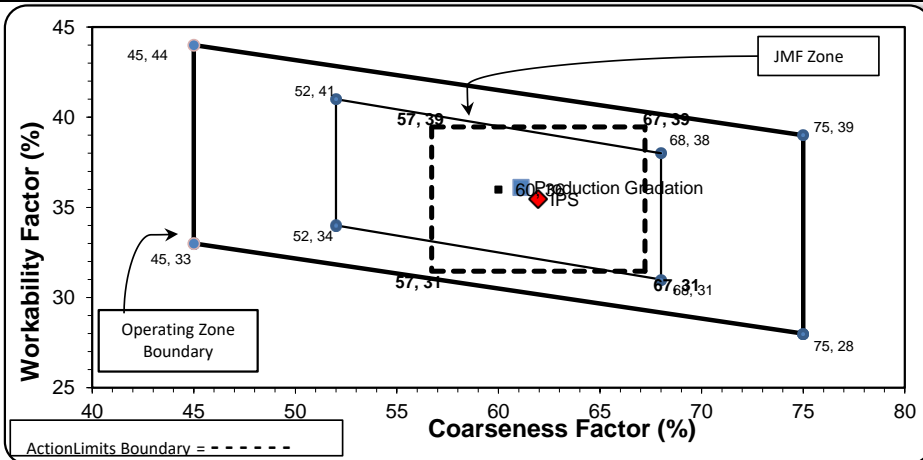

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	100.0	0.0	0.0
3/4"	95.0	5.0	5.0
1/2"	70.5	24.5	29.5
3/8"	60.0	10.5	40.0
#4	44.4	15.6	55.6
#8	35.5	9.0	64.5
#16	28.5	7.0	71.5
#30	21.5	7.0	78.5
#50	10.2	11.3	89.8
#100	3.1	7.1	96.9
LBW	1.3	1.8	98.7

PREPARED BY:  
 SM, LLC Technical Service

Approved By:

# Aggregate Optimization Chart

**PLANT #:** **P-102**

Sample Date: 8/17/20

Concrete Grade: **DM**

Contractor: \_\_\_\_\_

Dates Test Represents: 8/18/2020 through 8/24/2020

MDOT No.: \_\_\_\_\_

Agg. Class	Pit #	Source	Weight (SSD)	ft <sup>3</sup>	Specific Gravity	% Contribution
6AA	58-003	Stoneco	1500	8.94	2.69	50.8
26A	58-003	Stoneco	305	1.82	2.69	10.3
2NS	63-114	Highland	1150	6.95	2.65	38.9
<b>Total Wt</b>			<b>2955</b>	<b>17.71</b>		<b>100.0</b>

<----- Verify this number is 100%



**Superior Materials, LLC**  
 30701 W. 10 Mile Rd.  
 Suite 500  
 Farmington Hills, MI 48336

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	100.0	100.0	100.0	100.0	0.0	0.0
3/4"	84.8	100.0	100.0	92.3	7.7	7.7
1/2"	45.8	99.7	100.0	72.5	19.8	27.5
3/8"	23.8	89.3	100.0	60.2	12.2	39.8
#4	5.8	21.1	99.3	43.8	16.4	56.2
#8	2.2	3.3	83.6	34.0	9.8	66.0
#16	1.7	1.3	65.0	26.3	7.7	73.7
#30	1.5	1.1	47.2	19.2	7.0	80.8
#50	1.3	1.1	21.9	9.3	9.9	90.7
#100	1.2	0.9	5.3	2.8	6.5	97.2
LBW	1.0	0.7	0.5	0.8	2.0	99.2


\*Maximum % Retained must be above the 3/8" sieve.  
 \*Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation  Batch Plant Gradations  Aggregate Supplier Gradations

Adjusted WF Initial Production Sample (IPS)

<b>Coarseness Factor:</b>	<b>60</b>	<b>Workability Factor:</b>	<b>34</b>	<b>36.5</b>
---------------------------	-----------	----------------------------	-----------	-------------

<b>Coarseness Factor:</b>	<b>61</b>
<b>Workability Factor:</b>	<b>36</b>

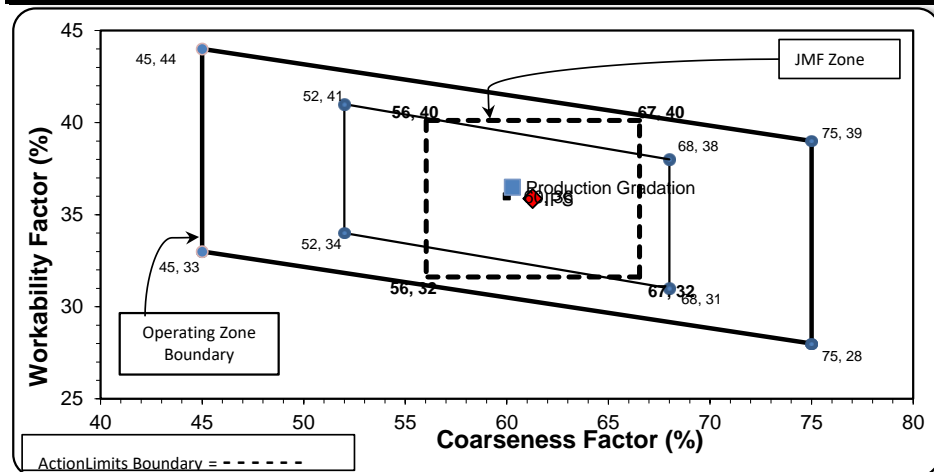

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	99.3	0.7	0.7
3/4"	89.2	10.1	10.8
1/2"	70.7	18.5	29.3
3/8"	60.7	10.0	39.3
#4	44.4	16.3	55.6
#8	35.9	8.5	64.1
#16	27.3	8.6	72.7
#30	19.1	8.2	80.9
#50	7.4	11.7	92.6
#100	1.9	5.6	98.1
LBW	0.7	1.2	99.3

PREPARED BY:  
 SM, LLC Technical Service

Approved By:

# Aggregate Optimization Chart

**PLANT #:** **P-103**

Sample Date: 8/17/20

Concrete Grade: **DM**

Contractor: \_\_\_\_\_

Dates Test Represents: 8/18/2020 through 8/24/2020

MDOT No.: \_\_\_\_\_

Agg. Class	Pit #	Source	Weight (SSD)	ft <sup>3</sup>	Specific Gravity	% Contribution
6AA	58-003	Stoneco	1500	8.94	2.69	50.8
26A	58-003	Stoneco	305	1.82	2.69	10.3
2NS	63-114	Highland	1150	6.95	2.65	38.9
<b>Total Wt</b>			<b>2955</b>	<b>17.71</b>		<b>100.0</b>

<----- Verify this number is 100%



**Superior Materials, LLC**  
 30701 W. 10 Mile Rd.  
 Suite 500  
 Farmington Hills, MI 48336

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	100.0	100.0	100.0	100.0	0.0	0.0
3/4"	84.8	100.0	100.0	92.3	7.7	7.7
1/2"	45.8	99.7	100.0	72.5	19.8	27.5
3/8"	23.8	89.3	100.0	60.2	12.2	39.8
#4	5.8	21.1	99.3	43.8	16.4	56.2
#8	2.2	3.3	83.6	34.0	9.8	66.0
#16	1.7	1.3	65.0	26.3	7.7	73.7
#30	1.5	1.1	47.2	19.2	7.0	80.8
#50	1.3	1.1	21.9	9.3	9.9	90.7
#100	1.2	0.9	5.3	2.8	6.5	97.2
LBW	1.0	0.7	0.5	0.8	2.0	99.2


\*Maximum % Retained must be above the 3/8" sieve.  
 \*Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation  Batch Plant Gradations  Aggregate Supplier Gradations

Adjusted WF Initial Production Sample (IPS)

<b>Coarseness Factor:</b>	<b>60</b>	<b>Workability Factor:</b>	<b>34</b>	<b>36.5</b>
---------------------------	-----------	----------------------------	-----------	-------------

<b>Coarseness Factor:</b>	<b>61</b>
<b>Workability Factor:</b>	<b>36</b>

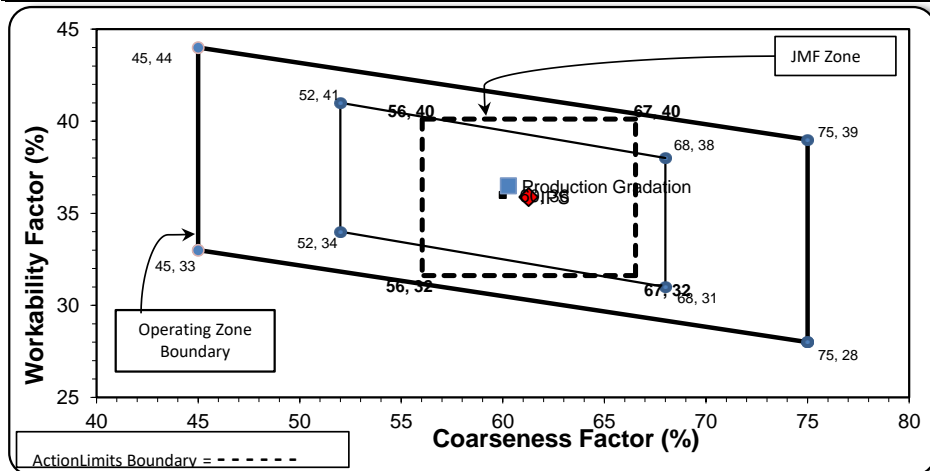

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	99.3	0.7	0.7
3/4"	89.2	10.1	10.8
1/2"	70.7	18.5	29.3
3/8"	60.7	10.0	39.3
#4	44.4	16.3	55.6
#8	35.9	8.5	64.1
#16	27.3	8.6	72.7
#30	19.1	8.2	80.9
#50	7.4	11.7	92.6
#100	1.9	5.6	98.1
LBW	0.7	1.2	99.3

PREPARED BY:  
 SM, LLC Technical Service

Approved BY:

# Aggregate Optimization Chart

**PLANT #:** **P-12**

Sample Date: 8/17/20

Concrete Grade: **DM**

Contractor: \_\_\_\_\_

Dates Test Represents: 8/18/2020 through 8/24/2020

MDOT No.: \_\_\_\_\_

Agg. Class	Pit #	Source	Weight (SSD)	ft <sup>3</sup>	Specific Gravity	% Contribution
6AA	71-47	Presque Isle	1505	9.21	2.62	51.8
26A	71-47	Presque Isle	250	1.53	2.62	8.6
2NS	63-115	Ray Rd	1150	6.95	2.65	39.6
<b>Total Wt</b>			<b>2905</b>	<b>17.69</b>		<b>100.0</b>

<----- Verify this number is 100%



**Superior Materials, LLC**  
 30701 W. 10 Mile Rd.  
 Suite 500  
 Farmington Hills, MI 48336

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	98.3	100.0	100.0	99.1	0.9	0.9
3/4"	74.8	100.0	100.0	86.9	12.2	13.1
1/2"	31.0	96.7	100.0	64.0	23.0	36.0
3/8"	15.6	86.8	100.0	55.1	8.8	44.9
#4	3.4	26.2	97.6	42.7	12.5	57.3
#8	2.2	8.2	79.2	33.2	9.5	66.8
#16	2.0	4.4	62.0	26.0	7.2	74.0
#30	1.9	3.7	46.9	19.9	6.1	80.1
#50	1.8	3.4	25.2	11.2	8.7	88.8
#100	1.7	3.2	5.3	3.3	7.9	96.7
LBW	1.2	2.6	0.7	1.1	2.1	98.9


\*Maximum % Retained must be above the 3/8" sieve.  
 \*Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation  Batch Plant Gradations  Aggregate Supplier Gradations

Adjusted WF Initial Production Sample (IPS)

Coarseness Factor:	<b>67</b>	Workability Factor:	<b>33</b>	Adjusted WF	<b>35.7</b>
--------------------	-----------	---------------------	-----------	-------------	-------------

Coarseness Factor:	<b>63</b>
Workability Factor:	<b>36</b>

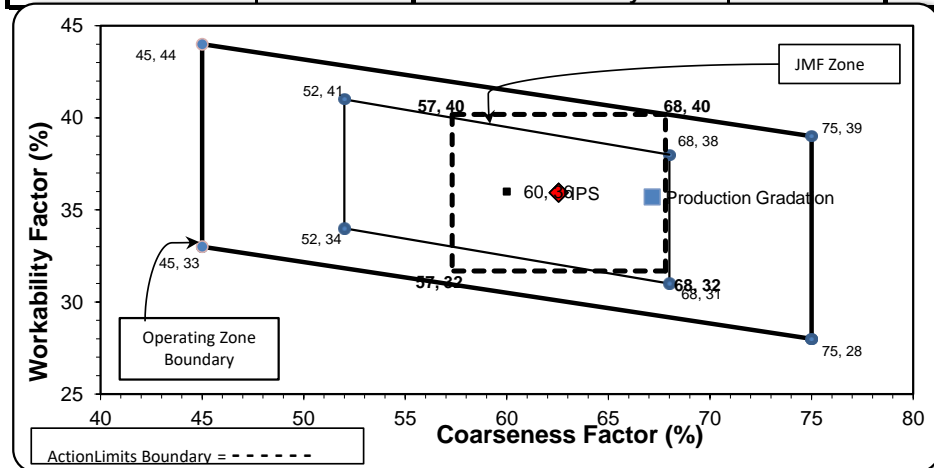

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	99.3	0.7	0.7
3/4"	89.0	10.3	11.0
1/2"	70.3	18.7	29.7
3/8"	59.9	10.4	40.1
#4	41.9	18.0	58.1
#8	35.9	6.0	64.1
#16	27.8	8.2	72.2
#30	18.9	8.8	81.1
#50	6.3	12.6	93.7
#100	1.7	4.6	98.3
LBW	1.0	0.7	99.0

PREPARED BY:  
 SM, LLC Technical Service

Approved By:

# Aggregate Optimization Chart

**PLANT #:** **P-20**

Sample Date: 8/17/20 Concrete Grade: DM  
 Dates Test Represents: 8/18/2020 through 8/24/2020

Contractor: \_\_\_\_\_

MDOT No.: \_\_\_\_\_

Agg. Class	Pit #	Source	Weight (SSD)	ft <sup>3</sup>	Specific Gravity	% Contribution
6AA	71-47	Presque Isle	1605	9.82	2.62	55.2
26A	71-47	Presque Isle	200	1.22	2.62	6.9
2NS	63-92	Grange Hall	1100	6.65	2.65	37.9
<b>Total Wt</b>			<b>2905</b>	<b>17.69</b>		<b>100.0</b>

<----- Verify this number is 100%



**Superior Materials, LLC**  
 30701 W. 10 Mile Rd.  
 Suite 500  
 Farmington Hills, MI 48336


Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	97.8	100.0	100.0	98.8	1.2	1.2
3/4"	81.3	100.0	100.0	89.7	9.1	10.3
1/2"	36.5	97.1	100.0	64.7	25.0	35.3
3/8"	20.9	92.0	100.0	55.7	9.0	44.3
#4	3.3	28.2	97.6	40.7	15.0	59.3
#8	2.0	7.5	85.2	33.9	6.8	66.1
#16	1.8	3.1	70.9	28.1	5.8	71.9
#30	1.8	2.2	49.2	19.8	8.3	80.2
#50	1.7	2.0	15.8	7.1	12.7	92.9
#100	1.6	1.8	1.6	1.6	5.4	98.4
LBW	1.5	1.6	0.2	1.0	0.6	99.0

\*Maximum % Retained must be above the 3/8" sieve.  
 \*Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation  Batch Plant Gradations  Aggregate Supplier Gradations  Adjusted WF Initial Production Sample (IPS)

<b>Coarseness Factor:</b>	<b>67</b>	<b>Workability Factor:</b>	<b>34</b>	<b>Adjusted WF</b>	<b>36.4</b>
---------------------------	-----------	----------------------------	-----------	--------------------	-------------

<b>Coarseness Factor:</b>	<b>63</b>
<b>Workability Factor:</b>	<b>36</b>

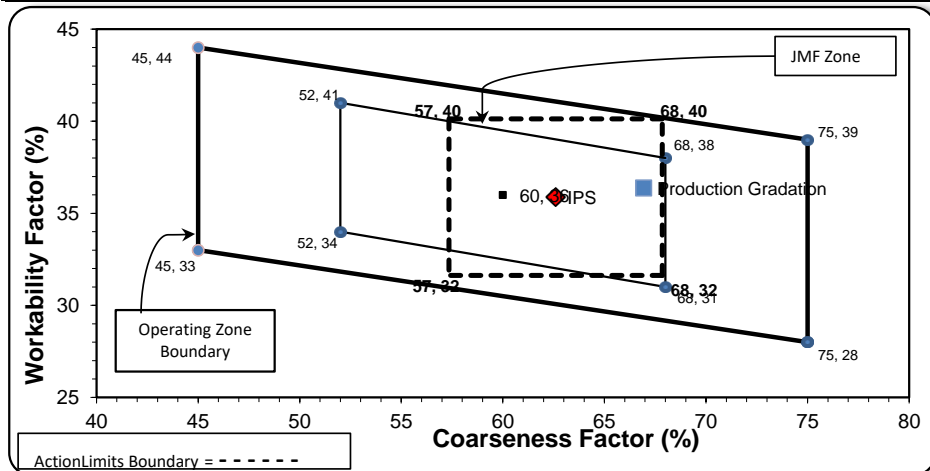

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	100.0	0.0	0.0
3/4"	89.2	10.8	10.8
1/2"	68.4	20.8	31.6
3/8"	59.9	8.6	40.1
#4	43.0	16.9	57.0
#8	35.9	7.1	64.1
#16	29.0	6.8	71.0
#30	21.3	7.7	78.7
#50	9.9	11.4	90.1
#100	2.4	7.5	97.6
LBW	1.2	1.2	98.8

PREPARED BY:  
 SM, LLC Technical Service

Approved By:

# Aggregate Optimization Chart

**PLANT #:** **P-32**

Sample Date: 8/17/20 Concrete Grade: DM  
 Dates Test Represents: 8/18/2020 through 8/24/2020

Contractor: \_\_\_\_\_

MDOT No.: \_\_\_\_\_

Agg. Class	Pit #	Source	Weight (SSD)	ft <sup>3</sup>	Specific Gravity	% Contribution
6AA	71-47	Presque Isle	1555	9.51	2.62	53.5
26A	71-47	Presque Isle	200	1.22	2.62	6.9
2NS	95-013	Smelter Bay	1150	6.95	2.65	39.6
<b>Total Wt</b>			<b>2905</b>	<b>17.69</b>		<b>100.0</b>

<----- Verify this number is 100%

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	98.8	100.0	100.0	99.4	0.6	0.6
3/4"	81.8	100.0	100.0	90.3	9.1	9.7
1/2"	39.9	96.7	100.0	67.6	22.7	32.4
3/8"	22.1	86.8	100.0	57.4	10.2	42.6
#4	4.2	26.2	96.7	42.3	15.1	57.7
#8	2.4	8.2	83.1	34.7	7.6	65.3
#16	2.1	4.4	67.2	28.0	6.7	72.0
#30	2.0	3.7	45.7	19.4	8.6	80.6
#50	2.0	3.4	21.3	9.7	9.7	90.3
#100	1.9	3.2	5.4	3.4	6.4	96.6
LBW	1.6	2.6	0.8	1.4	2.0	98.6




**Superior Materials, LLC**  
 30701 W. 10 Mile Rd.  
 Suite 500  
 Farmington Hills, MI 48336

\*Maximum % Retained must be above the 3/8" sieve.  
 \*Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation  Batch Plant Gradations  Aggregate Supplier Gradations  Adjusted WF Initial Production Sample (IPS)

<b>Coarseness Factor:</b>	<b>65</b>	<b>Workability Factor:</b>	<b>35</b>	<b>Adjusted WF</b>	<b>37.2</b>
---------------------------	-----------	----------------------------	-----------	--------------------	-------------

<b>Coarseness Factor:</b>	<b>62</b>
<b>Workability Factor:</b>	<b>36</b>

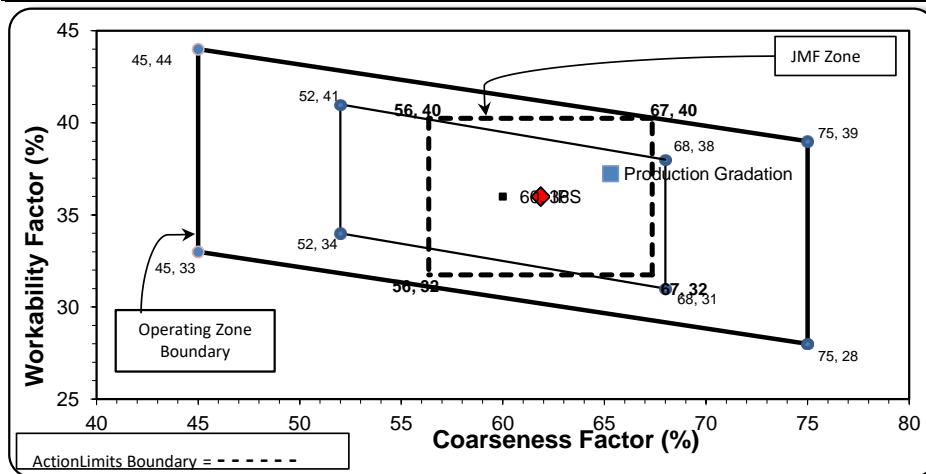

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	100.0	0.0	0.0
3/4"	95.0	5.0	5.0
1/2"	72.3	22.8	27.7
3/8"	60.4	11.8	39.6
#4	42.6	17.8	57.4
#8	36.0	6.6	64.0
#16	29.5	6.5	70.5
#30	20.3	9.2	79.7
#50	9.5	10.8	90.5
#100	3.4	6.1	96.6
LBW	1.3	2.1	98.7

PREPARED BY:  
 SM, LLC Technical Service

Approved By:

# Aggregate Optimization Chart

**PLANT #:** **P-35**

Sample Date: 8/17/20 Concrete Grade: **DM**  
 Dates Test Represents: 8/18/2020 through 8/24/2020

Contractor: \_\_\_\_\_

MDOT No.: \_\_\_\_\_

Agg. Class	Pit #	Source	Weight (SSD)	ft <sup>3</sup>	Specific Gravity	% Contribution
6AA	58-003	Stoneco	1500	8.94	2.69	50.8
26A	58-003	Stoneco	355	2.11	2.69	12.0
2NS	81-093	Burmeister	1100	6.65	2.65	37.2
<b>Total Wt</b>			<b>2955</b>	<b>17.70</b>		<b>100.0</b>

<----- Verify this number is 100%



**Superior Materials, LLC**  
 30701 W. 10 Mile Rd.  
 Suite 500  
 Farmington Hills, MI 48336

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	100.0	100.0	100.0	100.0	0.0	0.0
3/4"	84.8	100.0	100.0	92.3	7.7	7.7
1/2"	45.8	99.7	100.0	72.5	19.8	27.5
3/8"	23.8	89.3	100.0	60.0	12.4	40.0
#4	5.8	21.1	97.3	41.7	18.3	58.3
#8	2.2	3.3	88.6	34.5	7.2	65.5
#16	1.7	1.3	62.8	24.4	10.1	75.6
#30	1.5	1.1	44.1	17.3	7.1	82.7
#50	1.3	1.1	20.0	8.2	9.1	91.8
#100	1.2	0.9	5.2	2.7	5.6	97.3
LBW	1.0	0.7	1.3	1.1	1.6	98.9


\*Maximum % Retained must be above the 3/8" sieve.  
 \*Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation  Batch Plant Gradations  Aggregate Supplier Gradations

Adjusted WF Initial Production Sample (IPS)

<b>Coarseness Factor:</b>	<b>61</b>	<b>Workability Factor:</b>	<b>34</b>	<b>37.0</b>
---------------------------	-----------	----------------------------	-----------	-------------

<b>Coarseness Factor:</b>	<b>61</b>
<b>Workability Factor:</b>	<b>36</b>

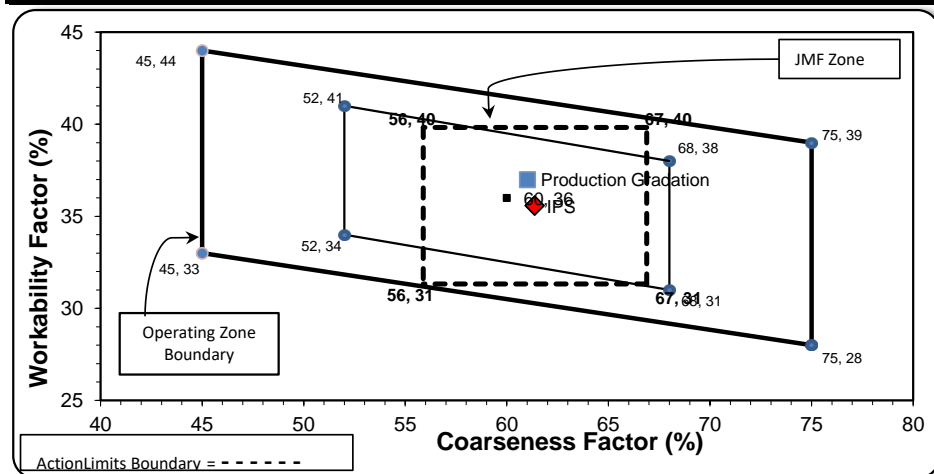

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	99.3	0.7	0.7
3/4"	89.1	10.2	10.9
1/2"	70.5	18.6	29.5
3/8"	60.5	10.0	39.5
#4	44.1	16.4	55.9
#8	35.6	8.5	64.4
#16	27.7	7.9	72.3
#30	20.6	7.1	79.4
#50	8.7	11.8	91.3
#100	1.6	7.1	98.4
LBW	1.1	0.6	98.9

PREPARED BY:  
 SM, LLC Technical Service

Approved By:

# Aggregate Optimization Chart

**PLANT #:** **P-36**

Sample Date: 8/17/20 Concrete Grade: DM  
 Dates Test Represents: 8/18/2020 through 8/24/2020

Contractor: \_\_\_\_\_

MDOT No.: \_\_\_\_\_



**Superior Materials, LLC**  
 30701 W. 10 Mile Rd.  
 Suite 500  
 Farmington Hills, MI 48336

Agg. Class	Pit #	Source	Weight (SSD)	ft <sup>3</sup>	Specific Gravity	% Contribution
6AA	71-47	Presque Isle	1455	8.90	2.62	50.1
26A	71-47	Presque Isle	350	2.14	2.62	12.0
2NS	63-92	Grange Hall	1100	6.65	2.65	37.9
<b>Total Wt</b>			<b>2905</b>	<b>17.69</b>		<b>100.0</b>

<----- Verify this number is 100%


Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	98.3	100.0	100.0	99.1	0.9	0.9
3/4"	74.8	100.0	100.0	87.4	11.8	12.6
1/2"	31.0	96.7	100.0	65.0	22.3	35.0
3/8"	15.6	86.8	100.0	56.1	8.9	43.9
#4	3.4	26.2	97.6	41.8	14.3	58.2
#8	2.2	8.2	85.2	34.4	7.5	65.6
#16	2.0	4.4	70.9	28.4	6.0	71.6
#30	1.9	3.7	49.2	20.0	8.4	80.0
#50	1.8	3.4	15.8	7.3	12.7	92.7
#100	1.7	3.2	1.6	1.8	5.5	98.2
LBW	1.2	2.6	0.2	1.0	0.9	99.0

\*Maximum % Retained must be above the 3/8" sieve.  
 \*Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation  Batch Plant Gradations  Aggregate Supplier Gradations  Adjusted WF Initial Production Sample (IPS)

<b>Coarseness Factor:</b>	<b>67</b>	<b>Workability Factor:</b>	<b>34</b>	<b>Adjusted WF</b>	<b>36.9</b>
---------------------------	-----------	----------------------------	-----------	--------------------	-------------

<b>Coarseness Factor:</b>	<b>63</b>
<b>Workability Factor:</b>	<b>35</b>

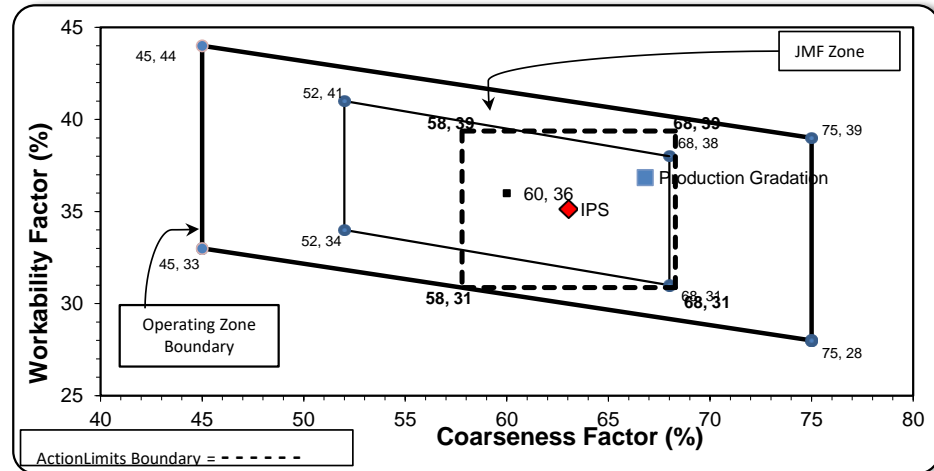

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	99.1	0.9	0.9
3/4"	90.3	8.8	9.7
1/2"	69.2	21.1	30.8
3/8"	59.1	10.1	40.9
#4	41.8	17.3	58.2
#8	35.1	6.6	64.9
#16	28.5	6.6	71.5
#30	21.2	7.3	78.8
#50	8.7	12.5	91.3
#100	1.8	7.0	98.2
LBW	0.7	1.0	99.3

PREPARED BY:  
 SM, LLC Technical Service

Approved By:



# Aggregate Optimization Chart

**PLANT #:** **P-39**

Sample Date: 8/17/20 Concrete Grade: **DM**

Dates Test Represents: 8/18/2020 through 8/24/2020

Contractor: \_\_\_\_\_

MDOT No.: \_\_\_\_\_

Agg. Class	Pit #	Source	Weight (SSD)	ft <sup>3</sup>	Specific Gravity	% Contribution
6AA	71-47	Presque Isle	1505	9.21	2.62	51.8
26A	71-47	Presque Isle	250	1.53	2.62	8.6
2NS	44-051	Krake Willis Rd	1150	6.95	2.65	39.6
<b>Total Wt</b>			<b>2905</b>	<b>17.69</b>		<b>100.0</b>

<----- Verify this number is 100%



**Superior Materials, LLC**  
 30701 W. 10 Mile Rd.  
 Suite 500  
 Farmington Hills, MI 48336

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	97.4	100.0	100.0	98.7	1.3	1.3
3/4"	80.2	100.0	100.0	89.7	8.9	10.3
1/2"	38.4	96.6	100.0	67.8	21.9	32.2
3/8"	21.6	88.1	100.0	58.4	9.4	41.6
#4	3.6	26.3	95.8	42.1	16.3	57.9
#8	1.8	7.2	80.7	33.5	8.6	66.5
#16	1.4	3.2	66.3	27.2	6.3	72.8
#30	1.4	2.4	51.2	21.2	6.0	78.8
#50	1.3	2.3	25.8	11.1	10.1	88.9
#100	1.2	2.2	7.1	3.6	7.5	96.4
LBW	1.1	2.1	1.2	1.2	2.4	98.8


\*Maximum % Retained must be above the 3/8" sieve.  
 \*Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation  Batch Plant Gradations  Aggregate Supplier Gradations

Adjusted WF Initial Production Sample (IPS)

<b>Coarseness Factor:</b>	<b>63</b>	<b>Workability Factor:</b>	<b>33</b>	<b>Adjusted WF</b>	<b>36.0</b>
---------------------------	-----------	----------------------------	-----------	--------------------	-------------

<b>Coarseness Factor:</b>	<b>63</b>
<b>Workability Factor:</b>	<b>36</b>

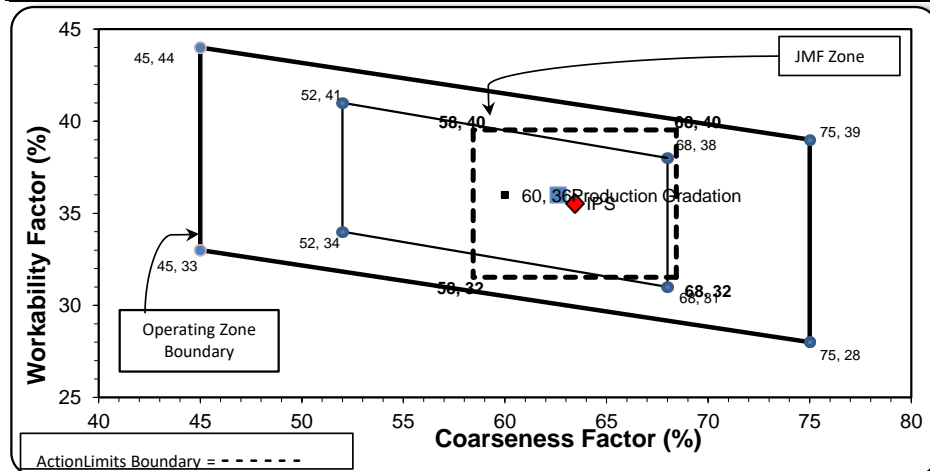

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	100.0	0.0	0.0
3/4"	89.7	10.3	10.3
1/2"	70.3	19.4	29.7
3/8"	59.1	11.2	40.9
#4	42.8	16.3	57.2
#8	35.5	7.3	64.5
#16	29.0	6.5	71.0
#30	21.2	7.7	78.8
#50	9.8	11.5	90.2
#100	3.7	6.1	96.3
LBW	1.2	2.5	98.8

PREPARED BY:  
 SM, LLC Technical Service

Approved By:

# Aggregate Optimization Chart

**PLANT #:** **P-02**

Sample Date: 8/17/20 Concrete Grade: **DM**  
 Dates Test Represents: 8/18/2020 through 8/24/2020

Contractor: \_\_\_\_\_

MDOT No.: \_\_\_\_\_

Agg. Class	Pit #	Source	Weight (SSD)	ft <sup>3</sup>	Specific Gravity	% Contribution
6AA	71-47	Presque Isle	1505	9.21	2.62	51.8
26A	71-47	Presque Isle	250	1.53	2.62	8.6
2NS	63-115	Ray Rd	1150	6.95	2.65	39.6
<b>Total Wt</b>			<b>2905</b>	<b>17.69</b>		<b>100.0</b>

<----- Verify this number is 100%



**Superior Materials, LLC**  
 30701 W. 10 Mile Rd.  
 Suite 500  
 Farmington Hills, MI 48336


Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	98.3	100.0	100.0	99.1	0.9	0.9
3/4"	74.8	100.0	100.0	86.9	12.2	13.1
1/2"	31.0	96.7	100.0	64.0	23.0	36.0
3/8"	15.6	86.8	100.0	55.1	8.8	44.9
#4	3.4	26.2	97.6	42.7	12.5	57.3
#8	2.2	8.2	79.2	33.2	9.5	66.8
#16	2.0	4.4	62.0	26.0	7.2	74.0
#30	1.9	3.7	46.9	19.9	6.1	80.1
#50	1.8	3.4	25.2	11.2	8.7	88.8
#100	1.7	3.2	5.3	3.3	7.9	96.7
LBW	1.2	2.6	0.7	1.1	2.1	98.9

\*Maximum % Retained must be above the 3/8" sieve.  
 \*Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation  Batch Plant Gradations  Aggregate Supplier Gradations  Adjusted WF Initial Production Sample (IPS)

<b>Coarseness Factor:</b>	<b>67</b>	<b>Workability Factor:</b>	<b>33</b>	<b>Adjusted WF</b>	<b>35.7</b>
---------------------------	-----------	----------------------------	-----------	--------------------	-------------

<b>Coarseness Factor:</b>	<b>63</b>
<b>Workability Factor:</b>	<b>35</b>

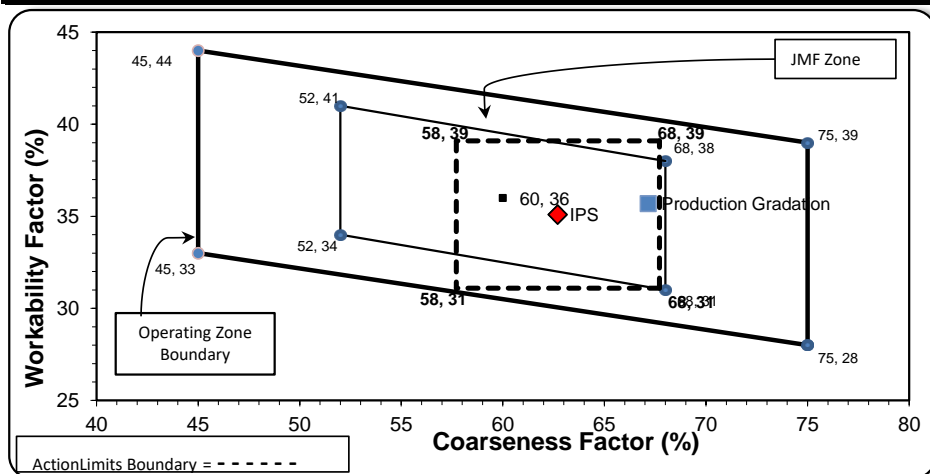

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	100.0	0.0	0.0
3/4"	95.1	4.9	4.9
1/2"	74.6	20.5	25.4
3/8"	59.3	15.3	40.7
#4	42.1	17.2	57.9
#8	35.1	7.1	64.9
#16	29.2	5.9	70.8
#30	21.9	7.3	78.1
#50	9.6	12.4	90.4
#100	2.4	7.2	97.6
LBW	0.9	1.5	99.1

PREPARED BY:  
 SM, LLC Technical Service

Approved By:
