

Aggregate Optimization Chart

Production Gradation Report

PLANT #: **P-101**

Sample Date: **8/31/20**

Concrete Grade: **DM**

Contractor: _____

Dates Test Represents: **9/1/2020** through **9/7/2020**

MDOT No.: _____

Agg. Class	Pit #	Source	Weight (SSD)	ft ³	Specific Gravity	% Contribution
6AA	71-47	Presque Isle	1610	9.85	2.62	55.3
26A	71-47	Presque Isle	150	0.92	2.62	5.2
2NS	75-051	Mid-Michigan	1150	6.93	2.66	39.5
Total Wt			2910	17.69		100.0

<----- Verify this number is 100%



Superior Materials, LLC
 30701 W. 10 Mile Rd.
 Suite 500
 Farmington Hills, MI 48336

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	95.8	100.0	100.0	97.7	2.3	2.3
3/4"	77.9	100.0	100.0	87.8	9.9	12.2
1/2"	38.0	98.0	100.0	65.6	22.2	34.4
3/8"	20.9	86.7	100.0	55.6	10.0	44.4
#4	2.9	18.0	98.0	41.3	14.3	58.7
#8	1.5	4.2	77.2	31.6	9.7	68.4
#16	1.3	2.2	58.9	24.1	7.4	75.9
#30	1.3	1.8	43.8	18.1	6.0	81.9
#50	1.2	1.7	22.3	9.6	8.6	90.4
#100	1.2	1.6	5.4	2.9	6.7	97.1
LBW	1.1	1.4	0.8	1.0	1.9	99.0


*Maximum % Retained must be above the 3/8" sieve.
 *Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation Batch Plant Gradations Aggregate Supplier Gradations

Adjusted WF Initial Production Sample (IPS)

Coarseness Factor:	65	Workability Factor:	32	34.1
---------------------------	-----------	----------------------------	-----------	-------------

Coarseness Factor:	62
Workability Factor:	35

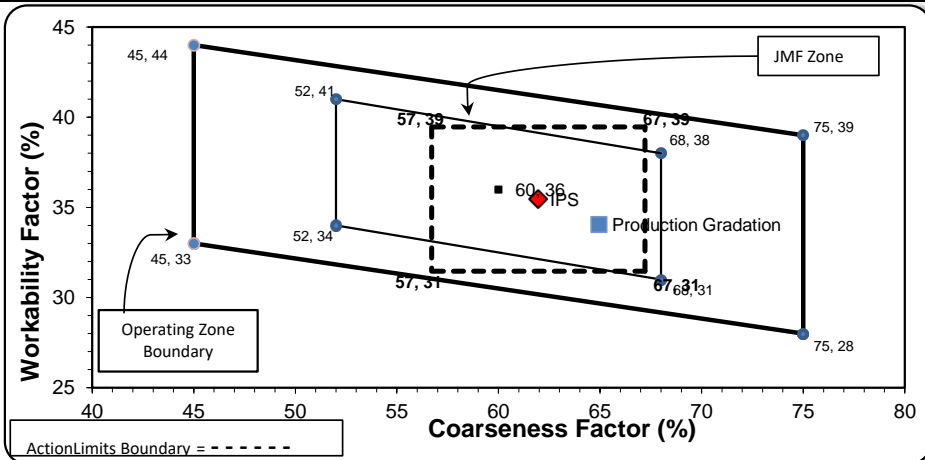

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	100.0	0.0	0.0
3/4"	95.0	5.0	5.0
1/2"	70.5	24.5	29.5
3/8"	60.0	10.5	40.0
#4	44.4	15.6	55.6
#8	35.5	9.0	64.5
#16	28.5	7.0	71.5
#30	21.5	7.0	78.5
#50	10.2	11.3	89.8
#100	3.1	7.1	96.9
LBW	1.3	1.8	98.7

PREPARED BY:
 SM, LLC Technical Service

Approved By:

Aggregate Optimization Chart

PLANT #: **P-102**

Sample Date: 8/31/20

Concrete Grade: **DM**

Contractor: _____

Dates Test Represents: 9/1/2020 through 9/7/2020

MDOT No.: _____

Agg. Class	Pit #	Source	Weight (SSD)	ft ³	Specific Gravity	% Contribution
6AA	58-003	Stoneco	1500	8.94	2.69	50.8
26A	58-003	Stoneco	305	1.82	2.69	10.3
2NS	63-114	Highland	1150	6.95	2.65	38.9
Total Wt			2955	17.71		100.0

<----- Verify this number is 100%



Superior Materials, LLC
 30701 W. 10 Mile Rd.
 Suite 500
 Farmington Hills, MI 48336

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	100.0	100.0	100.0	100.0	0.0	0.0
3/4"	85.3	100.0	100.0	92.5	7.5	7.5
1/2"	47.0	99.2	100.0	73.0	19.5	27.0
3/8"	25.0	76.9	100.0	59.5	13.5	40.5
#4	4.7	24.8	99.2	43.6	16.0	56.4
#8	1.8	6.0	83.4	34.0	9.6	66.0
#16	1.5	2.4	65.2	26.4	7.6	73.6
#30	1.3	1.7	48.0	19.5	6.9	80.5
#50	1.2	1.6	20.5	8.8	10.8	91.2
#100	1.1	1.5	4.0	2.3	6.5	97.7
LBW	0.8	0.9	0.3	0.6	1.7	99.4


*Maximum % Retained must be above the 3/8" sieve.
 *Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation Batch Plant Gradations Aggregate Supplier Gradations

Adjusted WF Initial Production Sample (IPS)

Coarseness Factor:	61	Workability Factor:	34	36.5
---------------------------	-----------	----------------------------	-----------	-------------

Coarseness Factor:	61
Workability Factor:	36

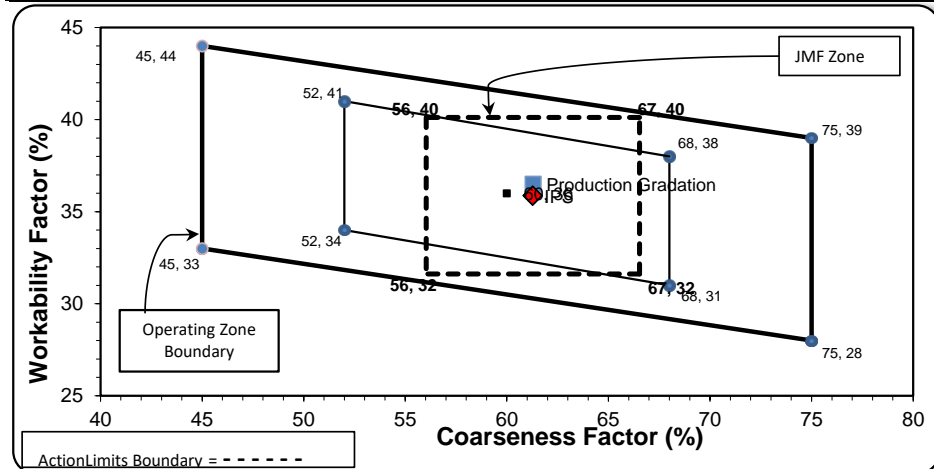

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	99.3	0.7	0.7
3/4"	89.2	10.1	10.8
1/2"	70.7	18.5	29.3
3/8"	60.7	10.0	39.3
#4	44.4	16.3	55.6
#8	35.9	8.5	64.1
#16	27.3	8.6	72.7
#30	19.1	8.2	80.9
#50	7.4	11.7	92.6
#100	1.9	5.6	98.1
LBW	0.7	1.2	99.3

PREPARED BY:
 SM, LLC Technical Service

Approved By:

Aggregate Optimization Chart

PLANT #: **P-103**

Sample Date: 8/31/20

Concrete Grade: **DM**

Contractor: _____

Dates Test Represents: 9/1/2020 through 9/7/2020

MDOT No.: _____

Agg. Class	Pit #	Source	Weight (SSD)	ft ³	Specific Gravity	% Contribution
6AA	58-003	Stoneco	1500	8.94	2.69	50.8
26A	58-003	Stoneco	305	1.82	2.69	10.3
2NS	63-114	Highland	1150	6.95	2.65	38.9
Total Wt			2955	17.71		100.0

<----- Verify this number is 100%



Superior Materials, LLC
 30701 W. 10 Mile Rd.
 Suite 500
 Farmington Hills, MI 48336

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	100.0	100.0	100.0	100.0	0.0	0.0
3/4"	85.3	100.0	100.0	92.5	7.5	7.5
1/2"	47.0	99.2	100.0	73.0	19.5	27.0
3/8"	25.0	76.9	100.0	59.5	13.5	40.5
#4	4.7	24.8	99.2	43.6	16.0	56.4
#8	1.8	6.0	83.4	34.0	9.6	66.0
#16	1.5	2.4	65.2	26.4	7.6	73.6
#30	1.3	1.7	48.0	19.5	6.9	80.5
#50	1.2	1.6	20.5	8.8	10.8	91.2
#100	1.1	1.5	4.0	2.3	6.5	97.7
LBW	0.8	0.9	0.3	0.6	1.7	99.4


*Maximum % Retained must be above the 3/8" sieve.
 *Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation Batch Plant Gradations Aggregate Supplier Gradations

Adjusted WF Initial Production Sample (IPS)

Coarseness Factor:	61	Workability Factor:	34	Adjusted WF	36.5
---------------------------	-----------	----------------------------	-----------	--------------------	-------------

Coarseness Factor:	61
Workability Factor:	36

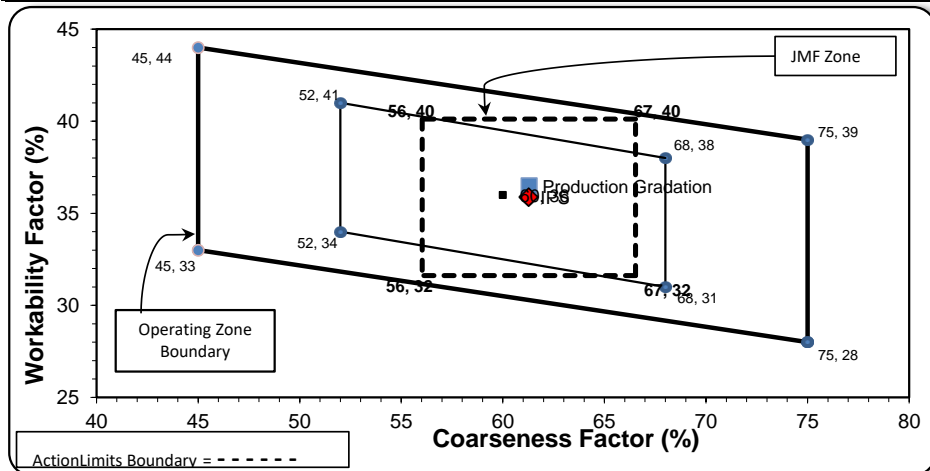

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	99.3	0.7	0.7
3/4"	89.2	10.1	10.8
1/2"	70.7	18.5	29.3
3/8"	60.7	10.0	39.3
#4	44.4	16.3	55.6
#8	35.9	8.5	64.1
#16	27.3	8.6	72.7
#30	19.1	8.2	80.9
#50	7.4	11.7	92.6
#100	1.9	5.6	98.1
LBW	0.7	1.2	99.3

PREPARED BY:
 SM, LLC Technical Service

Approved BY:

Aggregate Optimization Chart

PLANT #: **P-12**

Sample Date: 8/31/20

Concrete Grade: **DM**

Contractor: _____

Dates Test Represents: 9/1/2020 through 9/7/2020

MDOT No.: _____

Agg. Class	Pit #	Source	Weight (SSD)	ft ³	Specific Gravity	% Contribution
6AA	71-47	Presque Isle	1505	9.21	2.62	51.8
26A	71-47	Presque Isle	250	1.53	2.62	8.6
2NS	63-115	Ray Rd	1150	6.95	2.65	39.6
Total Wt			2905	17.69		100.0

<----- Verify this number is 100%



Superior Materials, LLC
 30701 W. 10 Mile Rd.
 Suite 500
 Farmington Hills, MI 48336

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	98.6	100.0	100.0	99.3	0.7	0.7
3/4"	85.7	100.0	100.0	92.6	6.7	7.4
1/2"	44.1	96.0	100.0	70.7	21.9	29.3
3/8"	26.4	80.7	100.0	60.2	10.5	39.8
#4	6.4	15.9	98.0	43.5	16.7	56.5
#8	2.9	5.0	80.9	34.0	9.5	66.0
#16	2.4	2.8	64.5	27.0	6.9	73.0
#30	2.3	2.4	48.6	20.6	6.4	79.4
#50	2.2	2.2	23.9	10.8	9.8	89.2
#100	2.1	2.1	4.2	2.9	7.9	97.1
LBW	1.8	1.8	0.3	1.2	1.7	98.8


*Maximum % Retained must be above the 3/8" sieve.
 *Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation Batch Plant Gradations Aggregate Supplier Gradations

Adjusted WF Initial Production Sample (IPS)

Coarseness Factor:	60	Workability Factor:	34	Adjusted WF	36.5
---------------------------	-----------	----------------------------	-----------	--------------------	-------------

Coarseness Factor:	63
Workability Factor:	36

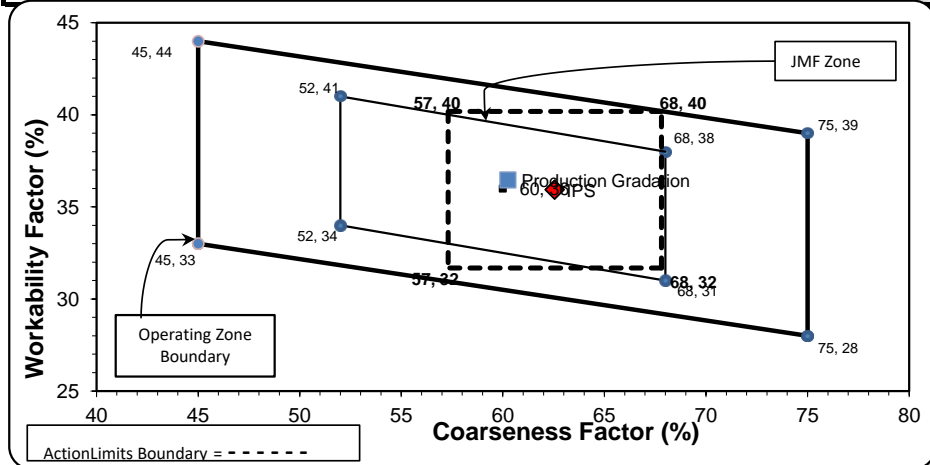

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	99.3	0.7	0.7
3/4"	89.0	10.3	11.0
1/2"	70.3	18.7	29.7
3/8"	59.9	10.4	40.1
#4	41.9	18.0	58.1
#8	35.9	6.0	64.1
#16	27.8	8.2	72.2
#30	18.9	8.8	81.1
#50	6.3	12.6	93.7
#100	1.7	4.6	98.3
LBW	1.0	0.7	99.0

PREPARED BY:
 SM, LLC Technical Service

Approved By:

Aggregate Optimization Chart

PLANT #: **P-20**

Sample Date: 8/31/20

Concrete Grade: **DM**

Contractor: _____

Dates Test Represents: 9/1/2020 through 9/7/2020

MDOT No.: _____

Agg. Class	Pit #	Source	Weight (SSD)	ft ³	Specific Gravity	% Contribution
6AA	71-47	Presque Isle	1605	9.82	2.62	55.2
26A	71-47	Presque Isle	200	1.22	2.62	6.9
2NS	63-92	Grange Hall	1100	6.65	2.65	37.9
Total Wt			2905	17.69		100.0

<----- Verify this number is 100%



Superior Materials, LLC
 30701 W. 10 Mile Rd.
 Suite 500
 Farmington Hills, MI 48336

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	98.6	100.0	100.0	99.2	0.8	0.8
3/4"	87.9	100.0	100.0	93.3	5.9	6.7
1/2"	47.4	98.4	100.0	70.8	22.5	29.2
3/8"	29.1	91.2	100.0	60.2	10.6	39.8
#4	4.7	26.6	97.2	41.2	19.0	58.8
#8	2.3	7.1	84.5	33.8	7.5	66.2
#16	2.0	3.0	69.8	27.7	6.0	72.3
#30	1.9	2.1	50.2	20.2	7.5	79.8
#50	1.9	1.9	19.3	8.5	11.7	91.5
#100	1.8	1.8	2.4	2.0	6.5	98.0
LBW	1.6	1.6	0.6	1.2	0.8	98.8


*Maximum % Retained must be above the 3/8" sieve.
 *Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation Batch Plant Gradations Aggregate Supplier Gradations

Adjusted WF Initial Production Sample (IPS)

Coarseness Factor:	60	Workability Factor:	34	Adjusted WF	36.3
---------------------------	-----------	----------------------------	-----------	--------------------	-------------

Coarseness Factor:	63
Workability Factor:	36

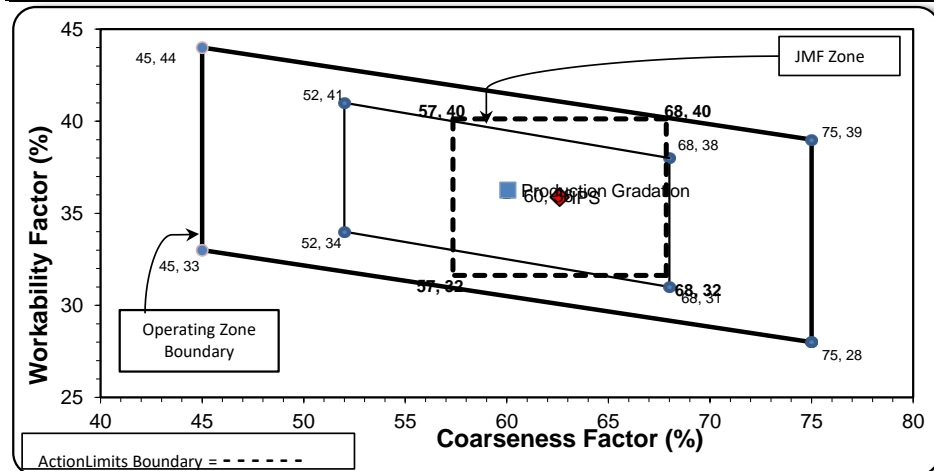

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	100.0	0.0	0.0
3/4"	89.2	10.8	10.8
1/2"	68.4	20.8	31.6
3/8"	59.9	8.6	40.1
#4	43.0	16.9	57.0
#8	35.9	7.1	64.1
#16	29.0	6.8	71.0
#30	21.3	7.7	78.7
#50	9.9	11.4	90.1
#100	2.4	7.5	97.6
LBW	1.2	1.2	98.8

PREPARED BY:
 SM, LLC Technical Service

Approved By:

Aggregate Optimization Chart

PLANT #: **P-32**

Sample Date: 8/31/20

Concrete Grade: **DM**

Contractor: _____

Dates Test Represents: 9/1/2020 through 9/7/2020

MDOT No.: _____

Agg. Class	Pit #	Source	Weight (SSD)	ft ³	Specific Gravity	% Contribution
6AA	71-47	Presque Isle	1555	9.51	2.62	53.5
26A	71-47	Presque Isle	200	1.22	2.62	6.9
2NS	95-013	Smelter Bay	1150	6.95	2.65	39.6
Total Wt			2905	17.69		100.0

<----- Verify this number is 100%



Superior Materials, LLC
 30701 W. 10 Mile Rd.
 Suite 500
 Farmington Hills, MI 48336

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	100.0	100.0	100.0	100.0	0.0	0.0
3/4"	82.1	100.0	100.0	90.4	9.6	9.6
1/2"	48.0	96.0	100.0	71.9	18.5	28.1
3/8"	30.1	80.7	100.0	61.3	10.6	38.7
#4	7.5	15.9	96.6	43.4	17.9	56.6
#8	3.7	5.0	82.7	35.1	8.3	64.9
#16	3.0	2.8	67.2	28.4	6.7	71.6
#30	2.9	2.4	46.7	20.2	8.2	79.8
#50	2.7	2.2	20.8	9.8	10.4	90.2
#100	2.5	2.1	5.7	3.7	6.1	96.3
LBW	1.7	1.8	1.0	1.4	2.3	98.6


*Maximum % Retained must be above the 3/8" sieve.
 *Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation Batch Plant Gradations Aggregate Supplier Gradations

Adjusted WF Initial Production Sample (IPS)

Coarseness Factor:	60	Workability Factor:	35	37.6
---------------------------	-----------	----------------------------	-----------	-------------

Coarseness Factor:	62
Workability Factor:	36

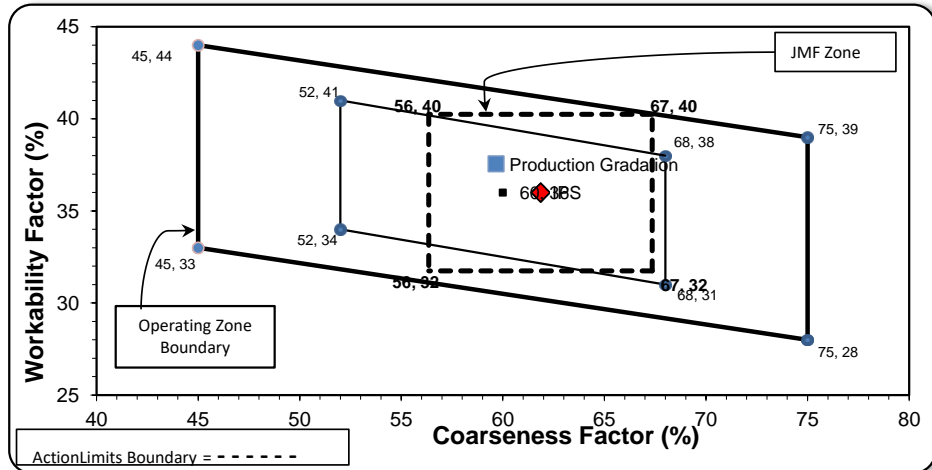

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	100.0	0.0	0.0
3/4"	95.0	5.0	5.0
1/2"	72.3	22.8	27.7
3/8"	60.4	11.8	39.6
#4	42.6	17.8	57.4
#8	36.0	6.6	64.0
#16	29.5	6.5	70.5
#30	20.3	9.2	79.7
#50	9.5	10.8	90.5
#100	3.4	6.1	96.6
LBW	1.3	2.1	98.7

PREPARED BY:
 SM, LLC Technical Service

Approved By:

Aggregate Optimization Chart

PLANT #: **P-35**

Sample Date: 8/31/20

Concrete Grade: **DM**

Contractor: _____

Dates Test Represents: 9/1/2020 through 9/7/2020

MDOT No.: _____

Agg. Class	Pit #	Source	Weight (SSD)	ft ³	Specific Gravity	% Contribution
6AA	58-003	Stoneco	1450	8.64	2.69	49.1
26A	58-003	Stoneco	405	2.41	2.69	13.7
2NS	81-093	Burmeister	1100	6.65	2.65	37.2
Total Wt			2955	17.70		100.0

<----- Verify this number is 100%



Superior Materials, LLC
 30701 W. 10 Mile Rd.
 Suite 500
 Farmington Hills, MI 48336

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	100.0	100.0	100.0	100.0	0.0	0.0
3/4"	85.3	100.0	100.0	92.8	7.2	7.2
1/2"	47.0	99.2	100.0	73.9	18.9	26.1
3/8"	25.0	76.9	100.0	60.0	13.9	40.0
#4	4.7	24.8	98.2	42.3	17.8	57.7
#8	1.8	6.0	90.8	35.5	6.8	64.5
#16	1.5	2.4	68.8	26.7	8.8	73.3
#30	1.3	1.7	49.0	19.1	7.6	80.9
#50	1.2	1.6	19.4	8.0	11.1	92.0
#100	1.1	1.5	3.9	2.2	5.8	97.8
LBW	0.8	0.9	1.2	1.0	1.2	99.0


*Maximum % Retained must be above the 3/8" sieve.
 *Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation Batch Plant Gradations Aggregate Supplier Gradations

Adjusted WF Initial Production Sample (IPS)

Coarseness Factor:	62	Workability Factor:	36	38.0	Coarseness Factor:	61
---------------------------	-----------	----------------------------	-----------	-------------	---------------------------	-----------

Workability Factor:	36
----------------------------	-----------

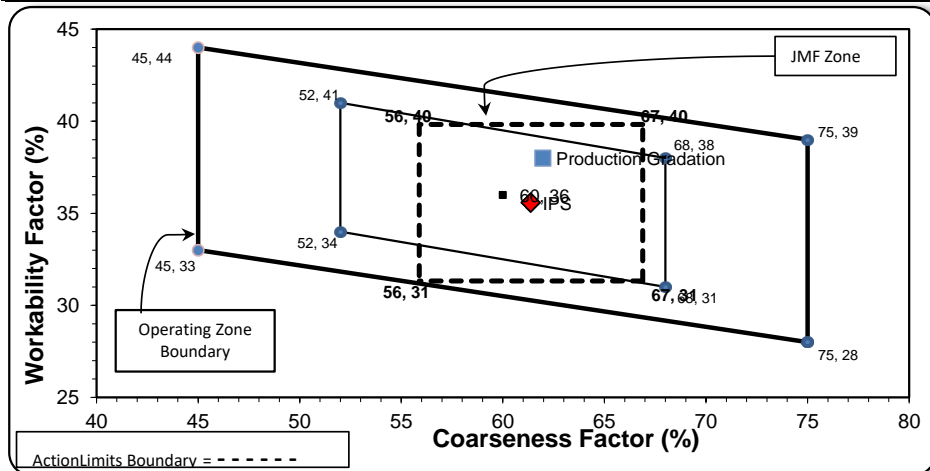

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	99.3	0.7	0.7
3/4"	89.1	10.2	10.9
1/2"	70.5	18.6	29.5
3/8"	60.5	10.0	39.5
#4	44.1	16.4	55.9
#8	35.6	8.5	64.4
#16	27.7	7.9	72.3
#30	20.6	7.1	79.4
#50	8.7	11.8	91.3
#100	1.6	7.1	98.4
LBW	1.1	0.6	98.9

PREPARED BY:
 SM, LLC Technical Service

Approved By:

Aggregate Optimization Chart

PLANT #: **P-36**

Sample Date: 8/31/20

Concrete Grade: **DM**

Contractor: _____

Dates Test Represents: 9/1/2020 through 9/7/2020

MDOT No.: _____

Agg. Class	Pit #	Source	Weight (SSD)	ft ³	Specific Gravity	% Contribution
6AA	71-47	Presque Isle	1455	8.90	2.62	50.1
26A	71-47	Presque Isle	350	2.14	2.62	12.0
2NS	63-92	Grange Hall	1100	6.65	2.65	37.9
Total Wt			2905	17.69		100.0

<----- Verify this number is 100%



Superior Materials, LLC
 30701 W. 10 Mile Rd.
 Suite 500
 Farmington Hills, MI 48336

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	98.6	100.0	100.0	99.3	0.7	0.7
3/4"	85.7	100.0	100.0	92.8	6.5	7.2
1/2"	44.1	96.0	100.0	71.5	21.3	28.5
3/8"	26.4	80.7	100.0	60.8	10.7	39.2
#4	6.4	15.9	97.2	41.9	18.9	58.1
#8	2.9	5.0	84.5	34.1	7.9	65.9
#16	2.4	2.8	69.8	28.0	6.1	72.0
#30	2.3	2.4	50.2	20.4	7.5	79.6
#50	2.2	2.2	19.3	8.7	11.8	91.3
#100	2.1	2.1	2.4	2.2	6.5	97.8
LBW	1.8	1.8	0.6	1.3	0.9	98.7


*Maximum % Retained must be above the 3/8" sieve.
 *Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation Batch Plant Gradations Aggregate Supplier Gradations

Adjusted WF Initial Production Sample (IPS)

Coarseness Factor:	59	Workability Factor:	34	Adjusted WF	36.6
---------------------------	-----------	----------------------------	-----------	--------------------	-------------

Coarseness Factor:	63
Workability Factor:	35

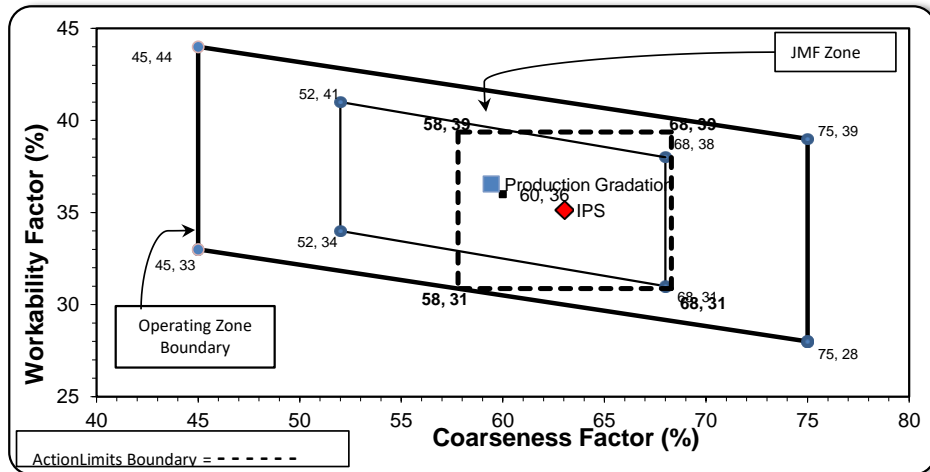

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	99.1	0.9	0.9
3/4"	90.3	8.8	9.7
1/2"	69.2	21.1	30.8
3/8"	59.1	10.1	40.9
#4	41.8	17.3	58.2
#8	35.1	6.6	64.9
#16	28.5	6.6	71.5
#30	21.2	7.3	78.8
#50	8.7	12.5	91.3
#100	1.8	7.0	98.2
LBW	0.7	1.0	99.3

PREPARED BY:
 SM, LLC Technical Service

Approved By:

Aggregate Optimization Chart

PLANT #: **P-39**

Sample Date: 8/31/20

Concrete Grade: **DM**

Contractor: _____

Dates Test Represents: 9/1/2020 through 9/7/2020

MDOT No.: _____

Agg. Class	Pit #	Source	Weight (SSD)	ft ³	Specific Gravity	% Contribution
6AA	71-47	Presque Isle	1605	9.82	2.62	55.2
26A	71-47	Presque Isle	150	0.92	2.62	5.2
2NS	44-051	Krake Willis Rd	1150	6.95	2.65	39.6
Total Wt			2905	17.69		100.0

<----- Verify this number is 100%



Superior Materials, LLC
 30701 W. 10 Mile Rd.
 Suite 500
 Farmington Hills, MI 48336

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	95.8	100.0	100.0	97.7	2.3	2.3
3/4"	77.9	100.0	100.0	87.8	9.9	12.2
1/2"	38.0	98.0	100.0	65.6	22.1	34.4
3/8"	20.9	86.7	100.0	55.6	10.0	44.4
#4	2.9	18.0	95.6	40.4	15.2	59.6
#8	1.5	4.2	80.5	32.9	7.5	67.1
#16	1.3	2.2	64.8	26.5	6.4	73.5
#30	1.3	1.8	48.9	20.2	6.3	79.8
#50	1.2	1.7	25.6	10.9	9.3	89.1
#100	1.2	1.6	8.0	3.9	7.0	96.1
LBW	1.1	1.4	1.1	1.1	2.8	98.9


*Maximum % Retained must be above the 3/8" sieve.
 *Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation Batch Plant Gradations Aggregate Supplier Gradations

Adjusted WF Initial Production Sample (IPS)

Coarseness Factor:	66	Workability Factor:	33	Adjusted WF	35.4
---------------------------	-----------	----------------------------	-----------	--------------------	-------------

Coarseness Factor:	63
Workability Factor:	36

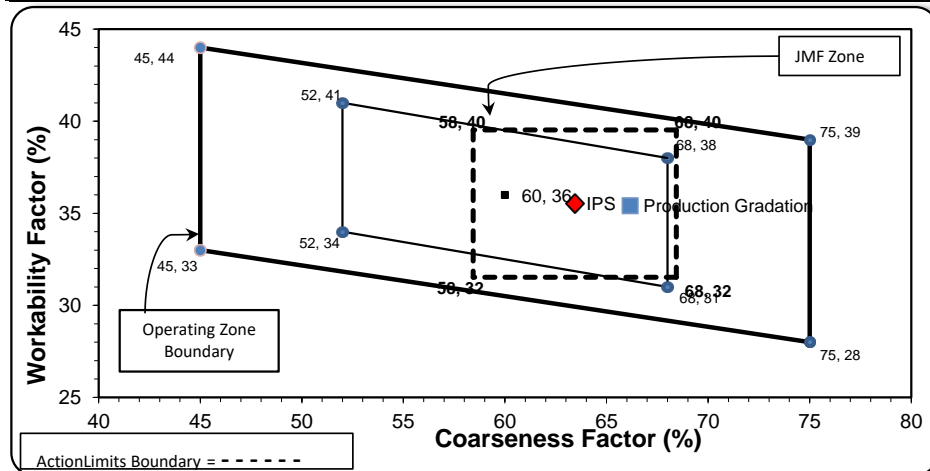

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	100.0	0.0	0.0
3/4"	89.7	10.3	10.3
1/2"	70.3	19.4	29.7
3/8"	59.1	11.2	40.9
#4	42.8	16.3	57.2
#8	35.5	7.3	64.5
#16	29.0	6.5	71.0
#30	21.2	7.7	78.8
#50	9.8	11.5	90.2
#100	3.7	6.1	96.3
LBW	1.2	2.5	98.8

PREPARED BY:
 SM, LLC Technical Service

Approved By:

Aggregate Optimization Chart

PLANT #: **P-02**

Sample Date: 8/31/20

Concrete Grade: **DM**

Contractor: _____

Dates Test Represents: 9/1/2020 through 9/7/2020

MDOT No.: _____

Agg. Class	Pit #	Source	Weight (SSD)	ft ³	Specific Gravity	% Contribution
6AA	71-47	Presque Isle	1505	9.21	2.62	51.8
26A	71-47	Presque Isle	250	1.53	2.62	8.6
2NS	63-115	Ray Rd	1150	6.95	2.65	39.6
Total Wt			2905	17.69		100.0

<----- Verify this number is 100%



Superior Materials, LLC
 30701 W. 10 Mile Rd.
 Suite 500
 Farmington Hills, MI 48336

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	98.6	100.0	100.0	99.3	0.7	0.7
3/4"	85.7	100.0	100.0	92.6	6.7	7.4
1/2"	44.1	96.0	100.0	70.7	21.9	29.3
3/8"	26.4	80.7	100.0	60.2	10.5	39.8
#4	6.4	15.9	98.0	43.5	16.7	56.5
#8	2.9	5.0	80.9	34.0	9.5	66.0
#16	2.4	2.8	64.5	27.0	6.9	73.0
#30	2.3	2.4	48.6	20.6	6.4	79.4
#50	2.2	2.2	23.9	10.8	9.8	89.2
#100	2.1	2.1	4.2	2.9	7.9	97.1
LBW	1.8	1.8	0.3	1.2	1.7	98.8


*Maximum % Retained must be above the 3/8" sieve.
 *Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation Batch Plant Gradations Aggregate Supplier Gradations

Adjusted WF Initial Production Sample (IPS)

Coarseness Factor:	60	Workability Factor:	34	Adjusted WF	36.5
---------------------------	-----------	----------------------------	-----------	--------------------	-------------

Coarseness Factor:	63
Workability Factor:	35

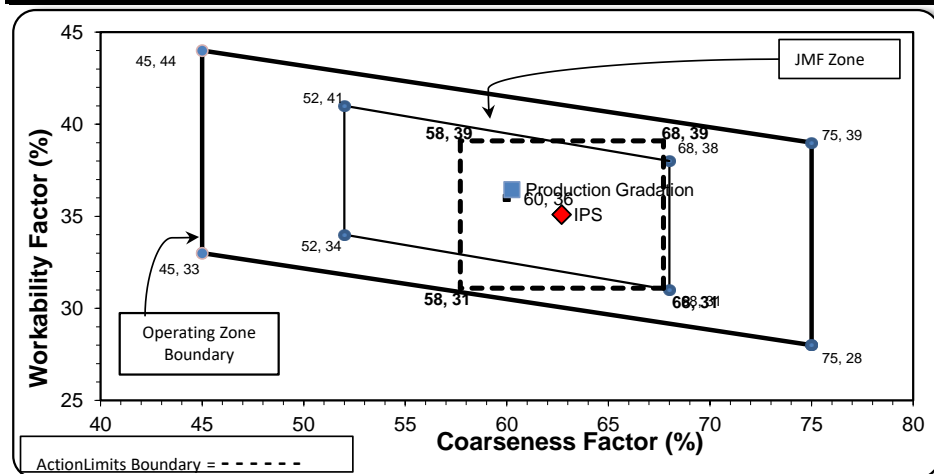

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	100.0	0.0	0.0
3/4"	95.1	4.9	4.9
1/2"	74.6	20.5	25.4
3/8"	59.3	15.3	40.7
#4	42.1	17.2	57.9
#8	35.1	7.1	64.9
#16	29.2	5.9	70.8
#30	21.9	7.3	78.1
#50	9.6	12.4	90.4
#100	2.4	7.2	97.6
LBW	0.9	1.5	99.1

PREPARED BY:
 SM, LLC Technical Service

Approved By:
