

Aggregate Optimization Chart

PLANT #: **P-32**

Sample Date: 4/13/20

Concrete Grade: **P1M**

Contractor: _____

Dates Test Represents: 4/14/2020 through 4/20/2020

MDOT No.: _____

Agg. Class	Pit #	Source	Weight (SSD)	ft ³	Specific Gravity	% Contribution
CA	71-47	Presque Isle	900	5.50	2.62	29.3
IA	71-47	Presque Isle	900	5.50	2.62	29.3
2NS	63-115	Ray Rd	1270	7.68	2.65	41.4
Total Wt			3070	18.69		100.0

<----- Verify this number is 100%




Superior Materials, LLC
 30701 W. 10 Mile Rd.
 Suite 500
 Farmington Hills, MI 48336

Sieve	CA	IA	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	97.4	100.0	100.0	99.2	0.8	0.8
1"	39.8	100.0	100.0	82.4	16.9	17.6
3/4"	9.4	98.2	100.0	72.9	9.4	27.1
1/2"	2.7	81.6	100.0	66.1	6.8	33.9
3/8"	2.1	57.1	100.0	58.7	7.4	41.3
#4	2.1	12.8	98.2	45.0	13.7	55.0
#8	2.0	4.9	80.3	35.2	9.8	64.8
#16	1.9	3.3	63.9	28.0	7.3	72.0
#30	1.9	3.0	48.2	21.4	6.6	78.6
#50	1.8	2.8	24.6	11.5	9.9	88.5
#100	1.7	2.6	4.2	3.0	8.5	97.0
LBW	1.3	2.4	0.7	1.4	1.6	98.6

*Maximum % Retained must be above the 3/8" sieve.
 *Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation Batch Plant Gradations Aggregate Supplier Gradations

Coarseness Factor: **64** **Workability Factor:** **35**

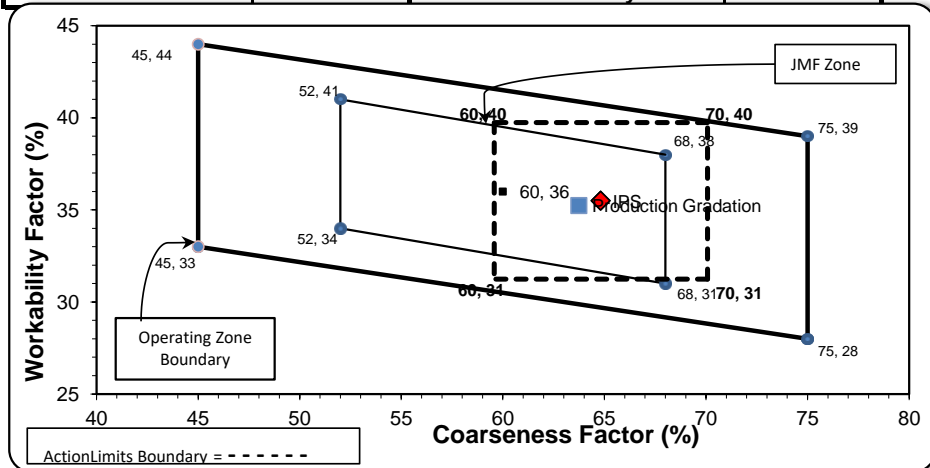

Initial Production Sample (IPS)

Coarseness Factor: **65**
Workability Factor: **35**

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	99.4	0.6	0.6
1"	84.0	15.3	16.0
3/4"	73.5	10.5	26.5
1/2"	65.2	8.2	34.8
3/8"	58.2	7.1	41.8
#4	44.1	14.1	55.9
#8	35.5	8.6	64.5
#16	29.1	6.4	70.9
#30	21.9	7.3	78.1
#50	9.6	12.2	90.4
#100	2.6	7.1	97.4
LBW	1.0	1.6	99.0

PREPARED BY:
 SM, LLC Technical Service

Approved By:

Aggregate Optimization Chart

PLANT #: **P-36**

Sample Date: 4/13/20

Concrete Grade: **P1M**

Contractor: _____

Dates Test Represents: 4/14/2020 through 4/20/2020

MDOT No.: _____

Agg. Class	Pit #	Source	Weight (SSD)	ft ³	Specific Gravity	% Contribution
CA	71-47	Presque Isle	870	5.32	2.62	28.3
IA	71-47	Presque Isle	1000	6.12	2.62	32.6
2NS	63-92	Grange Hall	1200	7.26	2.65	39.1
Total Wt			3070	18.70		100.0

<----- Verify this number is 100%




Superior Materials, LLC
 30701 W. 10 Mile Rd.
 Suite 500
 Farmington Hills, MI 48336

Sieve	CA	IA	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	97.4	100.0	100.0	99.3	0.7	0.7
1"	39.8	100.0	100.0	82.9	16.3	17.1
3/4"	9.4	98.2	100.0	73.7	9.2	26.3
1/2"	2.7	81.6	100.0	66.4	7.3	33.6
3/8"	2.1	57.1	100.0	58.3	8.2	41.7
#4	2.1	12.8	97.3	42.8	15.5	57.2
#8	2.0	4.9	84.4	35.2	7.6	64.8
#16	1.9	3.3	69.1	28.6	6.5	71.4
#30	1.9	3.0	49.9	21.0	7.6	79.0
#50	1.8	2.8	22.7	10.3	10.7	89.7
#100	1.7	2.6	3.6	2.7	7.6	97.3
LBW	1.3	2.4	0.8	1.5	1.3	98.5

*Maximum % Retained must be above the 3/8" sieve.
 *Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation Batch Plant Gradations Aggregate Supplier Gradations

Coarseness Factor:	64	Workability Factor:	35
---------------------------	-----------	----------------------------	-----------

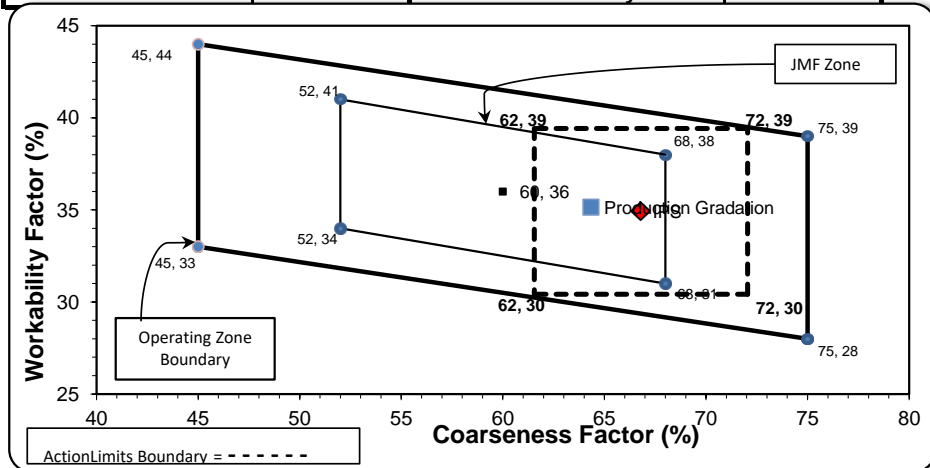

Initial Production Sample (IPS)

Coarseness Factor:	67		
Workability Factor:	35		
Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	85.0	15.0	15.0
3/4"	72.1	12.9	27.9
1/2"	64.5	7.6	35.5
3/8"	56.5	8.0	43.5
#4	42.7	13.8	57.3
#8	34.9	7.8	65.1
#16	29.0	5.9	71.0
#30	21.0	8.0	79.0
#50	8.2	12.8	91.8
#100	1.6	6.5	98.4
LBW	0.7	0.9	99.3

PREPARED BY:
 SM, LLC Technical Service

Approved By:

Aggregate Optimization Chart

PLANT #: **P-39**

Sample Date: 4/13/20

Concrete Grade: **P1M**

Contractor: _____

Dates Test Represents: 4/14/2020 through 4/20/2020

MDOT No.: _____

Agg. Class	Pit #	Source	Weight (SSD)	ft ³	Specific Gravity	% Contribution
CA	71-47	Presque Isle	1000	6.12	2.62	32.6
IA	71-47	Presque Isle	850	5.20	2.62	27.7
2NS	63-92	Grange Hall	1220	7.38	2.65	39.7
Total Wt			3070	18.69		100.0

<----- Verify this number is 100%




Superior Materials, LLC
 30701 W. 10 Mile Rd.
 Suite 500
 Farmington Hills, MI 48336

Sieve	CA	IA	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	97.2	100.0	100.0	99.1	0.9	0.9
1"	38.7	100.0	100.0	80.0	19.1	20.0
3/4"	10.3	98.8	100.0	70.4	9.6	29.6
1/2"	3.2	89.3	100.0	65.5	4.9	34.5
3/8"	2.3	65.1	100.0	58.5	7.0	41.5
#4	1.9	18.4	97.3	44.4	14.1	55.6
#8	1.7	6.5	84.4	35.9	8.5	64.1
#16	1.6	3.7	69.1	29.0	6.9	71.0
#30	1.5	2.9	49.9	21.1	7.9	78.9
#50	1.5	2.6	22.7	10.2	10.9	89.8
#100	1.4	2.4	3.6	2.6	7.7	97.4
LBW	1.2	2.1	0.8	1.3	1.3	98.7

*Maximum % Retained must be above the 3/8" sieve.
 *Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation Batch Plant Gradations Aggregate Supplier Gradations

Coarseness Factor: **65** **Workability Factor:** **36**

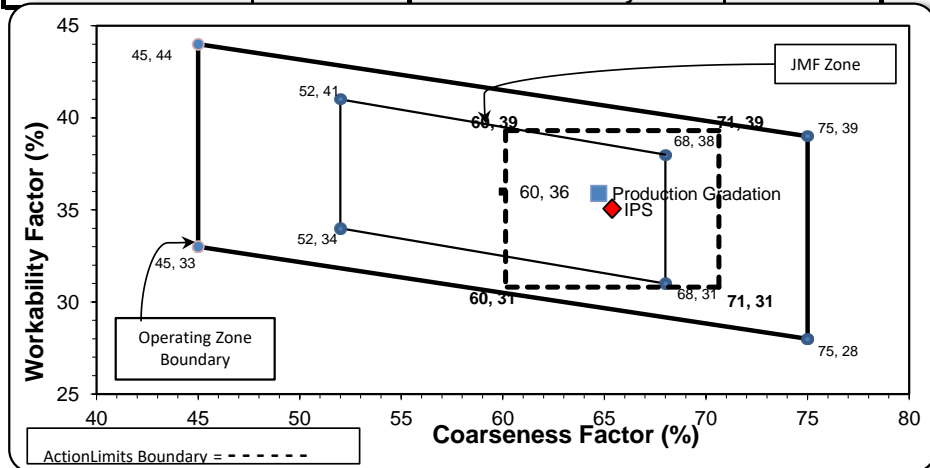

Initial Production Sample (IPS)

Coarseness Factor: **65**
Workability Factor: **35**

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	99.6	0.4	0.4
1"	83.9	15.7	16.1
3/4"	74.1	9.8	25.9
1/2"	64.3	9.7	35.7
3/8"	57.5	6.8	42.5
#4	44.5	13.1	55.5
#8	35.1	9.4	64.9
#16	27.9	7.2	72.1
#30	21.7	6.2	78.3
#50	12.6	9.1	87.4
#100	3.5	9.1	96.5
LBW	1.2	2.4	98.8

PREPARED BY:
 SM, LLC Technical Service

Approved By:

Aggregate Optimization Chart

PLANT #: **P-02**

Sample Date: 4/13/20

Concrete Grade: **P1M**

Contractor: _____

Dates Test Represents: 4/14/2020 through 4/20/2020

MDOT No.: _____

Agg. Class	Pit #	Source	Weight (SSD)	ft ³	Specific Gravity	% Contribution
CA	71-47	Presque Isle	920	5.63	2.62	30.0
IA	71-47	Presque Isle	900	5.50	2.62	29.3
2NS	63-115	Ray Rd	1250	7.56	2.65	40.7
Total Wt			3070	18.69		100.0

<----- Verify this number is 100%




Superior Materials, LLC
 30701 W. 10 Mile Rd.
 Suite 500
 Farmington Hills, MI 48336

Sieve	CA	IA	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	97.4	100.0	100.0	99.2	0.8	0.8
1"	39.8	100.0	100.0	82.0	17.3	18.0
3/4"	9.4	98.2	100.0	72.3	9.6	27.7
1/2"	2.7	81.6	100.0	65.4	6.9	34.6
3/8"	2.1	57.1	100.0	58.1	7.4	41.9
#4	2.1	12.8	98.2	44.4	13.7	55.6
#8	2.0	4.9	80.3	34.7	9.6	65.3
#16	1.9	3.3	63.9	27.6	7.2	72.4
#30	1.9	3.0	48.2	21.1	6.5	78.9
#50	1.8	2.8	24.6	11.4	9.7	88.6
#100	1.7	2.6	4.2	3.0	8.4	97.0
LBW	1.3	2.4	0.7	1.4	1.6	98.6

*Maximum % Retained must be above the 3/8" sieve.
 *Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation Batch Plant Gradations Aggregate Supplier Gradations

Coarseness Factor:	64	Workability Factor:	35
---------------------------	-----------	----------------------------	-----------

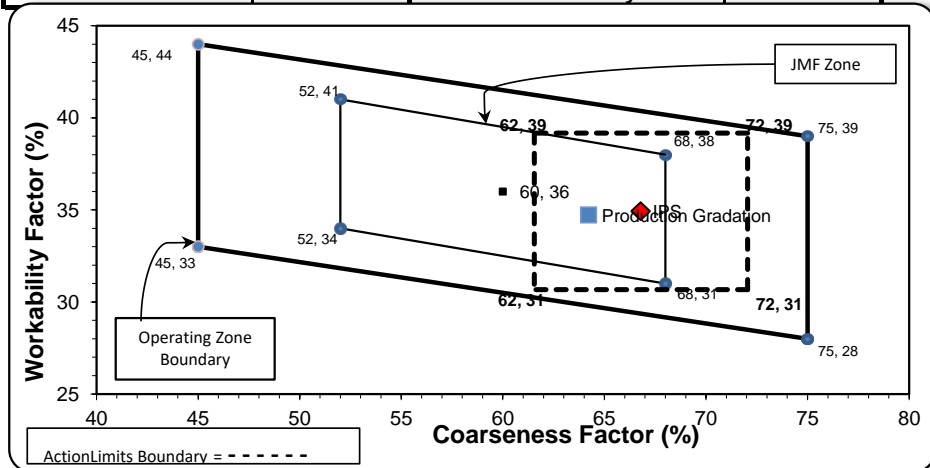

Initial Production Sample (IPS)

Coarseness Factor:	67		
Workability Factor:	35		
Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	85.0	15.0	15.0
3/4"	72.3	12.7	27.7
1/2"	64.5	7.8	35.5
3/8"	56.5	8.0	43.5
#4	42.7	13.8	57.3
#8	34.9	7.8	65.1
#16	29.0	5.9	71.0
#30	21.0	8.0	79.0
#50	8.2	12.8	91.8
#100	1.6	6.5	98.4
LBW	0.7	0.9	99.3

PREPARED BY:
 SM, LLC Technical Service

Approved By:
