

Aggregate Optimization Chart

PLANT #: **P-101**

Sample Date: 8/24/20

Concrete Grade: **P1M**

Contractor: _____

Dates Test Represents: 8/25/2020 through 8/31/2020

MDOT No.: _____

Agg. Class	Pit #	Source	Weight (SSD)	ft ³	Specific Gravity	% Contribution
CA	71-47	Presque Isle	920	5.63	2.62	30.0
IA	71-47	Presque Isle	950	5.81	2.62	30.9
2NS	75-051	Mid-Michigan	1200	7.23	2.66	39.1
Total Wt			3070	18.67		100.0

<---- Verify this number is 100%



Superior Materials, LLC
 30701 W. 10 Mile Rd.
 Suite 500
 Farmington Hills, MI 48336

Sieve	CA	IA	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	94.6	100.0	100.0	98.4	1.6	1.6
1"	33.3	100.0	100.0	80.0	18.4	20.0
3/4"	8.2	94.6	100.0	70.8	9.2	29.2
1/2"	2.4	64.0	100.0	59.6	11.2	40.4
3/8"	1.8	40.4	100.0	52.1	7.5	47.9
#4	1.6	11.2	97.8	42.2	10.0	57.8
#8	1.4	4.2	79.9	33.0	9.2	67.0
#16	1.4	3.1	63.1	26.0	6.9	74.0
#30	1.4	2.6	47.4	19.8	6.3	80.2
#50	1.3	2.3	24.6	10.7	9.0	89.3
#100	1.2	2.1	6.3	3.5	7.2	96.5
LBW	1.0	1.6	0.9	1.1	2.3	98.9

*Maximum % Retained must be above the 3/8" sieve.
 *Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation Batch Plant Gradations Aggregate Supplier Gradations


Coarseness Factor: **71** **Workability Factor:** **33**

Initial Production Sample (IPS)

Coarseness Factor: **66**

Workability Factor: **35**

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	99.6	0.4	0.4
1"	84.3	15.3	15.7
3/4"	74.8	9.6	25.2
1/2"	64.3	10.4	35.7
3/8"	56.8	7.5	43.2
#4	43.0	13.8	57.0
#8	34.9	8.1	65.1
#16	26.4	8.5	73.6
#30	19.9	6.5	80.1
#50	10.4	9.5	89.6
#100	3.4	7.0	96.6
LBW	1.2	2.2	98.8

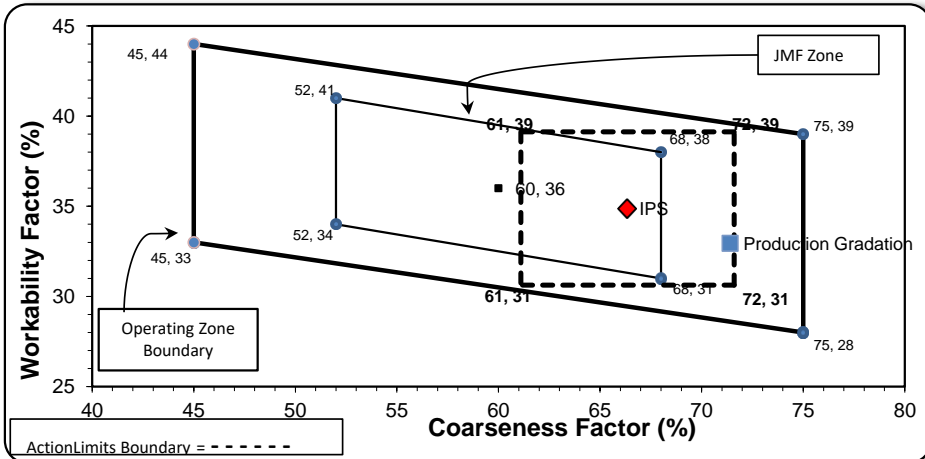

PREPARED BY:
 SM, LLC Technical Service

Approved By:

Aggregate Optimization Chart

PLANT #: **P-102**

Sample Date: 8/24/20

Concrete Grade: **P1M**

Contractor: _____

Dates Test Represents: 8/25/2020 through 8/31/2020

MDOT No.: _____

Agg. Class	Pit #	Source	Weight (SSD)	ft ³	Specific Gravity	% Contribution
CA	58-003	Stoneco	1420	8.46	2.69	45.5
IA	58-003	Stoneco	500	2.98	2.69	16.0
2NS	63-114	Highland	1200	7.26	2.65	38.5
Total Wt			3120	18.70		100.0

<----- Verify this number is 100%




Superior Materials, LLC
 30701 W. 10 Mile Rd.
 Suite 500
 Farmington Hills, MI 48336

Sieve	CA	IA	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	68.5	100.0	100.0	85.7	14.3	14.3
3/4"	33.6	100.0	100.0	69.8	15.9	30.2
1/2"	10.6	93.7	100.0	58.3	11.5	41.7
3/8"	5.1	84.6	100.0	54.3	4.0	45.7
#4	1.5	27.8	99.0	43.2	11.1	56.8
#8	1.4	6.8	83.1	33.7	9.5	66.3
#16	1.3	2.4	65.1	26.0	7.7	74.0
#30	1.1	1.8	47.8	19.2	6.8	80.8
#50	1.1	1.6	21.4	9.0	10.2	91.0
#100	1.0	1.5	4.5	2.4	6.6	97.6
LBW	1.0	1.3	0.3	0.8	1.6	99.2

*Maximum % Retained must be above the 3/8" sieve.
 *Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation Batch Plant Gradations Aggregate Supplier Gradations

Coarseness Factor:	69	Workability Factor:	34
---------------------------	-----------	----------------------------	-----------

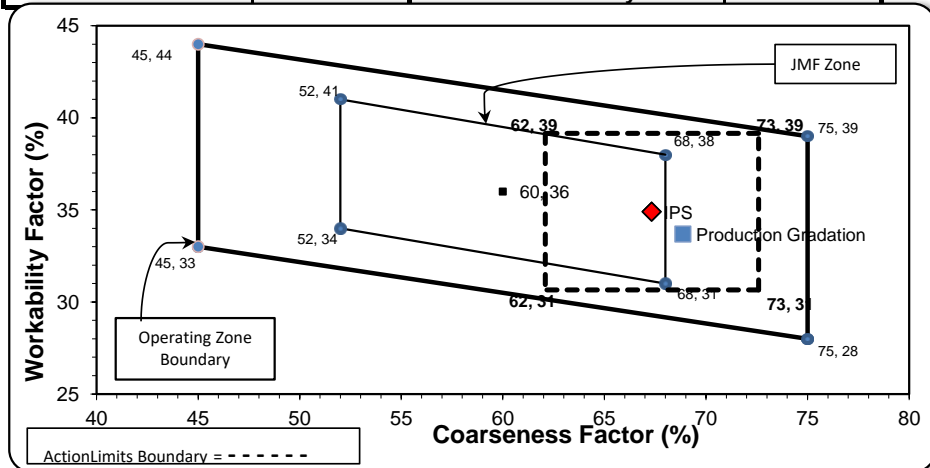

Initial Production Sample (IPS)

Coarseness Factor:	67		
Workability Factor:	35		
Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	85.5	14.5	14.5
3/4"	73.4	12.1	26.6
1/2"	61.0	12.4	39.0
3/8"	56.2	4.8	43.8
#4	43.1	13.1	56.9
#8	34.9	8.2	65.1
#16	29.4	5.5	70.6
#30	21.6	7.8	78.4
#50	8.1	13.4	91.9
#100	2.2	5.9	97.8
LBW	1.4	0.8	98.6

PREPARED BY:
 SM, LLC Technical Service

Approved By:

Aggregate Optimization Chart

PLANT #: **P-12**

Sample Date: 8/24/20

Concrete Grade: **P1M**

Contractor: _____

Dates Test Represents: 8/25/2020 through 8/31/2020

MDOT No.: _____

Agg. Class	Pit #	Source	Weight (SSD)	ft ³	Specific Gravity	% Contribution
CA	71-47	Presque Isle	920	5.63	2.62	30.0
IA	71-47	Presque Isle	900	5.50	2.62	29.3
2NS	63-115	Ray Rd	1250	7.56	2.65	40.7
Total Wt			3070	18.69		100.0

<----- Verify this number is 100%




Superior Materials, LLC
 30701 W. 10 Mile Rd.
 Suite 500
 Farmington Hills, MI 48336

Sieve	CA	IA	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	94.6	100.0	100.0	98.4	1.6	1.6
1"	33.3	100.0	100.0	80.0	18.4	20.0
3/4"	8.2	94.6	100.0	70.9	9.1	29.1
1/2"	2.4	64.0	100.0	60.2	10.7	39.8
3/8"	1.8	40.4	100.0	53.1	7.1	46.9
#4	1.6	11.2	97.8	43.6	9.5	56.4
#8	1.4	4.2	80.3	34.3	9.2	65.7
#16	1.4	3.1	63.7	27.3	7.1	72.7
#30	1.4	2.6	48.0	20.7	6.5	79.3
#50	1.3	2.3	24.6	11.1	9.6	88.9
#100	1.2	2.1	5.0	3.0	8.1	97.0
LBW	1.0	1.6	0.6	1.0	2.0	99.0

*Maximum % Retained must be above the 3/8" sieve.
 *Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation Batch Plant Gradations Aggregate Supplier Gradations

Coarseness Factor:	71	Workability Factor:	34
---------------------------	-----------	----------------------------	-----------

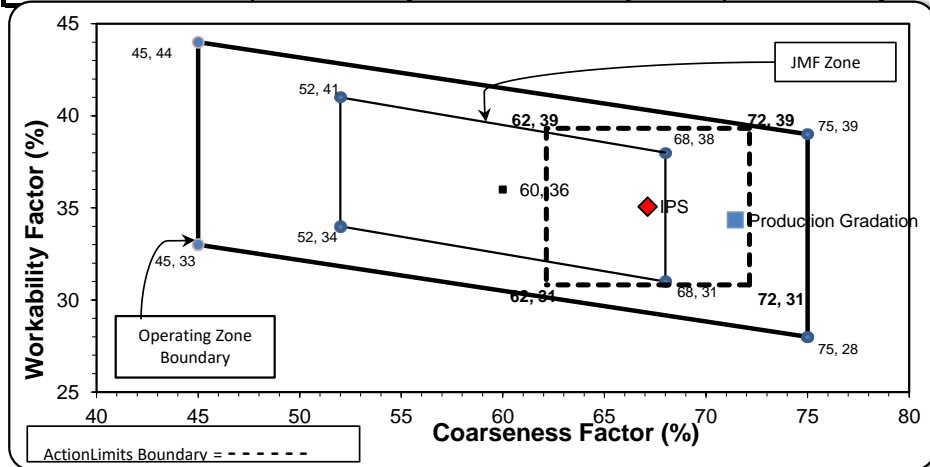

Initial Production Sample (IPS)

Coarseness Factor:	67
Workability Factor:	35

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	99.6	0.4	0.4
1"	83.9	15.7	16.1
3/4"	74.0	9.8	26.0
1/2"	63.7	10.3	36.3
3/8"	56.4	7.3	43.6
#4	43.0	13.4	57.0
#8	35.1	7.9	64.9
#16	29.0	6.1	71.0
#30	20.9	8.0	79.1
#50	8.1	12.8	91.9
#100	1.6	6.5	98.4
LBW	0.9	0.8	99.1

PREPARED BY:
 SM, LLC Technical Service

Approved By:

Aggregate Optimization Chart

PLANT #: **P-20**

Sample Date: 8/24/20

Concrete Grade: **P1M**

Contractor: _____

Dates Test Represents: 8/25/2020 through 8/31/2020

MDOT No.: _____

Agg. Class	Pit #	Source	Weight (SSD)	ft ³	Specific Gravity	% Contribution
CA	71-47	Presque Isle	1000	6.12	2.62	32.6
IA	71-47	Presque Isle	870	5.32	2.62	28.3
2NS	63-92	Grange Hall	1200	7.26	2.65	39.1
Total Wt			3070	18.70		100.0

<----- Verify this number is 100%




Superior Materials, LLC
 30701 W. 10 Mile Rd.
 Suite 500
 Farmington Hills, MI 48336

Sieve	CA	IA	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	97.2	100.0	100.0	99.1	0.9	0.9
1"	41.2	100.0	100.0	80.8	18.2	19.2
3/4"	12.2	99.5	100.0	71.3	9.6	28.7
1/2"	2.6	84.8	100.0	64.0	7.3	36.0
3/8"	1.6	64.0	100.0	57.7	6.2	42.3
#4	1.2	15.7	97.9	43.1	14.6	56.9
#8	1.1	5.7	86.5	35.8	7.3	64.2
#16	1.1	3.0	72.4	29.5	6.3	70.5
#30	1.1	2.4	52.5	21.6	7.9	78.4
#50	1.0	2.2	19.9	8.7	12.8	91.3
#100	0.9	2.1	2.0	1.7	7.1	98.3
LBW	0.8	1.9	0.4	1.0	0.7	99.0

*Maximum % Retained must be above the 3/8" sieve.
 *Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation Batch Plant Gradations Aggregate Supplier Gradations

Coarseness Factor: **66** **Workability Factor:** **36**

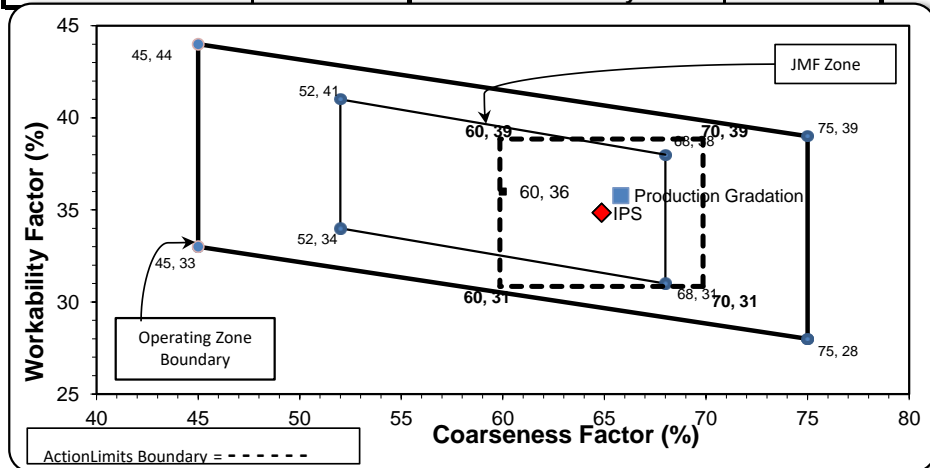

Initial Production Sample (IPS)

Coarseness Factor: **65**
Workability Factor: **35**

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	99.1	0.9	0.9
1"	80.8	18.2	19.2
3/4"	71.3	9.6	28.7
1/2"	64.0	7.3	36.0
3/8"	57.7	6.2	42.3
#4	42.8	15.0	57.2
#8	34.8	7.9	65.2
#16	28.4	6.4	71.6
#30	20.2	8.2	79.8
#50	7.6	12.6	92.4
#100	1.6	6.0	98.4
LBW	1.0	0.6	99.0

PREPARED BY:
 SM, LLC Technical Service

Approved By:

Aggregate Optimization Chart

PLANT #: **P-32**

Sample Date: 8/24/20

Concrete Grade: **P1M**

Contractor: _____

Dates Test Represents: 8/25/2020 through 8/31/2020

MDOT No.: _____

Agg. Class	Pit #	Source	Weight (SSD)	ft ³	Specific Gravity	% Contribution
CA	71-47	Presque Isle	720	4.40	2.62	23.5
IA	71-47	Presque Isle	1100	6.73	2.62	35.8
2NS	95-013	Smelter Bay	1250	7.56	2.65	40.7
Total Wt			3070	18.69		100.0

<----- Verify this number is 100%




Superior Materials, LLC
 30701 W. 10 Mile Rd.
 Suite 500
 Farmington Hills, MI 48336

Sieve	CA	IA	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	94.6	100.0	100.0	98.7	1.3	1.3
1"	33.3	100.0	100.0	84.4	14.4	15.6
3/4"	8.2	94.6	100.0	76.5	7.8	23.5
1/2"	2.4	64.0	100.0	64.2	12.3	35.8
3/8"	1.8	40.4	100.0	55.6	8.6	44.4
#4	1.6	11.2	96.6	43.7	11.9	56.3
#8	1.4	4.2	83.4	35.8	7.9	64.2
#16	1.4	3.1	67.5	28.9	6.9	71.1
#30	1.4	2.6	46.6	20.2	8.7	79.8
#50	1.3	2.3	21.6	9.9	10.3	90.1
#100	1.2	2.1	5.6	3.3	6.6	96.7
LBW	1.0	1.6	1.1	1.3	2.1	98.7

*Maximum % Retained must be above the 3/8" sieve.
 *Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation Batch Plant Gradations Aggregate Supplier Gradations

Coarseness Factor: **69** **Workability Factor:** **36**

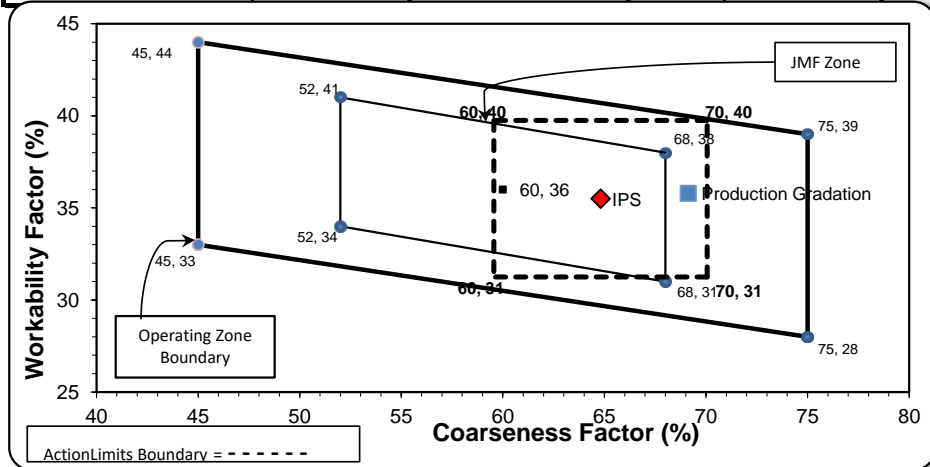

Initial Production Sample (IPS)

Coarseness Factor: **65**
Workability Factor: **36**

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	99.0	0.6	0.6
1"	84.0	15.3	16.0
3/4"	73.5	10.5	26.5
1/2"	65.2	8.2	34.8
3/8"	58.2	7.1	41.8
#4	44.1	14.1	55.9
#8	35.5	8.6	64.5
#16	29.1	6.4	70.9
#30	21.9	7.3	78.1
#50	9.6	12.2	90.4
#100	2.6	7.1	97.4
LBW	1.0	1.6	99.0

PREPARED BY:
 SM, LLC Technical Service

Approved By:

Aggregate Optimization Chart

PLANT #: **P-36**

Sample Date: 8/24/20

Concrete Grade: **P1M**

Contractor: _____

Dates Test Represents: 8/25/2020 through 8/31/2020

MDOT No.: _____

Agg. Class	Pit #	Source	Weight (SSD)	ft ³	Specific Gravity	% Contribution
CA	71-47	Presque Isle	750	4.59	2.62	24.4
IA	71-47	Presque Isle	1120	6.85	2.62	36.5
2NS	63-92	Grange Hall	1200	7.26	2.65	39.1
Total Wt			3070	18.70		100.0

<----- Verify this number is 100%




Superior Materials, LLC
 30701 W. 10 Mile Rd.
 Suite 500
 Farmington Hills, MI 48336

Sieve	CA	IA	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	94.6	100.0	100.0	98.7	1.3	1.3
1"	33.3	100.0	100.0	83.7	15.0	16.3
3/4"	8.2	94.6	100.0	75.6	8.1	24.4
1/2"	2.4	64.0	100.0	63.0	12.6	37.0
3/8"	1.8	40.4	100.0	54.3	8.8	45.7
#4	1.6	11.2	97.9	42.7	11.5	57.3
#8	1.4	4.2	86.5	35.7	7.1	64.3
#16	1.4	3.1	72.4	29.8	5.9	70.2
#30	1.4	2.6	52.5	21.8	8.0	78.2
#50	1.3	2.3	19.9	8.9	12.9	91.1
#100	1.2	2.1	2.0	1.8	7.1	98.2
LBW	1.0	1.6	0.4	1.0	0.9	99.0

*Maximum % Retained must be above the 3/8" sieve.
 *Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation Batch Plant Gradations Aggregate Supplier Gradations

Coarseness Factor:	71	Workability Factor:	36
---------------------------	-----------	----------------------------	-----------

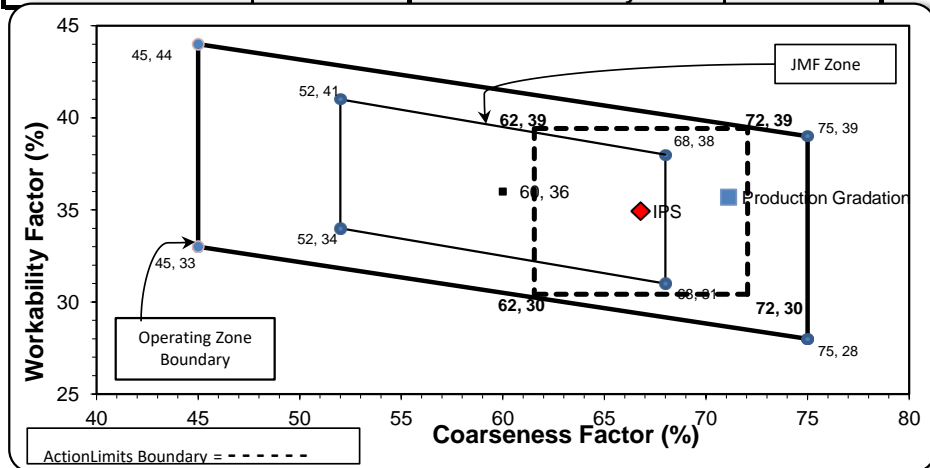

Initial Production Sample (IPS)

Coarseness Factor:	67
Workability Factor:	35

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	85.0	15.0	15.0
3/4"	72.1	12.9	27.9
1/2"	64.5	7.6	35.5
3/8"	56.5	8.0	43.5
#4	42.7	13.8	57.3
#8	34.9	7.8	65.1
#16	29.0	5.9	71.0
#30	21.0	8.0	79.0
#50	8.2	12.8	91.8
#100	1.6	6.5	98.4
LBW	0.7	0.9	99.3

PREPARED BY:
 SM, LLC Technical Service

Approved By:

Aggregate Optimization Chart

PLANT #: **P-39**

Sample Date: 8/24/20

Concrete Grade: **P1M**

Contractor: _____

Dates Test Represents: 8/25/2020 through 8/31/2020

MDOT No.: _____

Agg. Class	Pit #	Source	Weight (SSD)	ft ³	Specific Gravity	% Contribution
CA	71-47	Presque Isle	750	4.59	2.62	24.4
IA	71-47	Presque Isle	1100	6.73	2.62	35.8
2NS	44-051	Krake Willis Rd	1220	7.38	2.65	39.7
Total Wt			3070	18.69		100.0

<----- Verify this number is 100%




Superior Materials, LLC
 30701 W. 10 Mile Rd.
 Suite 500
 Farmington Hills, MI 48336

Sieve	CA	IA	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	94.6	100.0	100.0	98.7	1.3	1.3
1"	33.3	100.0	100.0	83.7	15.0	16.3
3/4"	8.2	94.6	100.0	75.6	8.1	24.4
1/2"	2.4	64.0	100.0	63.3	12.4	36.7
3/8"	1.8	40.4	100.0	54.7	8.6	45.3
#4	1.6	11.2	95.6	42.4	12.3	57.6
#8	1.4	4.2	80.0	33.6	8.8	66.4
#16	1.4	3.1	64.2	27.0	6.7	73.0
#30	1.4	2.6	50.5	21.3	5.6	78.7
#50	1.3	2.3	25.6	11.3	10.0	88.7
#100	1.2	2.1	7.5	4.0	7.3	96.0
LBW	1.0	1.6	0.8	1.1	2.9	98.9

*Maximum % Retained must be above the 3/8" sieve.
 *Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation Batch Plant Gradations Aggregate Supplier Gradations

Coarseness Factor:	68	Workability Factor:	34
---------------------------	-----------	----------------------------	-----------

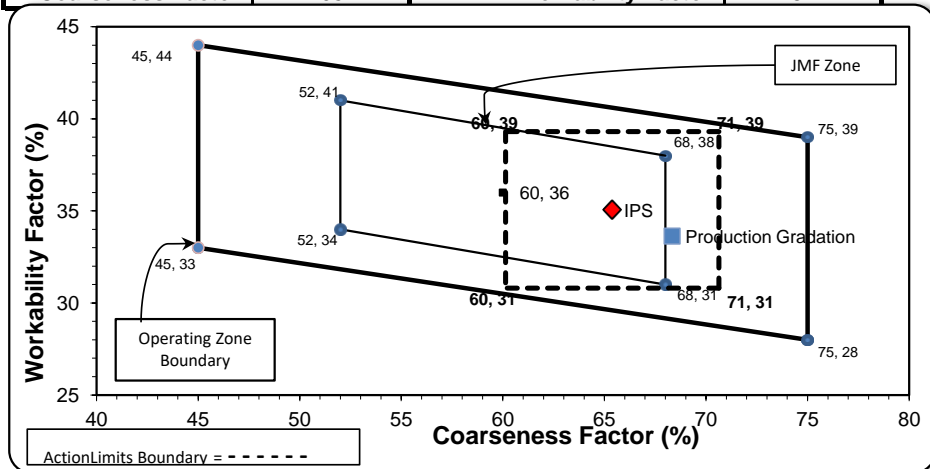

Initial Production Sample (IPS)

Coarseness Factor:	65		
Workability Factor:	35		
Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	99.6	0.4	0.4
1"	83.9	15.7	16.1
3/4"	74.1	9.8	25.9
1/2"	64.3	9.7	35.7
3/8"	57.5	6.8	42.5
#4	44.5	13.1	55.5
#8	35.1	9.4	64.9
#16	27.9	7.2	72.1
#30	21.7	6.2	78.3
#50	12.6	9.1	87.4
#100	3.5	9.1	96.5
LBW	1.2	2.4	98.8

PREPARED BY:
 SM, LLC Technical Service

Approved By:

Aggregate Optimization Chart

PLANT #: **P-02**

Sample Date: 8/24/20 Concrete Grade: **P1M**
 Dates Test Represents: 8/25/2020 through 8/31/2020

Contractor: _____

MDOT No.: _____

Agg. Class	Pit #	Source	Weight (SSD)	ft ³	Specific Gravity	% Contribution
CA	71-47	Presque Isle	920	5.63	2.62	30.0
IA	71-47	Presque Isle	900	5.50	2.62	29.3
2NS	63-115	Ray Rd	1250	7.56	2.65	40.7
Total Wt			3070	18.69		100.0

<----- Verify this number is 100%




Superior Materials, LLC
 30701 W. 10 Mile Rd.
 Suite 500
 Farmington Hills, MI 48336

Sieve	CA	IA	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	94.6	100.0	100.0	98.4	1.6	1.6
1"	33.3	100.0	100.0	80.0	18.4	20.0
3/4"	8.2	94.6	100.0	70.9	9.1	29.1
1/2"	2.4	64.0	100.0	60.2	10.7	39.8
3/8"	1.8	40.4	100.0	53.1	7.1	46.9
#4	1.6	11.2	97.8	43.6	9.5	56.4
#8	1.4	4.2	80.3	34.3	9.2	65.7
#16	1.4	3.1	63.7	27.3	7.1	72.7
#30	1.4	2.6	48.0	20.7	6.5	79.3
#50	1.3	2.3	24.6	11.1	9.6	88.9
#100	1.2	2.1	5.0	3.0	8.1	97.0
LBW	1.0	1.6	0.6	1.0	2.0	99.0

*Maximum % Retained must be above the 3/8" sieve.
 *Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation Batch Plant Gradations Aggregate Supplier Gradations

Coarseness Factor:	71	Workability Factor:	34
---------------------------	-----------	----------------------------	-----------

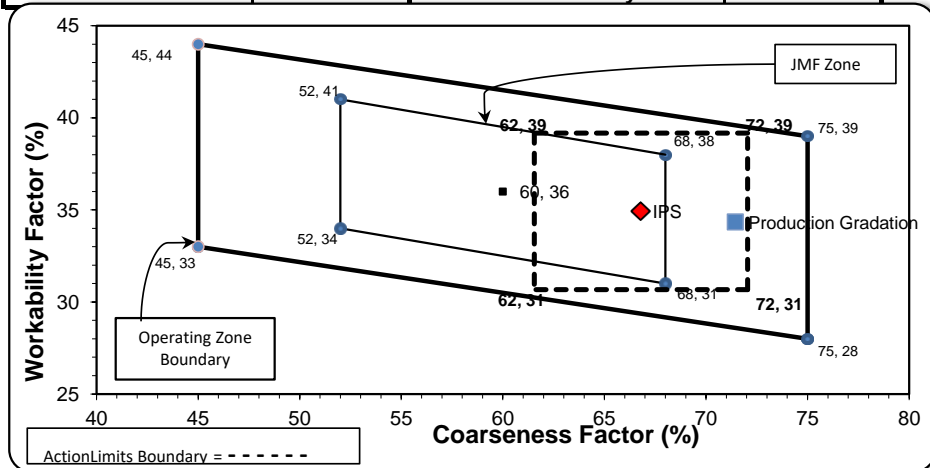

Initial Production Sample (IPS)

Coarseness Factor:	67		
Workability Factor:	35		
Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	85.0	15.0	15.0
3/4"	72.3	12.7	27.7
1/2"	64.5	7.8	35.5
3/8"	56.5	8.0	43.5
#4	42.7	13.8	57.3
#8	34.9	7.8	65.1
#16	29.0	5.9	71.0
#30	21.0	8.0	79.0
#50	8.2	12.8	91.8
#100	1.6	6.5	98.4
LBW	0.7	0.9	99.3

PREPARED BY:
 SM, LLC Technical Service

Approved By:
