

Aggregate Optimization Chart

PLANT #: **P-102**

Sample Date: 5/18/20

Concrete Grade: **S2M**

Contractor: _____

Dates Test Represents: 5/19/2020 through 5/25/2020

MDOT No.: _____

Agg. Class	Pit #	Source	Weight (SSD)	ft ³	Specific Gravity	% Contribution
6AA	58-003	Stoneco	1640	9.77	2.69	52.9
26A	58-003	Stoneco	250	1.49	2.69	8.1
2NS	63-114	Highland	1210	7.32	2.65	39.0
Total Wt			3100	18.58		100.0

<----- Verify this number is 100%




Superior Materials, LLC
 30701 W. 10 Mile Rd.
 Suite 500
 Farmington Hills, MI 48336

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	100.0	100.0	100.0	100.0	0.0	0.0
3/4"	86.1	100.0	100.0	92.6	7.4	7.4
1/2"	41.6	99.6	100.0	69.1	23.6	30.9
3/8"	19.6	79.5	100.0	55.8	13.3	44.2
#4	2.9	8.6	99.0	40.9	14.9	59.1
#8	1.4	1.6	82.2	33.0	7.9	67.0
#16	1.1	1.0	64.7	25.9	7.0	74.1
#30	0.9	0.9	47.1	18.9	7.0	81.1
#50	0.8	0.8	22.0	9.1	9.9	90.9
#100	0.7	0.7	4.5	2.2	6.9	97.8
LBW	0.7	0.5	0.5	0.6	1.6	99.4

*Maximum % Retained must be above the 3/8" sieve.
 *Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation Batch Plant Gradations Aggregate Supplier Gradations

Coarseness Factor:	66	Workability Factor:	33
---------------------------	-----------	----------------------------	-----------

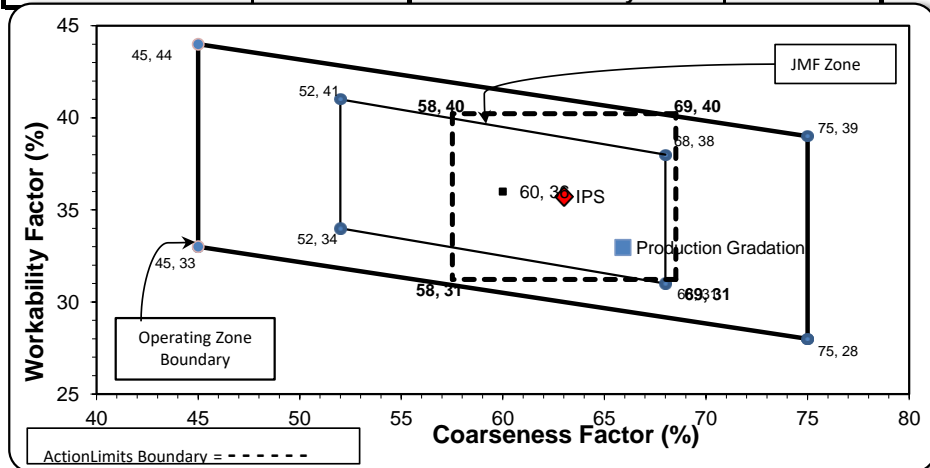

Initial Production Sample (IPS)

Coarseness Factor:	63		
Workability Factor:	36		
Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	99.2	0.8	0.8
3/4"	90.9	8.3	9.1
1/2"	71.3	19.6	28.7
3/8"	59.5	11.8	40.5
#4	43.8	15.7	56.2
#8	35.7	8.1	64.3
#16	27.0	8.7	73.0
#30	18.6	8.4	81.4
#50	6.8	11.8	93.2
#100	1.4	5.4	98.6
LBW	0.6	0.8	99.4

PREPARED BY:
 SM, LLC Technical Service

Approved By:

Aggregate Optimization Chart

PLANT #: **P-103**

Sample Date: 5/18/20

Concrete Grade: **S2M**

Contractor: _____

Dates Test Represents: 5/19/2020 through 5/25/2020

MDOT No.: _____

Agg. Class	Pit #	Source	Weight (SSD)	ft ³	Specific Gravity	% Contribution
6AA	58-003	Stoneco	1640	9.77	2.69	52.9
26A	58-003	Stoneco	250	1.49	2.69	8.1
2NS	63-114	Highland	1210	7.32	2.65	39.0
Total Wt			3100	18.58		100.0

<----- Verify this number is 100%




Superior Materials, LLC
 30701 W. 10 Mile Rd.
 Suite 500
 Farmington Hills, MI 48336

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	100.0	100.0	100.0	100.0	0.0	0.0
3/4"	86.1	100.0	100.0	92.6	7.4	7.4
1/2"	41.6	99.6	100.0	69.1	23.6	30.9
3/8"	19.6	79.5	100.0	55.8	13.3	44.2
#4	2.9	8.6	99.0	40.9	14.9	59.1
#8	1.4	1.6	82.2	33.0	7.9	67.0
#16	1.1	1.0	64.7	25.9	7.0	74.1
#30	0.9	0.9	47.1	18.9	7.0	81.1
#50	0.8	0.8	22.0	9.1	9.9	90.9
#100	0.7	0.7	4.5	2.2	6.9	97.8
LBW	0.7	0.5	0.5	0.6	1.6	99.4

*Maximum % Retained must be above the 3/8" sieve.
 *Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation Batch Plant Gradations Aggregate Supplier Gradations

Coarseness Factor:	66	Workability Factor:	33
---------------------------	-----------	----------------------------	-----------

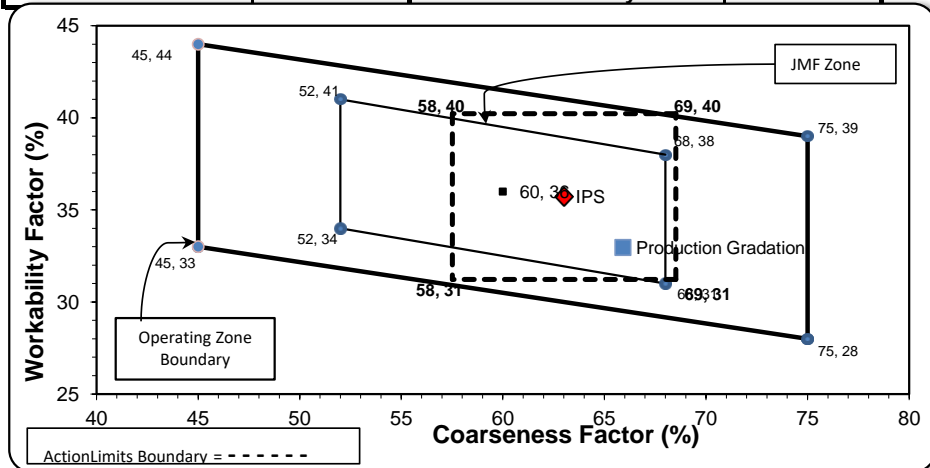

Initial Production Sample (IPS)

Coarseness Factor:	63		
Workability Factor:	36		
Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	99.2	0.8	0.8
3/4"	90.9	8.3	9.1
1/2"	71.3	19.6	28.7
3/8"	59.5	11.8	40.5
#4	43.8	15.7	56.2
#8	35.7	8.1	64.3
#16	27.0	8.7	73.0
#30	18.6	8.4	81.4
#50	6.8	11.8	93.2
#100	1.4	5.4	98.6
LBW	0.6	0.8	99.4

PREPARED BY:
 SM, LLC Technical Service

Approved BY:

Aggregate Optimization Chart

PLANT #: P-12

Sample Date: 5/18/20

Concrete Grade: S2M

Contractor: _____

Dates Test Represents: 5/19/2020 through 5/25/2020

MDOT No.: _____

Agg. Class	Pit #	Source	Weight (SSD)	ft ³	Specific Gravity	% Contribution
6AA	71-47	Presque Isle	1700	10.40	2.62	55.7
26A	71-47	Presque Isle	120	0.73	2.62	3.9
2NS	63-115	Ray Rd	1230	7.44	2.65	40.3
Total Wt			3050	18.57		100.0

<----- Verify this number is 100%




Superior Materials, LLC
 30701 W. 10 Mile Rd.
 Suite 500
 Farmington Hills, MI 48336

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	99.0	100.0	100.0	99.4	0.6	0.6
3/4"	88.0	100.0	100.0	93.3	6.1	6.7
1/2"	50.9	96.7	100.0	72.5	20.8	27.5
3/8"	26.9	84.8	100.0	58.7	13.8	41.3
#4	5.0	27.0	98.3	43.5	15.2	56.5
#8	2.4	8.6	80.2	34.0	9.5	66.0
#16	2.0	4.8	62.4	26.5	7.6	73.5
#30	1.9	4.0	46.0	19.8	6.7	80.2
#50	1.8	3.7	23.6	10.7	9.1	89.3
#100	1.6	3.4	4.8	3.0	7.7	97.0
LBW	1.3	2.8	0.8	1.2	1.8	98.8

*Maximum % Retained must be above the 3/8" sieve.
 *Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation Batch Plant Gradations Aggregate Supplier Gradations

Coarseness Factor: 63 **Workability Factor:** 34

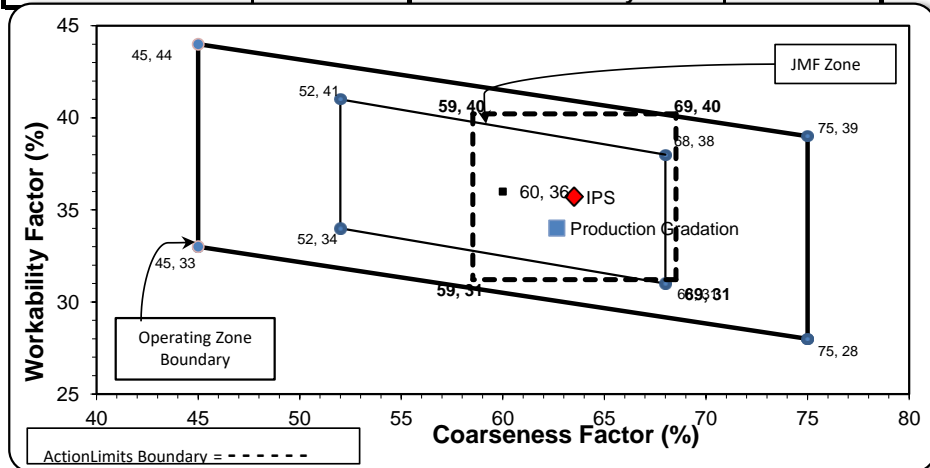

Initial Production Sample (IPS)

Coarseness Factor: 64
Workability Factor: 36

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	99.2	0.8	0.8
3/4"	90.9	8.3	9.1
1/2"	71.3	19.6	28.7
3/8"	59.2	12.1	40.8
#4	41.5	17.7	58.5
#8	35.7	5.8	64.3
#16	27.9	7.9	72.1
#30	18.3	9.5	81.7
#50	7.3	11.0	92.7
#100	2.0	5.3	98.0
LBW	0.9	1.1	99.1

PREPARED BY:
 SM, LLC Technical Service

Approved By:

Aggregate Optimization Chart

PLANT #: **P-32**

Sample Date: 5/18/20 Concrete Grade: **S2M**
 Dates Test Represents: 5/19/2020 through 5/25/2020

Contractor: _____

MDOT No.: _____

Agg. Class	Pit #	Source	Weight (SSD)	ft ³	Specific Gravity	% Contribution
6AA	71-47	Presque Isle	1420	8.69	2.62	46.6
26A	71-47	Presque Isle	400	2.45	2.62	13.1
2NS	95-013	Smelter Bay	1230	7.44	2.65	40.3
Total Wt			3050	18.57		100.0

<----- Verify this number is 100%




Superior Materials, LLC
 30701 W. 10 Mile Rd.
 Suite 500
 Farmington Hills, MI 48336

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	98.7	100.0	100.0	99.4	0.6	0.6
3/4"	72.1	100.0	100.0	87.0	12.4	13.0
1/2"	30.8	96.7	100.0	67.3	19.7	32.7
3/8"	14.6	84.8	100.0	58.2	9.1	41.8
#4	3.4	27.0	96.5	44.0	14.2	56.0
#8	2.2	8.6	84.4	36.2	7.9	63.8
#16	1.9	4.8	69.7	29.6	6.6	70.4
#30	1.5	4.0	51.0	21.8	7.8	78.2
#50	1.4	3.7	22.8	10.3	11.5	89.7
#100	1.3	3.4	5.5	3.3	7.1	96.7
LBW	1.0	2.8	1.1	1.3	2.0	98.7

*Maximum % Retained must be above the 3/8" sieve.
 *Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation Batch Plant Gradations Aggregate Supplier Gradations

Coarseness Factor: **65** **Workability Factor:** **36**

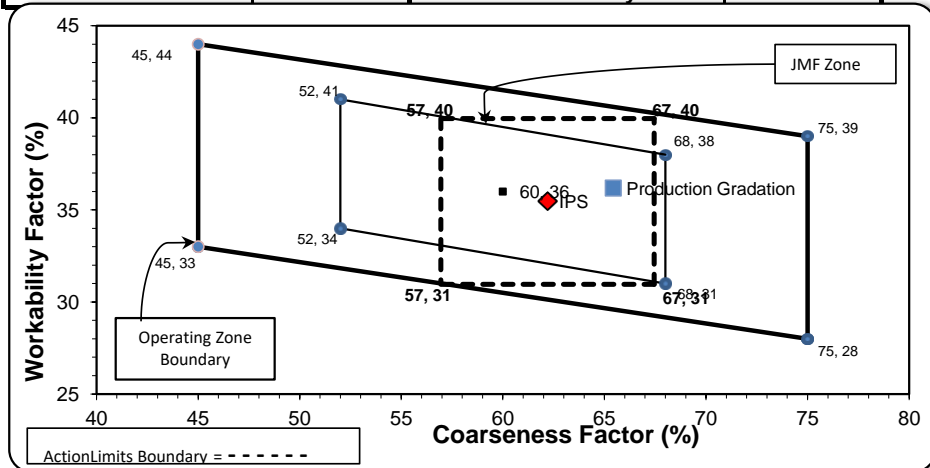

Initial Production Sample (IPS)

Coarseness Factor: **62**
Workability Factor: **35**

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	100.0	0.0	0.0
3/4"	94.0	6.0	6.0
1/2"	70.2	23.7	29.8
3/8"	59.9	10.4	40.1
#4	42.7	17.2	57.3
#8	35.5	7.2	64.5
#16	28.4	7.0	71.6
#30	19.2	9.2	80.8
#50	8.9	10.3	91.1
#100	3.1	5.9	96.9
LBW	1.4	1.7	98.6

PREPARED BY:
 SM, LLC Technical Service

Approved By:

Aggregate Optimization Chart

PLANT #: **P-36**

Sample Date: 5/18/20

Concrete Grade: **S2M**

Contractor: _____

Dates Test Represents: 5/19/2020 through 5/25/2020

MDOT No.: _____

Agg. Class	Pit #	Source	Weight (SSD)	ft ³	Specific Gravity	% Contribution
6AA	71-47	Presque Isle	1600	9.79	2.62	52.5
26A	71-47	Presque Isle	250	1.53	2.62	8.2
2NS	63-92	Grange Hall	1200	7.26	2.65	39.3
Total Wt			3050	18.57		100.0

<----- Verify this number is 100%




Superior Materials, LLC
 30701 W. 10 Mile Rd.
 Suite 500
 Farmington Hills, MI 48336

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	99.0	100.0	100.0	99.5	0.5	0.5
3/4"	88.0	100.0	100.0	93.7	5.8	6.3
1/2"	50.9	96.7	100.0	74.0	19.7	26.0
3/8"	26.9	84.8	100.0	60.4	13.6	39.6
#4	5.0	27.0	97.8	43.3	17.1	56.7
#8	2.4	8.6	85.8	35.7	7.6	64.3
#16	2.0	4.8	71.4	29.5	6.2	70.5
#30	1.9	4.0	51.7	21.7	7.9	78.3
#50	1.8	3.7	23.3	10.4	11.3	89.6
#100	1.6	3.4	3.1	2.3	8.1	97.7
LBW	1.3	2.8	0.6	1.1	1.2	98.9

*Maximum % Retained must be above the 3/8" sieve.
 *Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation Batch Plant Gradations Aggregate Supplier Gradations

Coarseness Factor: **62** **Workability Factor:** **36**

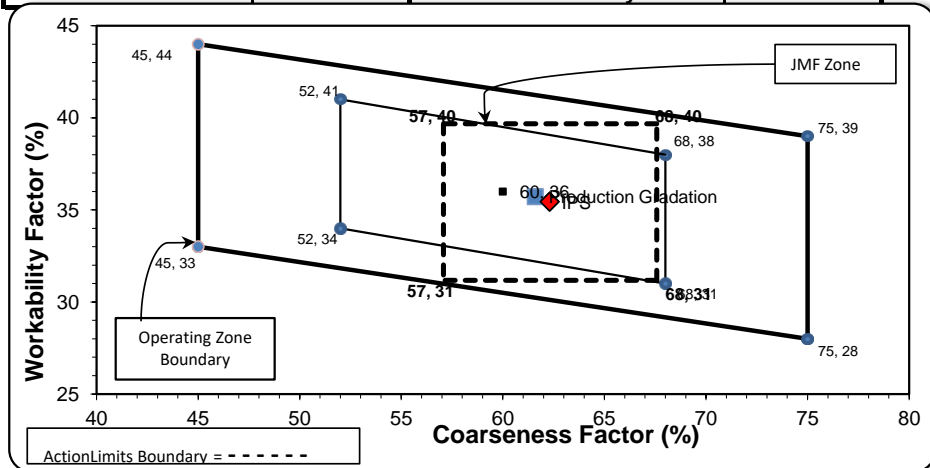

Initial Production Sample (IPS)

Coarseness Factor: **62**
Workability Factor: **35**

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	99.1	0.9	0.9
3/4"	90.5	8.6	9.5
1/2"	69.8	20.7	30.2
3/8"	59.8	10.0	40.2
#4	42.2	17.6	57.8
#8	35.4	6.7	64.6
#16	28.8	6.7	71.2
#30	21.4	7.4	78.6
#50	8.8	12.6	91.2
#100	1.8	7.0	98.2
LBW	0.7	1.0	99.3

PREPARED BY:
 SM, LLC Technical Service

Approved By:

Aggregate Optimization Chart

PLANT #: **P-39**

Sample Date: 5/18/20

Concrete Grade: **S2M**

Contractor: _____

Dates Test Represents: 5/19/2020 through 5/25/2020

MDOT No.: _____

Agg. Class	Pit #	Source	Weight (SSD)	ft ³	Specific Gravity	% Contribution
6AA	71-47	Presque Isle	1700	10.40	2.62	55.7
26A	71-47	Presque Isle	150	0.92	2.62	4.9
2NS	44-051	Krake Willis Rd	1200	7.26	2.65	39.3
Total Wt			3050	18.57		100.0

<----- Verify this number is 100%




Superior Materials, LLC
 30701 W. 10 Mile Rd.
 Suite 500
 Farmington Hills, MI 48336

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	98.0	100.0	100.0	98.9	1.1	1.1
3/4"	87.4	100.0	100.0	93.0	5.9	7.0
1/2"	51.2	96.1	100.0	72.6	20.4	27.4
3/8"	28.9	86.4	100.0	59.7	12.9	40.3
#4	5.3	23.5	96.2	42.0	17.7	58.0
#8	2.5	6.4	82.2	34.0	7.9	66.0
#16	2.0	2.9	66.4	27.4	6.7	72.6
#30	1.9	2.2	49.9	20.8	6.6	79.2
#50	1.8	2.0	22.6	10.0	10.8	90.0
#100	1.7	1.9	5.8	3.3	6.7	96.7
LBW	1.5	1.8	1.0	1.3	2.0	98.7

*Maximum % Retained must be above the 3/8" sieve.
 *Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation Batch Plant Gradations Aggregate Supplier Gradations

Coarseness Factor:	61	Workability Factor:	34
---------------------------	-----------	----------------------------	-----------

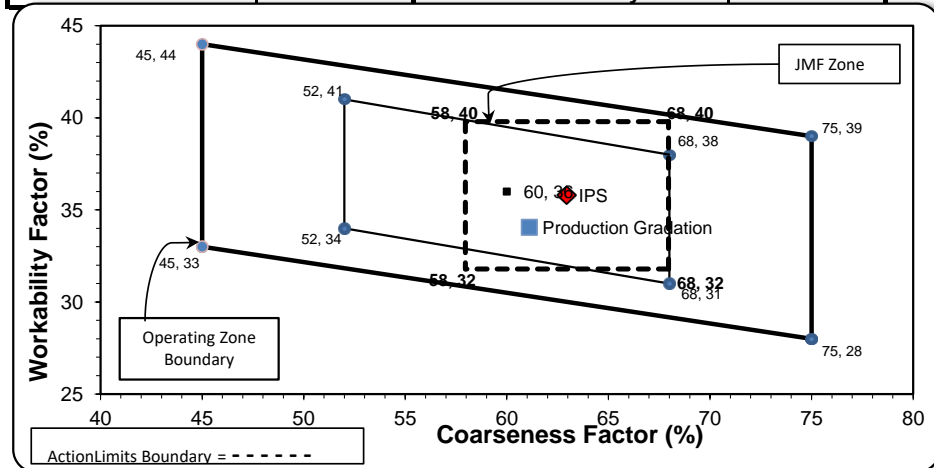

Initial Production Sample (IPS)

Coarseness Factor:	63		
Workability Factor:	36		
Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	100.0	0.0	0.0
3/4"	89.8	10.2	10.2
1/2"	70.7	19.1	29.3
3/8"	59.6	11.1	40.4
#4	43.2	16.4	56.8
#8	35.8	7.4	64.2
#16	29.2	6.6	70.8
#30	21.4	7.8	78.6
#50	9.8	11.6	90.2
#100	3.7	6.1	96.3
LBW	1.2	2.5	98.8

PREPARED BY:
 SM, LLC Technical Service

Approved By:

Aggregate Optimization Chart

PLANT #: **P-02**

Sample Date: 5/18/20

Concrete Grade: **S2M**

Contractor: _____

Dates Test Represents: 5/19/2020 through 5/25/2020

MDOT No.: _____

Agg. Class	Pit #	Source	Weight (SSD)	ft ³	Specific Gravity	% Contribution
6AA	71-47	Presque Isle	1600	9.79	2.62	52.5
26A	71-47	Presque Isle	150	0.92	2.62	4.9
2NS	63-115	Ray Rd	1300	7.86	2.65	42.6
Total Wt			3050	18.57		100.0

<----- Verify this number is 100%




Superior Materials, LLC
 30701 W. 10 Mile Rd.
 Suite 500
 Farmington Hills, MI 48336

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	99.0	100.0	100.0	99.5	0.5	0.5
3/4"	88.0	100.0	100.0	93.7	5.8	6.3
1/2"	50.9	96.7	100.0	74.1	19.6	25.9
3/8"	26.9	84.8	100.0	60.9	13.2	39.1
#4	5.0	27.0	98.3	45.8	15.1	54.2
#8	2.4	8.6	80.2	35.9	10.0	64.1
#16	2.0	4.8	62.4	27.9	8.0	72.1
#30	1.9	4.0	46.0	20.8	7.1	79.2
#50	1.8	3.7	23.6	11.2	9.6	88.8
#100	1.6	3.4	4.8	3.1	8.1	96.9
LBW	1.3	2.8	0.8	1.2	1.9	98.8

*Maximum % Retained must be above the 3/8" sieve.
 *Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation Batch Plant Gradations Aggregate Supplier Gradations

Coarseness Factor:	61	Workability Factor:	36
---------------------------	-----------	----------------------------	-----------

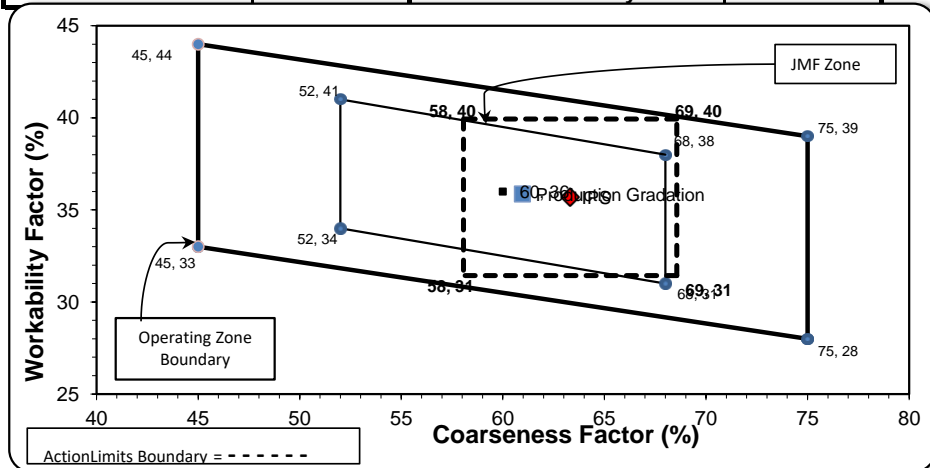

Initial Production Sample (IPS)

Coarseness Factor:	63		
Workability Factor:	36		
Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	100.0	0.0	0.0
3/4"	95.6	4.4	4.4
1/2"	73.1	22.6	26.9
3/8"	59.3	13.8	40.7
#4	42.8	16.5	57.2
#8	35.7	7.1	64.3
#16	28.9	6.8	71.1
#30	20.7	8.2	79.3
#50	9.9	10.8	90.1
#100	2.1	7.8	97.9
LBW	0.9	1.2	99.1

PREPARED BY:
 SM, LLC Technical Service

Approved By:
