

Aggregate Optimization Chart

Production Gradation Report

PLANT #: **P-101**

Contractor: _____

Sample Date: 9/20/21

Concrete Grade: **DM**

Dates Test Represents: 9/21/2021 through 9/27/2021

MDOT No.: _____

Agg. Class	Pit #	Source	Weight (SSD)	ft ³	Specific Gravity	% Contribution
6AA	71-47	Presque Isle	1560	9.54	2.62	53.6
26A	71-47	Presque Isle	200	1.22	2.62	6.9
2NS	75-051	Mid-Michigan	1150	6.93	2.66	39.5
Total Wt			2910	17.69		100.0

<----- Verify this number is 100%



Superior Materials, LLC
 30701 W. 10 Mile Rd.
 Suite 500
 Farmington Hills, MI 48336

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	98.1	100.0	100.0	99.0	1.0	1.0
3/4"	85.9	100.0	100.0	92.4	6.5	7.6
1/2"	39.5	98.1	100.0	67.4	25.0	32.6
3/8"	22.5	89.2	100.0	57.7	9.7	42.3
#4	3.5	16.7	99.0	42.1	15.6	57.9
#8	2.0	4.2	83.2	34.2	7.9	65.8
#16	1.8	2.2	67.3	27.7	6.5	72.3
#30	1.6	2.0	51.5	21.3	6.4	78.7
#50	1.5	1.8	25.3	10.9	10.4	89.1
#100	1.4	1.7	5.9	3.2	7.7	96.8
LBW	1.2	1.6	0.7	1.0	2.2	99.0


*Maximum % Retained must be above the 3/8" sieve.
 *Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation Batch Plant Gradations Aggregate Supplier Gradations Adjusted WF Initial Production Sample (IPS)

Coarseness Factor: 64	Workability Factor: 34	Adjusted WF 36.7	Coarseness Factor: 62
-------------------------------------	--------------------------------------	--------------------------------	-------------------------------------

Workability Factor: 35

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	100.0	0.0	0.0
3/4"	95.0	5.0	5.0
1/2"	70.5	24.5	29.5
3/8"	60.0	10.5	40.0
#4	44.4	15.6	55.6
#8	35.5	9.0	64.5
#16	28.5	7.0	71.5
#30	21.5	7.0	78.5
#50	10.2	11.3	89.8
#100	3.1	7.1	96.9
LBW	1.3	1.8	98.7

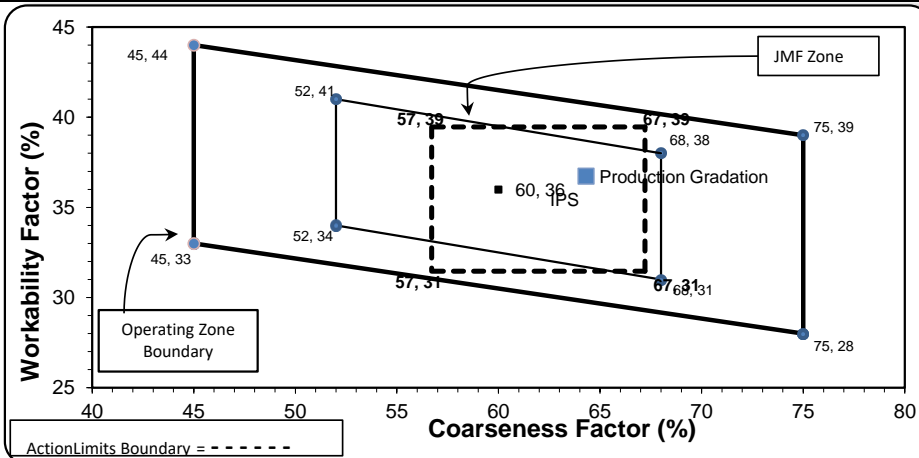

PREPARED BY:
 SM, LLC Technical Service

Approved By:

Aggregate Optimization Chart

PLANT #: **P-102**

Sample Date: 9/20/21

Concrete Grade: **DM**

Contractor: _____

Dates Test Represents: 9/21/2021 through 9/27/2021

MDOT No.: _____

Agg. Class	Pit #	Source	Weight (SSD)	ft ³	Specific Gravity	% Contribution
6AA	58-003	Stoneco	1550	9.23	2.69	52.5
26A	58-003	Stoneco	255	1.52	2.69	8.6
2NS	63-114	Highland	1150	6.95	2.65	38.9
Total Wt			2955	17.71		100.0

<----- Verify this number is 100%



Superior Materials, LLC
 30701 W. 10 Mile Rd.
 Suite 500
 Farmington Hills, MI 48336

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	100.0	100.0	100.0	100.0	0.0	0.0
3/4"	86.2	100.0	100.0	92.8	7.2	7.2
1/2"	49.2	98.7	100.0	73.2	19.5	26.8
3/8"	25.6	89.2	100.0	60.0	13.2	40.0
#4	4.0	27.9	98.8	43.0	17.1	57.0
#8	1.6	8.1	83.5	34.0	8.9	66.0
#16	1.3	3.3	66.2	26.7	7.3	73.3
#30	1.1	2.3	47.0	19.1	7.7	80.9
#50	1.0	2.1	20.4	8.6	10.4	91.4
#100	1.0	2.0	4.4	2.4	6.2	97.6
LBW	0.7	1.8	0.8	0.8	1.6	99.2


*Maximum % Retained must be above the 3/8" sieve.
 *Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation Batch Plant Gradations Aggregate Supplier Gradations

Adjusted WF Initial Production Sample (IPS)

Coarseness Factor:	61	Workability Factor:	34	36.5
---------------------------	-----------	----------------------------	-----------	-------------

Coarseness Factor:	61
Workability Factor:	36

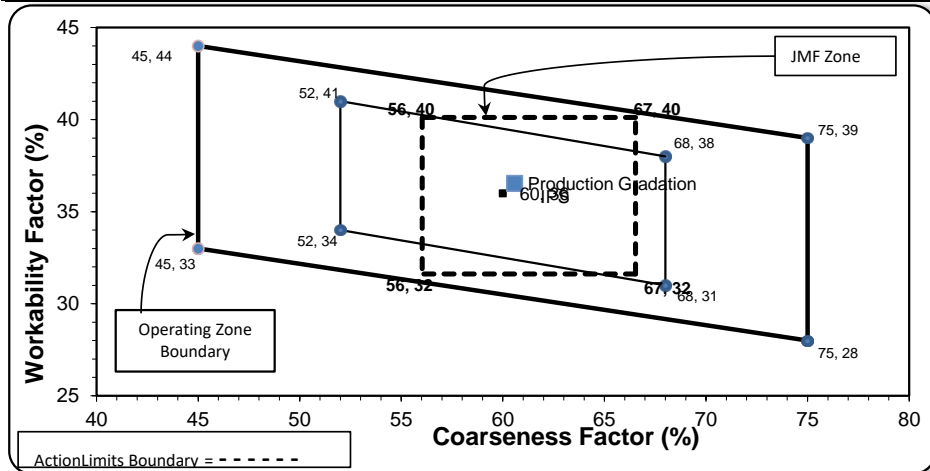

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	99.3	0.7	0.7
3/4"	89.2	10.1	10.8
1/2"	70.7	18.5	29.3
3/8"	60.7	10.0	39.3
#4	44.4	16.3	55.6
#8	35.9	8.5	64.1
#16	27.3	8.6	72.7
#30	19.1	8.2	80.9
#50	7.4	11.7	92.6
#100	1.9	5.6	98.1
LBW	0.7	1.2	99.3

PREPARED BY:
 SM, LLC Technical Service

Approved By:

Aggregate Optimization Chart

PLANT #: **P-20**

Sample Date: 9/20/21 Concrete Grade: **DM**
 Dates Test Represents: 9/21/2021 through 9/27/2021

Contractor: _____

MDOT No.: _____



Superior Materials, LLC
 30701 W. 10 Mile Rd.
 Suite 500
 Farmington Hills, MI 48336

Agg. Class	Pit #	Source	Weight (SSD)	ft ³	Specific Gravity	% Contribution
6AA	71-47	Presque Isle	1805	11.04	2.62	62.1
26A	71-47	Presque Isle	0	0.00	2.62	0.0
2NS	63-92	Grange Hall	1100	6.65	2.65	37.9
Total Wt			2905	17.69		100.0

<----- Verify this number is 100%


Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	98.0	100.0	100.0	98.8	1.2	1.2
3/4"	85.6	100.0	100.0	91.1	7.7	8.9
1/2"	52.7	97.8	100.0	70.6	20.4	29.4
3/8"	33.0	84.2	100.0	58.4	12.2	41.6
#4	6.9	14.9	97.7	41.3	17.1	58.7
#8	2.7	3.8	84.8	33.8	7.5	66.2
#16	2.0	2.2	69.5	27.6	6.2	72.4
#30	1.8	1.9	50.4	20.2	7.4	79.8
#50	1.8	1.7	22.5	9.6	10.6	90.4
#100	1.7	1.6	3.7	2.5	7.2	97.5
LBW	1.6	1.5	0.4	1.1	1.3	98.9

*Maximum % Retained must be above the 3/8" sieve.
 *Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation Batch Plant Gradations Aggregate Supplier Gradations Adjusted WF Initial Production Sample (IPS)

Coarseness Factor:	63	Workability Factor:	34	Adjusted WF	36.3
---------------------------	-----------	----------------------------	-----------	--------------------	-------------

Coarseness Factor:	63
Workability Factor:	36

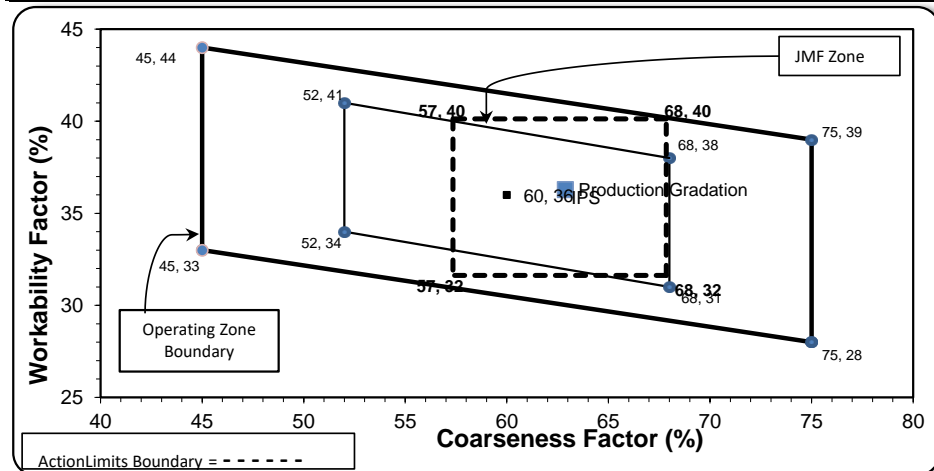

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	100.0	0.0	0.0
3/4"	89.2	10.8	10.8
1/2"	68.4	20.8	31.6
3/8"	59.9	8.6	40.1
#4	43.0	16.9	57.0
#8	35.9	7.1	64.1
#16	29.0	6.8	71.0
#30	21.3	7.7	78.7
#50	9.9	11.4	90.1
#100	2.4	7.5	97.6
LBW	1.2	1.2	98.8

PREPARED BY:
 SM, LLC Technical Service

Approved By:

Aggregate Optimization Chart

PLANT #: **P-32**

Sample Date: 9/20/21 Concrete Grade: DM

Dates Test Represents: 9/21/2021 through 9/27/2021

Contractor: _____

MDOT No.: _____

Agg. Class	Pit #	Source	Weight (SSD)	ft ³	Specific Gravity	% Contribution
6AA	71-47	Presque Isle	1600	9.79	2.62	55.1
26A	71-47	Presque Isle	155	0.95	2.62	5.3
2NS	95-013	Smelter Bay	1150	6.95	2.65	39.6
Total Wt			2905	17.69		100.0

<----- Verify this number is 100%



Superior Materials, LLC
 30701 W. 10 Mile Rd.
 Suite 500
 Farmington Hills, MI 48336


Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	97.2	100.0	100.0	98.5	1.5	1.5
3/4"	86.3	100.0	100.0	92.5	6.0	7.5
1/2"	49.1	95.6	100.0	71.7	20.7	28.3
3/8"	28.2	82.8	100.0	59.5	12.2	40.5
#4	5.7	16.0	95.0	41.6	17.9	58.4
#8	3.2	4.5	82.3	34.6	7.0	65.4
#16	2.4	2.4	67.3	28.1	6.5	71.9
#30	2.3	2.0	49.4	20.9	7.2	79.1
#50	2.2	1.8	25.2	11.3	9.6	88.7
#100	1.9	1.7	8.2	4.4	6.9	95.6
LBW	1.5	1.3	1.6	1.5	2.9	98.5

*Maximum % Retained must be above the 3/8" sieve.
 *Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation Batch Plant Gradations Aggregate Supplier Gradations Adjusted WF Initial Production Sample (IPS)

Coarseness Factor:	62	Workability Factor:	35	Adjusted WF	37.1
---------------------------	-----------	----------------------------	-----------	--------------------	-------------

Coarseness Factor:	62
Workability Factor:	36

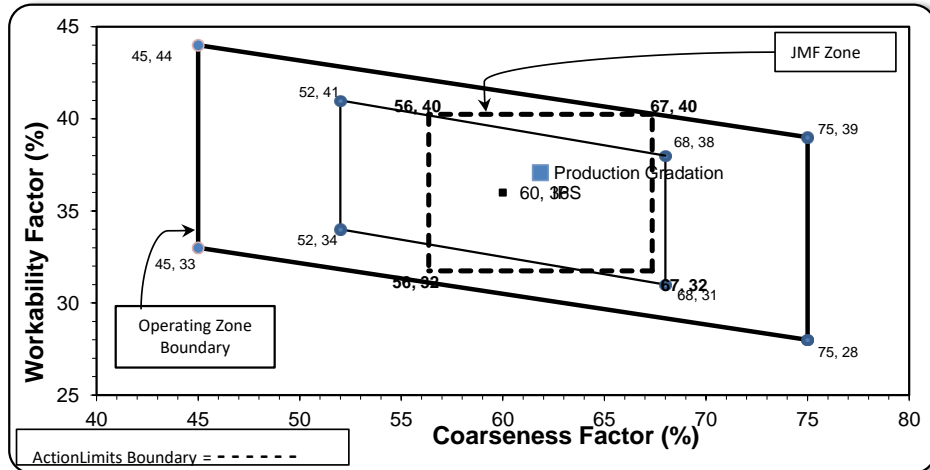

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	100.0	0.0	0.0
3/4"	95.0	5.0	5.0
1/2"	72.3	22.8	27.7
3/8"	60.4	11.8	39.6
#4	42.6	17.8	57.4
#8	36.0	6.6	64.0
#16	29.5	6.5	70.5
#30	20.3	9.2	79.7
#50	9.5	10.8	90.5
#100	3.4	6.1	96.6
LBW	1.3	2.1	98.7

PREPARED BY:
 SM, LLC Technical Service

Approved By:

Aggregate Optimization Chart

PLANT #: **P-35**

Sample Date: 9/20/21

Concrete Grade: **DM**

Contractor: _____

Dates Test Represents: 9/21/2021 through 9/27/2021

MDOT No.: _____

Agg. Class	Pit #	Source	Weight (SSD)	ft ³	Specific Gravity	% Contribution
6AA	58-003	Stoneco	1555	9.26	2.69	52.6
26A	58-003	Stoneco	300	1.79	2.69	10.2
2NS	81-093	Burmeister	1100	6.65	2.65	37.2
Total Wt			2955	17.70		100.0

<----- Verify this number is 100%



Superior Materials, LLC
 30701 W. 10 Mile Rd.
 Suite 500
 Farmington Hills, MI 48336

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	100.0	100.0	100.0	100.0	0.0	0.0
3/4"	86.2	100.0	100.0	92.7	7.3	7.3
1/2"	49.2	98.7	100.0	73.1	19.6	26.9
3/8"	25.6	89.2	100.0	59.8	13.4	40.2
#4	4.0	27.9	98.8	41.7	18.0	58.3
#8	1.6	8.1	85.6	33.5	8.2	66.5
#16	1.3	3.3	68.5	26.5	7.0	73.5
#30	1.1	2.3	48.2	18.8	7.8	81.2
#50	1.0	2.1	15.0	6.3	12.4	93.7
#100	1.0	2.0	1.9	1.4	4.9	98.6
LBW	0.7	1.8	0.5	0.7	0.7	99.3


*Maximum % Retained must be above the 3/8" sieve.
 *Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation Batch Plant Gradations Aggregate Supplier Gradations

Adjusted WF Initial Production Sample (IPS)

Coarseness Factor:	61	Workability Factor:	34	Adjusted WF	36.0
---------------------------	-----------	----------------------------	-----------	--------------------	-------------

Coarseness Factor:	61
Workability Factor:	36

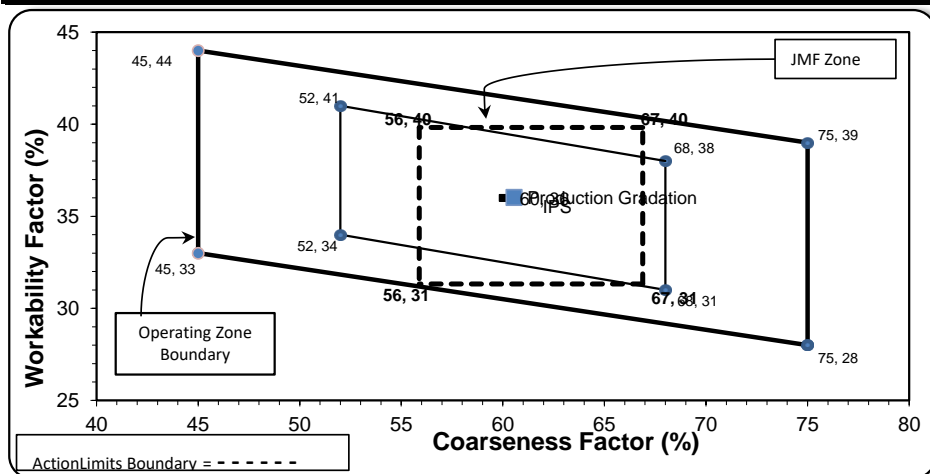

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	99.3	0.7	0.7
3/4"	89.1	10.2	10.9
1/2"	70.5	18.6	29.5
3/8"	60.5	10.0	39.5
#4	44.1	16.4	55.9
#8	35.6	8.5	64.4
#16	27.7	7.9	72.3
#30	20.6	7.1	79.4
#50	8.7	11.8	91.3
#100	1.6	7.1	98.4
LBW	1.1	0.6	98.9

PREPARED BY:
 SM, LLC Technical Service

Approved By:

Aggregate Optimization Chart

PLANT #: **P-36**

Sample Date: 9/20/21

Concrete Grade: **DM**

Contractor: _____

Dates Test Represents: 9/21/2021 through 9/27/2021

MDOT No.: _____

Agg. Class	Pit #	Source	Weight (SSD)	ft ³	Specific Gravity	% Contribution
6AA	71-47	Presque Isle	1505	9.21	2.62	51.8
26A	71-47	Presque Isle	300	1.83	2.62	10.3
2NS	63-92	Grange Hall	1100	6.65	2.65	37.9
Total Wt			2905	17.69		100.0

<----- Verify this number is 100%



Superior Materials, LLC
 30701 W. 10 Mile Rd.
 Suite 500
 Farmington Hills, MI 48336

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	98.2	100.0	100.0	99.1	0.9	0.9
3/4"	74.6	100.0	100.0	86.8	12.2	13.2
1/2"	43.2	95.6	100.0	70.1	16.7	29.9
3/8"	21.3	82.8	100.0	57.5	12.7	42.5
#4	4.8	16.0	97.7	41.1	16.3	58.9
#8	3.0	4.5	84.8	34.1	7.0	65.9
#16	2.3	2.4	69.5	27.8	6.4	72.2
#30	2.0	2.0	50.4	20.3	7.4	79.7
#50	1.9	1.8	22.5	9.7	10.6	90.3
#100	1.8	1.7	3.7	2.5	7.2	97.5
LBW	1.4	1.3	0.4	1.0	1.5	99.0


*Maximum % Retained must be above the 3/8" sieve.
 *Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation Batch Plant Gradations Aggregate Supplier Gradations

Adjusted WF Initial Production Sample (IPS)

Coarseness Factor:	65	Workability Factor:	34	Adjusted WF	36.6
---------------------------	-----------	----------------------------	-----------	--------------------	-------------

Coarseness Factor:	63
Workability Factor:	35

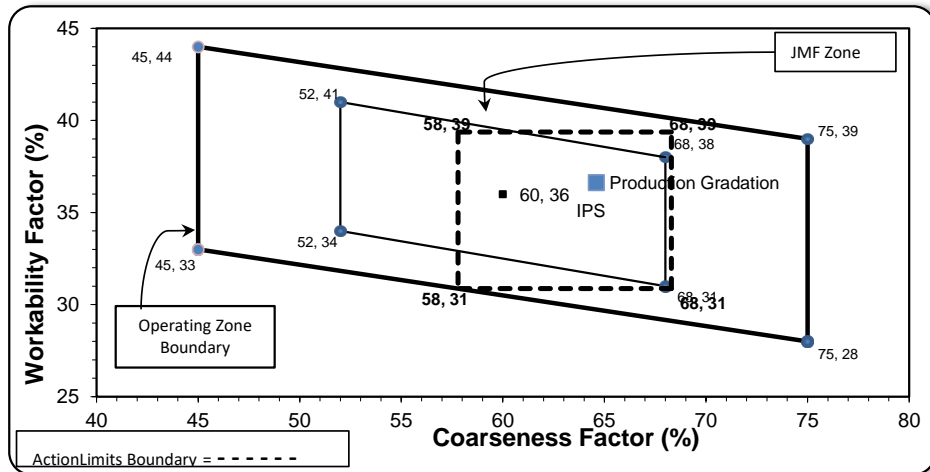

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	99.1	0.9	0.9
3/4"	90.3	8.8	9.7
1/2"	69.2	21.1	30.8
3/8"	59.1	10.1	40.9
#4	41.8	17.3	58.2
#8	35.1	6.6	64.9
#16	28.5	6.6	71.5
#30	21.2	7.3	78.8
#50	8.7	12.5	91.3
#100	1.8	7.0	98.2
LBW	0.7	1.0	99.3

PREPARED BY:
 SM, LLC Technical Service

Approved By:

Aggregate Optimization Chart

PLANT #: **P-39**

Sample Date: 9/20/21 Concrete Grade: DM

Dates Test Represents: 9/21/2021 through 9/27/2021

Contractor: _____

MDOT No.: _____

Agg. Class	Pit #	Source	Weight (SSD)	ft ³	Specific Gravity	% Contribution
6AA	71-47	Presque Isle	1605	9.82	2.62	55.2
26A	71-47	Presque Isle	200	1.22	2.62	6.9
2NS	44-051	Krake Willis Rd	1100	6.65	2.65	37.9
Total Wt			2905	17.69		100.0

<----- Verify this number is 100%



Superior Materials, LLC
 30701 W. 10 Mile Rd.
 Suite 500
 Farmington Hills, MI 48336

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	98.1	100.0	100.0	99.0	1.0	1.0
3/4"	85.9	100.0	100.0	92.2	6.7	7.8
1/2"	39.5	98.1	100.0	66.4	25.8	33.6
3/8"	22.5	89.2	100.0	56.4	10.0	43.6
#4	3.5	16.7	97.4	40.0	16.5	60.0
#8	2.0	4.2	79.6	31.5	8.4	68.5
#16	1.8	2.2	63.6	25.2	6.3	74.8
#30	1.6	2.0	48.4	19.3	5.9	80.7
#50	1.5	1.8	26.7	11.1	8.3	88.9
#100	1.4	1.7	8.9	4.3	6.8	95.7
LBW	1.2	1.6	1.2	1.2	3.0	98.8


*Maximum % Retained must be above the 3/8" sieve.
 *Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation Batch Plant Gradations Aggregate Supplier Gradations

Adjusted WF Initial Production Sample (IPS)

Coarseness Factor:	64	Workability Factor:	32	Adjusted WF	34.0
---------------------------	-----------	----------------------------	-----------	--------------------	-------------

Coarseness Factor:	63
Workability Factor:	36

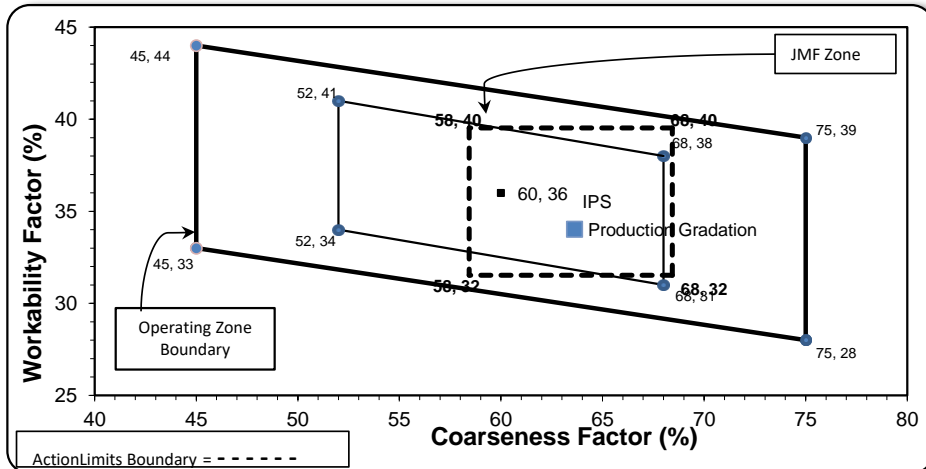

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	100.0	0.0	0.0
3/4"	89.7	10.3	10.3
1/2"	70.3	19.4	29.7
3/8"	59.1	11.2	40.9
#4	42.8	16.3	57.2
#8	35.5	7.3	64.5
#16	29.0	6.5	71.0
#30	21.2	7.7	78.8
#50	9.8	11.5	90.2
#100	3.7	6.1	96.3
LBW	1.2	2.5	98.8

PREPARED BY:
 SM, LLC Technical Service

Approved By:

Aggregate Optimization Chart

PLANT #: **P-02**

Sample Date: 9/20/21 Concrete Grade: **DM**

Dates Test Represents: 9/21/2021 through 9/27/2021

Contractor: _____

MDOT No.: _____

Agg. Class	Pit #	Source	Weight (SSD)	ft ³	Specific Gravity	% Contribution
6AA	71-47	Presque Isle	1555	9.51	2.62	53.5
26A	71-47	Presque Isle	250	1.53	2.62	8.6
2NS	63-115	Ray Rd	1100	6.65	2.65	37.9
Total Wt			2905	17.69		100.0

<----- Verify this number is 100%



Superior Materials, LLC
 30701 W. 10 Mile Rd.
 Suite 500
 Farmington Hills, MI 48336

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	98.2	100.0	100.0	99.0	1.0	1.0
3/4"	74.6	100.0	100.0	86.4	12.6	13.6
1/2"	43.2	95.6	100.0	69.2	17.2	30.8
3/8"	21.3	82.8	100.0	56.4	12.8	43.6
#4	4.8	16.0	95.7	40.2	16.2	59.8
#8	3.0	4.5	78.7	31.8	8.4	68.2
#16	2.3	2.4	63.0	25.3	6.5	74.7
#30	2.0	2.0	47.9	19.4	5.9	80.6
#50	1.9	1.8	26.9	11.4	8.0	88.6
#100	1.8	1.7	6.1	3.4	7.9	96.6
LBW	1.4	1.3	0.8	1.2	2.3	98.8


*Maximum % Retained must be above the 3/8" sieve.
 *Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation Batch Plant Gradations Aggregate Supplier Gradations

Adjusted WF Initial Production Sample (IPS)

Coarseness Factor:	64	Workability Factor:	32	Adjusted WF	34.3
---------------------------	-----------	----------------------------	-----------	--------------------	-------------

Coarseness Factor:	63
Workability Factor:	35

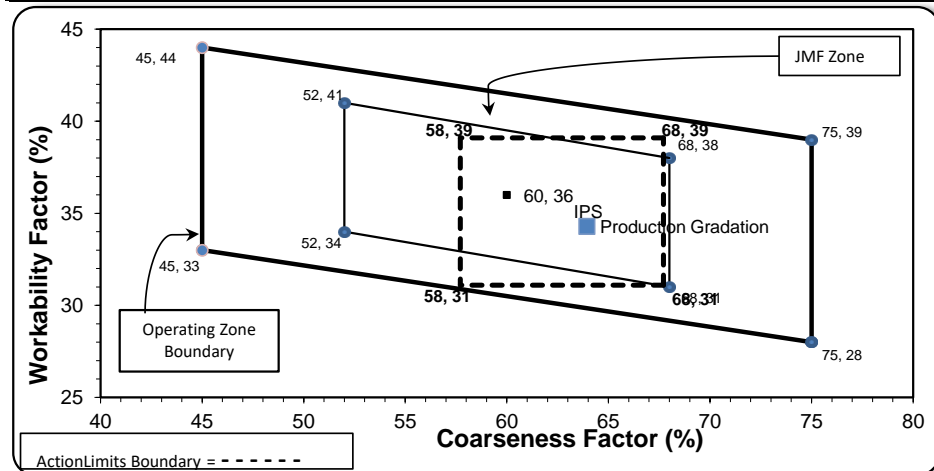

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	100.0	0.0	0.0
3/4"	95.1	4.9	4.9
1/2"	74.6	20.5	25.4
3/8"	59.3	15.3	40.7
#4	42.1	17.2	57.9
#8	35.1	7.1	64.9
#16	29.2	5.9	70.8
#30	21.9	7.3	78.1
#50	9.6	12.4	90.4
#100	2.4	7.2	97.6
LBW	0.9	1.5	99.1

PREPARED BY:
 SM, LLC Technical Service

Approved By:
