

Aggregate Optimization Chart

Production Gradation Report

PLANT #: **P-101**

Sample Date: 11/1/21

Concrete Grade: **DM**

Contractor: _____

Dates Test Represents: 11/2/2021 through 11/8/2021

MDOT No.: _____

Agg. Class	Pit #	Source	Weight (SSD)	ft ³	Specific Gravity	% Contribution
6AA	71-47	Presque Isle	1560	9.54	2.62	53.6
26A	71-47	Presque Isle	200	1.22	2.62	6.9
2NS	75-051	Mid-Michigan	1150	6.93	2.66	39.5
Total Wt			2910	17.69		100.0

<----- Verify this number is 100%



Superior Materials, LLC
 30701 W. 10 Mile Rd.
 Suite 500
 Farmington Hills, MI 48336

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	100.0	100.0	100.0	100.0	0.0	0.0
3/4"	86.9	100.0	100.0	93.0	7.0	7.0
1/2"	40.8	97.3	100.0	68.1	24.9	31.9
3/8"	23.4	88.3	100.0	58.1	9.9	41.9
#4	3.3	13.9	99.3	42.0	16.2	58.0
#8	2.0	4.5	82.9	34.1	7.8	65.9
#16	1.8	2.6	66.5	27.4	6.7	72.6
#30	1.7	2.3	50.2	20.9	6.5	79.1
#50	1.6	2.1	26.7	11.6	9.4	88.4
#100	1.5	1.9	7.2	3.8	7.8	96.2
LBW	1.4	1.8	0.9	1.2	2.6	98.8


*Maximum % Retained must be above the 3/8" sieve.
 *Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation Batch Plant Gradations Aggregate Supplier Gradations

Adjusted WF Initial Production Sample (IPS)

Coarseness Factor:	64	Workability Factor:	34	Adjusted WF	36.6
---------------------------	-----------	----------------------------	-----------	--------------------	-------------

Coarseness Factor:	62
Workability Factor:	35

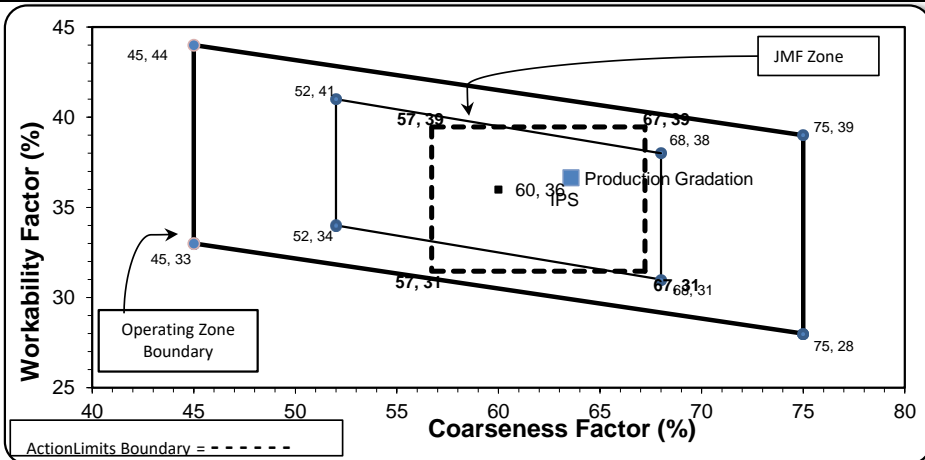

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	100.0	0.0	0.0
3/4"	95.0	5.0	5.0
1/2"	70.5	24.5	29.5
3/8"	60.0	10.5	40.0
#4	44.4	15.6	55.6
#8	35.5	9.0	64.5
#16	28.5	7.0	71.5
#30	21.5	7.0	78.5
#50	10.2	11.3	89.8
#100	3.1	7.1	96.9
LBW	1.3	1.8	98.7

PREPARED BY:
 SM, LLC Technical Service

Approved By:

Aggregate Optimization Chart

PLANT #: **P-102**

Sample Date: 11/1/21 Concrete Grade: DM
 Dates Test Represents: 11/2/2021 through 11/8/2021

Contractor: _____

MDOT No.: _____

Agg. Class	Pit #	Source	Weight (SSD)	ft ³	Specific Gravity	% Contribution
6AA	58-003	Stoneco	1500	8.94	2.69	50.8
26A	58-003	Stoneco	305	1.82	2.69	10.3
2NS	63-114	Highland	1150	6.95	2.65	38.9
Total Wt			2955	17.71		100.0

<----- Verify this number is 100%



Superior Materials, LLC
 30701 W. 10 Mile Rd.
 Suite 500
 Farmington Hills, MI 48336


Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	99.4	100.0	100.0	99.7	0.3	0.3
3/4"	80.7	100.0	100.0	90.2	9.5	9.8
1/2"	43.7	98.4	100.0	71.3	18.9	28.7
3/8"	19.4	83.8	100.0	57.4	13.8	42.6
#4	3.5	12.7	99.8	41.9	15.5	58.1
#8	1.4	2.3	88.0	35.2	6.7	64.8
#16	0.8	1.3	67.0	26.6	8.6	73.4
#30	0.8	1.1	45.2	18.1	8.5	81.9
#50	0.7	0.9	18.4	7.6	10.5	92.4
#100	0.6	0.9	3.7	1.8	5.8	98.2
LBW	0.7	0.6	0.5	0.6	1.2	99.4

*Maximum % Retained must be above the 3/8" sieve.
 *Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation Batch Plant Gradations Aggregate Supplier Gradations Adjusted WF Initial Production Sample (IPS)

Coarseness Factor:	66	Workability Factor:	35	Adjusted WF	37.7
---------------------------	-----------	----------------------------	-----------	--------------------	-------------

Coarseness Factor:	61
Workability Factor:	36

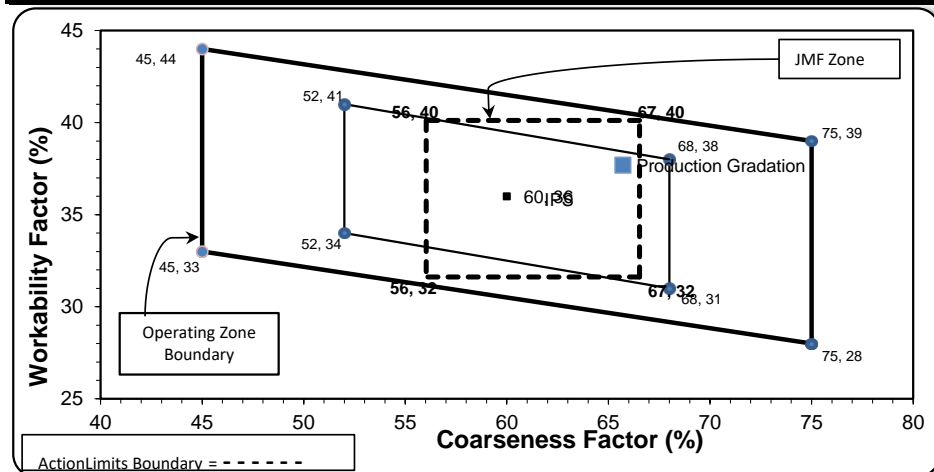

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	99.3	0.7	0.7
3/4"	89.2	10.1	10.8
1/2"	70.7	18.5	29.3
3/8"	60.7	10.0	39.3
#4	44.4	16.3	55.6
#8	35.9	8.5	64.1
#16	27.3	8.6	72.7
#30	19.1	8.2	80.9
#50	7.4	11.7	92.6
#100	1.9	5.6	98.1
LBW	0.7	1.2	99.3

PREPARED BY:
 SM, LLC Technical Service

Approved By:

Aggregate Optimization Chart

PLANT #: **P-32**

Sample Date: 11/1/21 Concrete Grade: DM
 Dates Test Represents: 11/2/2021 through 11/8/2021

Contractor: _____

MDOT No.: _____

Agg. Class	Pit #	Source	Weight (SSD)	ft ³	Specific Gravity	% Contribution
6AA	71-47	Presque Isle	1455	8.90	2.62	50.1
26A	71-47	Presque Isle	300	1.83	2.62	10.3
2NS	95-013	Smelter Bay	1150	6.95	2.65	39.6
Total Wt			2905	17.69		100.0

<----- Verify this number is 100%



Superior Materials, LLC
 30701 W. 10 Mile Rd.
 Suite 500
 Farmington Hills, MI 48336


Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	98.7	100.0	100.0	99.3	0.7	0.7
3/4"	74.1	100.0	100.0	87.0	12.3	13.0
1/2"	35.1	96.4	100.0	67.1	19.9	32.9
3/8"	20.7	84.1	100.0	58.6	8.5	41.4
#4	3.4	15.9	96.3	41.5	17.2	58.5
#8	1.8	4.1	84.2	34.7	6.8	65.3
#16	1.5	2.1	68.2	28.0	6.7	72.0
#30	1.4	1.7	49.2	20.4	7.6	79.6
#50	1.4	1.5	23.8	10.3	10.1	89.7
#100	1.3	1.4	7.4	3.7	6.6	96.3
LBW	1.0	1.0	1.6	1.2	2.5	98.8

*Maximum % Retained must be above the 3/8" sieve.
 *Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation Batch Plant Gradations Aggregate Supplier Gradations Adjusted WF Initial Production Sample (IPS)

Coarseness Factor:	63	Workability Factor:	35	Adjusted WF	37.2
---------------------------	-----------	----------------------------	-----------	--------------------	-------------

Coarseness Factor:	62
Workability Factor:	36

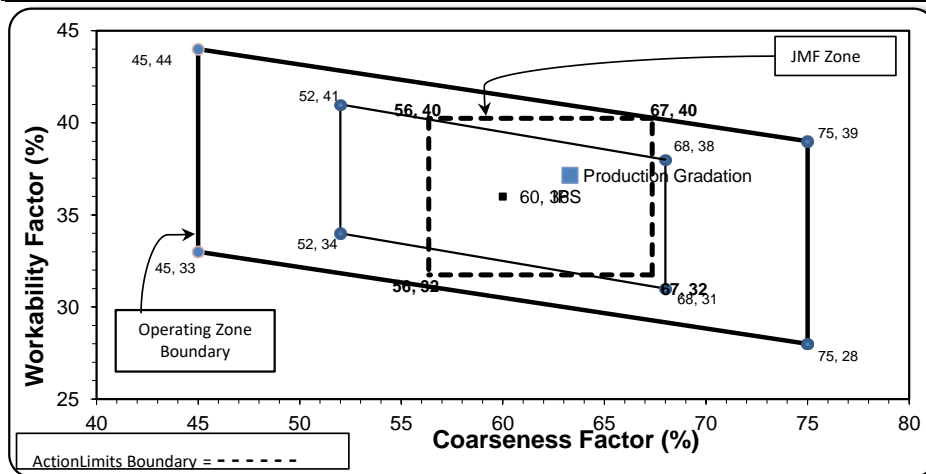

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	100.0	0.0	0.0
3/4"	95.0	5.0	5.0
1/2"	72.3	22.8	27.7
3/8"	60.4	11.8	39.6
#4	42.6	17.8	57.4
#8	36.0	6.6	64.0
#16	29.5	6.5	70.5
#30	20.3	9.2	79.7
#50	9.5	10.8	90.5
#100	3.4	6.1	96.6
LBW	1.3	2.1	98.7

PREPARED BY:
 SM, LLC Technical Service

Approved By:

Aggregate Optimization Chart

PLANT #: **P-35**

Sample Date: 11/1/21 Concrete Grade: **DM**
 Dates Test Represents: 11/2/2021 through 11/8/2021

Contractor: _____

MDOT No.: _____

Agg. Class	Pit #	Source	Weight (SSD)	ft ³	Specific Gravity	% Contribution
6AA	58-003	Stoneco	1555	9.26	2.69	52.6
26A	58-003	Stoneco	300	1.79	2.69	10.2
2NS	81-093	Burmeister	1100	6.65	2.65	37.2
Total Wt			2955	17.70		100.0

<----- Verify this number is 100%



Superior Materials, LLC
 30701 W. 10 Mile Rd.
 Suite 500
 Farmington Hills, MI 48336


Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	99.4	100.0	100.0	99.7	0.3	0.3
3/4"	80.7	100.0	100.0	89.8	9.8	10.2
1/2"	43.7	98.4	100.0	70.2	19.6	29.8
3/8"	19.4	83.8	100.0	55.9	14.3	44.1
#4	3.5	12.7	99.0	40.0	16.0	60.0
#8	1.4	2.3	85.2	32.7	7.3	67.3
#16	0.8	1.3	67.4	25.6	7.0	74.4
#30	0.8	1.1	48.4	18.5	7.1	81.5
#50	0.7	0.9	18.1	7.2	11.4	92.8
#100	0.6	0.9	2.9	1.5	5.7	98.5
LBW	0.7	0.6	0.9	0.8	0.7	99.2

*Maximum % Retained must be above the 3/8" sieve.
 *Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation Batch Plant Gradations Aggregate Supplier Gradations Adjusted WF Initial Production Sample (IPS)

Coarseness Factor:	65	Workability Factor:	33	Adjusted WF	35.2
---------------------------	-----------	----------------------------	-----------	--------------------	-------------

Coarseness Factor:	61
Workability Factor:	36

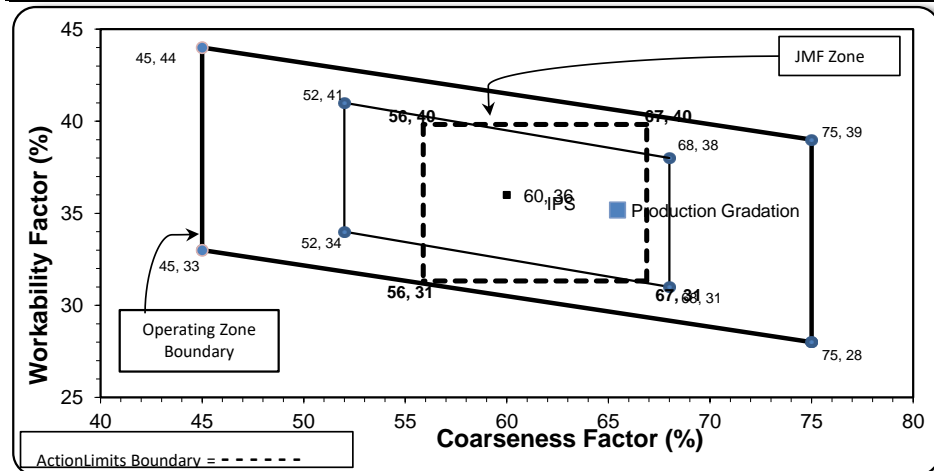

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	99.3	0.7	0.7
3/4"	89.1	10.2	10.9
1/2"	70.5	18.6	29.5
3/8"	60.5	10.0	39.5
#4	44.1	16.4	55.9
#8	35.6	8.5	64.4
#16	27.7	7.9	72.3
#30	20.6	7.1	79.4
#50	8.7	11.8	91.3
#100	1.6	7.1	98.4
LBW	1.1	0.6	98.9

PREPARED BY:
 SM, LLC Technical Service

Approved By:

Aggregate Optimization Chart

PLANT #: **P-36**

Sample Date: 11/1/21 Concrete Grade: **DM**

Dates Test Represents: 11/2/2021 through 11/8/2021

Contractor: _____

MDOT No.: _____



Superior Materials, LLC
 30701 W. 10 Mile Rd.
 Suite 500
 Farmington Hills, MI 48336

Agg. Class	Pit #	Source	Weight (SSD)	ft ³	Specific Gravity	% Contribution
6AA	71-47	Presque Isle	1455	8.90	2.62	50.1
26A	71-47	Presque Isle	350	2.14	2.62	12.0
2NS	63-92	Grange Hall	1100	6.65	2.65	37.9
Total Wt			2905	17.69		100.0

<----- Verify this number is 100%


Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	98.1	100.0	100.0	99.0	1.0	1.0
3/4"	72.0	100.0	100.0	86.0	13.1	14.0
1/2"	30.5	96.4	100.0	64.8	21.2	35.2
3/8"	16.4	84.1	100.0	56.2	8.5	43.8
#4	3.0	15.9	97.5	40.3	15.9	59.7
#8	2.0	4.1	82.9	32.9	7.5	67.1
#16	1.7	2.1	67.8	26.8	6.1	73.2
#30	1.6	1.7	49.9	19.9	6.9	80.1
#50	1.6	1.5	22.4	9.5	10.4	90.5
#100	1.5	1.4	3.1	2.1	7.4	97.9
LBW	1.1	1.0	0.1	0.7	1.4	99.3

*Maximum % Retained must be above the 3/8" sieve.
 *Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation Batch Plant Gradations Aggregate Supplier Gradations Adjusted WF Initial Production Sample (IPS)

Coarseness Factor:	65	Workability Factor:	33	Adjusted WF	35.4
---------------------------	-----------	----------------------------	-----------	--------------------	-------------

Coarseness Factor:	63
Workability Factor:	35

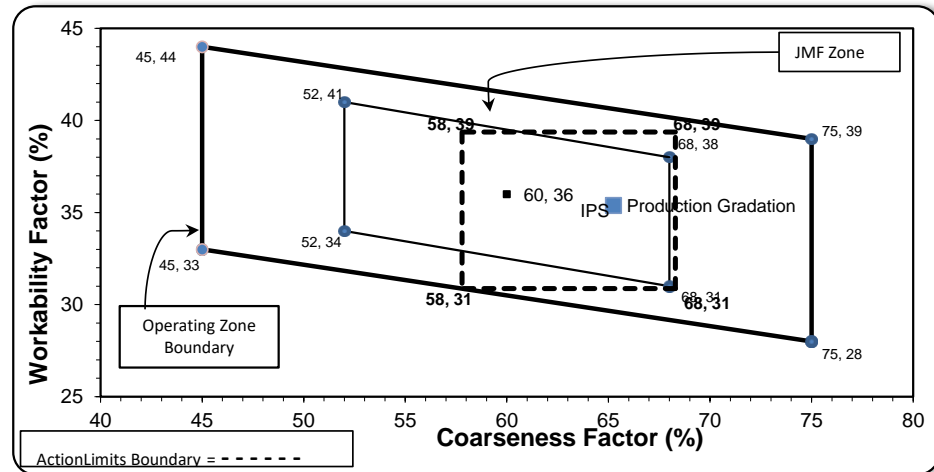

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	99.1	0.9	0.9
3/4"	90.3	8.8	9.7
1/2"	69.2	21.1	30.8
3/8"	59.1	10.1	40.9
#4	41.8	17.3	58.2
#8	35.1	6.6	64.9
#16	28.5	6.6	71.5
#30	21.2	7.3	78.8
#50	8.7	12.5	91.3
#100	1.8	7.0	98.2
LBW	0.7	1.0	99.3

PREPARED BY:
 SM, LLC Technical Service

Approved By:

Aggregate Optimization Chart

PLANT #: **P-39**

Sample Date: 11/1/21 Concrete Grade: DM
 Dates Test Represents: 11/2/2021 through 11/8/2021

Contractor: _____

MDOT No.: _____

Agg. Class	Pit #	Source	Weight (SSD)	ft ³	Specific Gravity	% Contribution
6AA	71-47	Presque Isle	1605	9.82	2.62	55.2
26A	71-47	Presque Isle	200	1.22	2.62	6.9
2NS	44-051	Krake Willis Rd	1100	6.65	2.65	37.9
Total Wt			2905	17.69		100.0

<----- Verify this number is 100%

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	100.0	100.0	100.0	100.0	0.0	0.0
3/4"	86.9	100.0	100.0	92.8	7.2	7.2
1/2"	40.8	97.3	100.0	67.1	25.7	32.9
3/8"	23.4	88.3	100.0	56.9	10.2	43.1
#4	3.3	13.9	96.8	39.4	17.4	60.6
#8	2.0	4.5	80.1	31.7	7.7	68.3
#16	1.8	2.6	64.5	25.6	6.1	74.4
#30	1.7	2.3	48.5	19.5	6.1	80.5
#50	1.6	2.1	25.4	10.6	8.8	89.4
#100	1.5	1.9	7.8	3.9	6.7	96.1
LBW	1.4	1.8	1.2	1.4	2.6	98.6

*Maximum % Retained must be above the 3/8" sieve.
 *Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.




Superior Materials, LLC
 30701 W. 10 Mile Rd.
 Suite 500
 Farmington Hills, MI 48336

Production Gradation Batch Plant Gradations Aggregate Supplier Gradations

Adjusted WF Initial Production Sample (IPS)

Coarseness Factor:	63	Workability Factor:	32	Adjusted WF	34.2
---------------------------	-----------	----------------------------	-----------	--------------------	-------------

Coarseness Factor:	63
Workability Factor:	36

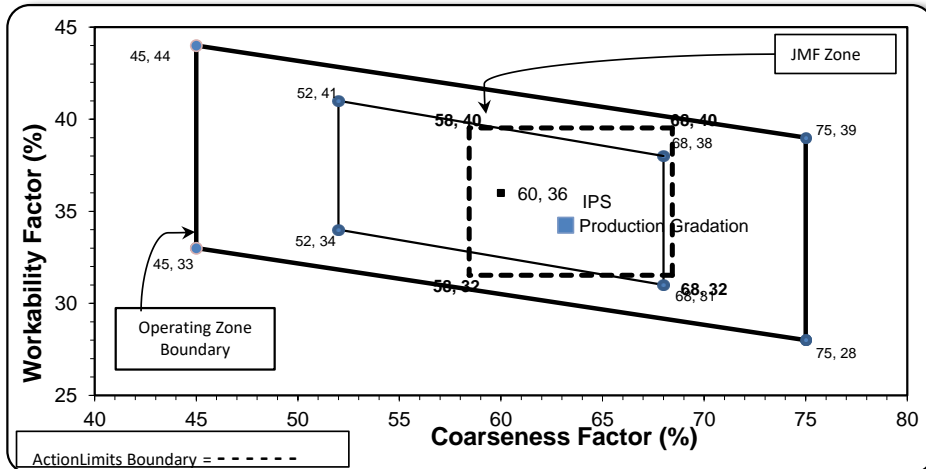

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	100.0	0.0	0.0
3/4"	89.7	10.3	10.3
1/2"	70.3	19.4	29.7
3/8"	59.1	11.2	40.9
#4	42.8	16.3	57.2
#8	35.5	7.3	64.5
#16	29.0	6.5	71.0
#30	21.2	7.7	78.8
#50	9.8	11.5	90.2
#100	3.7	6.1	96.3
LBW	1.2	2.5	98.8

PREPARED BY:
 SM, LLC Technical Service

Approved By:

Aggregate Optimization Chart

PLANT #: **P-02**

Sample Date: 11/1/21 Concrete Grade: DM
 Dates Test Represents: 11/2/2021 through 11/8/2021

Contractor: _____

MDOT No.: _____

Agg. Class	Pit #	Source	Weight (SSD)	ft ³	Specific Gravity	% Contribution
6AA	71-47	Presque Isle	1505	9.21	2.62	51.8
26A	71-47	Presque Isle	300	1.83	2.62	10.3
2NS	63-115	Ray Rd	1100	6.65	2.65	37.9
Total Wt			2905	17.69		100.0

<----- Verify this number is 100%



Superior Materials, LLC
 30701 W. 10 Mile Rd.
 Suite 500
 Farmington Hills, MI 48336


Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	98.1	100.0	100.0	99.0	1.0	1.0
3/4"	72.0	100.0	100.0	85.5	13.5	14.5
1/2"	30.5	96.4	100.0	63.6	21.9	36.4
3/8"	16.4	84.1	100.0	55.0	8.6	45.0
#4	3.0	15.9	96.2	39.6	15.4	60.4
#8	2.0	4.1	80.1	31.8	7.8	68.2
#16	1.7	2.1	65.1	25.7	6.0	74.3
#30	1.6	1.7	49.2	19.6	6.1	80.4
#50	1.6	1.5	26.2	10.9	8.7	89.1
#100	1.5	1.4	6.2	3.3	7.6	96.7
LBW	1.1	1.0	1.0	1.1	2.2	98.9

*Maximum % Retained must be above the 3/8" sieve.
 *Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation Batch Plant Gradations Aggregate Supplier Gradations Adjusted WF Initial Production Sample (IPS)

Coarseness Factor:	66	Workability Factor:	32	Adjusted WF	34.3
---------------------------	-----------	----------------------------	-----------	--------------------	-------------

Coarseness Factor:	63
Workability Factor:	35

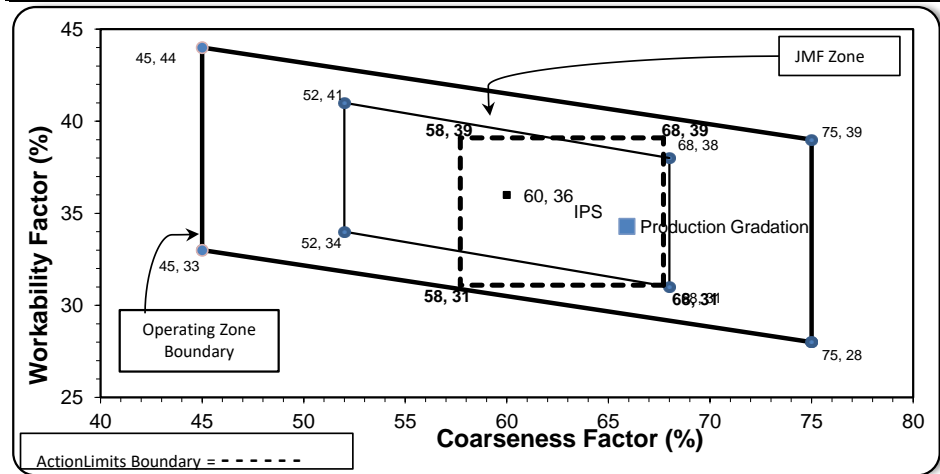

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	100.0	0.0	0.0
3/4"	95.1	4.9	4.9
1/2"	74.6	20.5	25.4
3/8"	59.3	15.3	40.7
#4	42.1	17.2	57.9
#8	35.1	7.1	64.9
#16	29.2	5.9	70.8
#30	21.9	7.3	78.1
#50	9.6	12.4	90.4
#100	2.4	7.2	97.6
LBW	0.9	1.5	99.1

PREPARED BY:
 SM, LLC Technical Service

Approved By:
