

Aggregate Optimization Chart

PLANT #: **P-102**

Sample Date: 11/22/21

Concrete Grade: **S2M**

Contractor: _____

Dates Test Represents: 11/23/2021 through 11/29/2021

MDOT No.: _____

Agg. Class	Pit #	Source	Weight (SSD)	ft ³	Specific Gravity	% Contribution
6AA	58-003	Stoneco	1600	9.53	2.69	51.6
26A	58-003	Stoneco	290	1.73	2.69	9.4
2NS	63-114	Highland	1210	7.32	2.65	39.0
Total Wt			3100	18.58		100.0

<----- Verify this number is 100%




Superior Materials, LLC
 30701 W. 10 Mile Rd.
 Suite 500
 Farmington Hills, MI 48336

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	100.0	100.0	100.0	100.0	0.0	0.0
3/4"	89.3	100.0	100.0	94.5	5.5	5.5
1/2"	47.0	99.8	100.0	72.6	21.9	27.4
3/8"	24.2	86.6	100.0	59.6	13.0	40.4
#4	4.3	16.0	99.7	42.6	17.0	57.4
#8	1.5	5.3	86.2	34.9	7.7	65.1
#16	1.3	2.8	65.2	26.4	8.5	73.6
#30	1.1	1.9	44.7	18.2	8.2	81.8
#50	1.0	1.6	18.7	8.0	10.2	92.0
#100	0.9	1.5	3.7	2.0	5.9	98.0
LBW	0.7	1.3	0.6	0.7	1.3	99.3

*Maximum % Retained must be above the 3/8" sieve.
 *Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation Batch Plant Gradations Aggregate Supplier Gradations

Coarseness Factor:	62	Workability Factor:	35
---------------------------	-----------	----------------------------	-----------

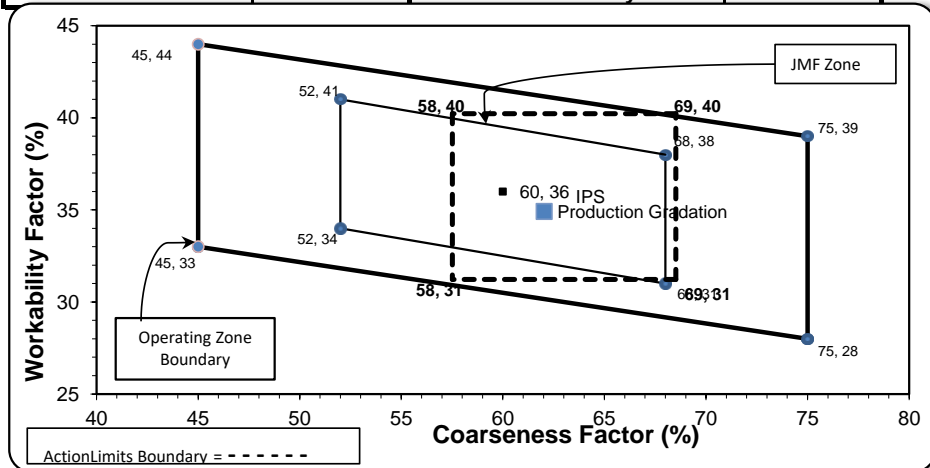

Initial Production Sample (IPS)

Coarseness Factor:	63		
Workability Factor:	36		
Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	99.2	0.8	0.8
3/4"	90.9	8.3	9.1
1/2"	71.3	19.6	28.7
3/8"	59.5	11.8	40.5
#4	43.8	15.7	56.2
#8	35.7	8.1	64.3
#16	27.0	8.7	73.0
#30	18.6	8.4	81.4
#50	6.8	11.8	93.2
#100	1.4	5.4	98.6
LBW	0.6	0.8	99.4

PREPARED BY:
 SM, LLC Technical Service

Approved By:

Aggregate Optimization Chart

PLANT #: **P-32**

Sample Date: 11/22/21

Concrete Grade: **S2M**

Contractor: _____

Dates Test Represents: 11/23/2021 through 11/29/2021

MDOT No.: _____

Agg. Class	Pit #	Source	Weight (SSD)	ft ³	Specific Gravity	% Contribution
6AA	71-47	Presque Isle	1550	9.48	2.62	50.8
26A	71-47	Presque Isle	270	1.65	2.62	8.9
2NS	95-013	Smelter Bay	1230	7.44	2.65	40.3
Total Wt			3050	18.57		100.0

<----- Verify this number is 100%




Superior Materials, LLC
 30701 W. 10 Mile Rd.
 Suite 500
 Farmington Hills, MI 48336

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	95.0	100.0	100.0	97.5	2.5	2.5
3/4"	76.2	100.0	100.0	87.9	9.6	12.1
1/2"	33.3	95.0	100.0	65.7	22.2	34.3
3/8"	19.5	82.1	100.0	57.5	8.2	42.5
#4	3.7	16.7	95.7	42.0	15.6	58.0
#8	1.8	4.7	82.3	34.5	7.4	65.5
#16	1.5	2.4	67.3	28.1	6.4	71.9
#30	1.4	1.9	48.8	20.6	7.6	79.4
#50	1.4	1.7	25.5	11.1	9.4	88.9
#100	1.3	1.5	8.1	4.1	7.1	95.9
LBW	0.9	1.1	1.4	1.1	2.9	98.9

*Maximum % Retained must be above the 3/8" sieve.
 *Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation Batch Plant Gradations Aggregate Supplier Gradations

Coarseness Factor:	65	Workability Factor:	35
---------------------------	-----------	----------------------------	-----------

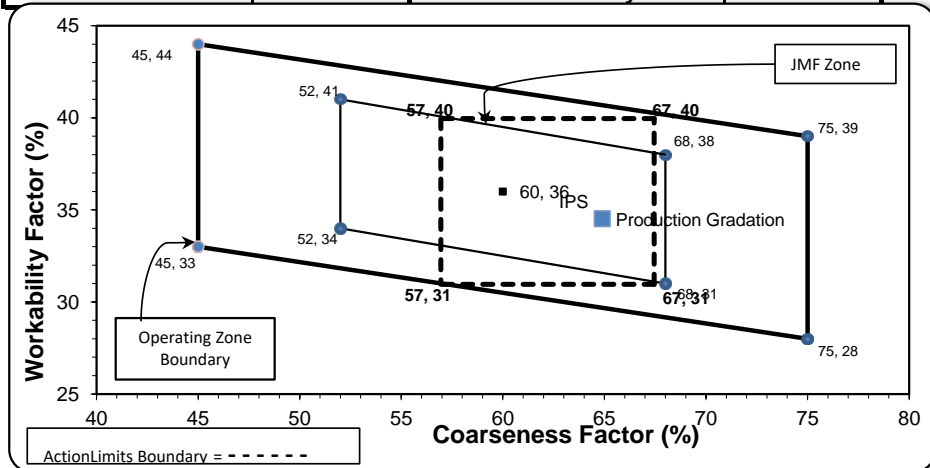

Initial Production Sample (IPS)

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	100.0	0.0	0.0
3/4"	94.0	6.0	6.0
1/2"	70.2	23.7	29.8
3/8"	59.9	10.4	40.1
#4	42.7	17.2	57.3
#8	35.5	7.2	64.5
#16	28.4	7.0	71.6
#30	19.2	9.2	80.8
#50	8.9	10.3	91.1
#100	3.1	5.9	96.9
LBW	1.4	1.7	98.6

PREPARED BY:
 SM, LLC Technical Service

Approved By:

Aggregate Optimization Chart

PLANT #: **P-35**

Sample Date: 11/22/21

Concrete Grade: **S2M**

Contractor: _____

Dates Test Represents: 11/23/2021 through 11/29/2021

MDOT No.: _____

Agg. Class	Pit #	Source	Weight (SSD)	ft ³	Specific Gravity	% Contribution
6AA	58-003	Stoneco	1600	9.53	2.69	51.6
26A	58-003	Stoneco	300	1.79	2.69	9.7
2NS	81-093	Burmeister	1200	7.26	2.65	38.7
Total Wt			3100	18.58		100.0

<----- Verify this number is 100%




Superior Materials, LLC
 30701 W. 10 Mile Rd.
 Suite 500
 Farmington Hills, MI 48336

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	100.0	100.0	100.0	100.0	0.0	0.0
3/4"	89.3	100.0	100.0	94.5	5.5	5.5
1/2"	47.0	99.8	100.0	72.6	21.9	27.4
3/8"	24.2	86.6	100.0	59.6	13.0	40.4
#4	4.3	16.0	98.7	42.0	17.6	58.0
#8	1.5	5.3	85.2	34.3	7.7	65.7
#16	1.3	2.8	67.0	26.9	7.4	73.1
#30	1.1	1.9	46.6	18.8	8.1	81.2
#50	1.0	1.6	16.3	7.0	11.8	93.0
#100	0.9	1.5	2.8	1.7	5.3	98.3
LBW	0.7	1.3	1.0	0.9	0.8	99.1

*Maximum % Retained must be above the 3/8" sieve.
 *Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation Batch Plant Gradations Aggregate Supplier Gradations

Coarseness Factor: 61 **Workability Factor:** 34

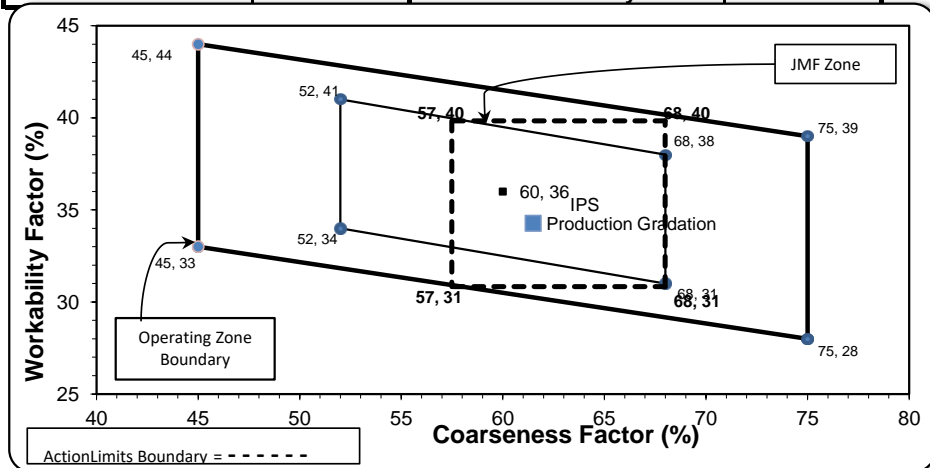

Initial Production Sample (IPS)

Coarseness Factor: 63
Workability Factor: 35

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	99.2	0.8	0.8
3/4"	90.9	8.3	9.1
1/2"	71.3	19.6	28.7
3/8"	59.4	11.9	40.6
#4	43.0	16.5	57.0
#8	35.3	7.6	64.7
#16	28.2	7.1	71.8
#30	21.6	6.6	78.4
#50	9.1	12.5	90.9
#100	1.7	7.4	98.3
LBW	1.1	0.6	98.9

PREPARED BY:
 SM, LLC Technical Service

Approved By:

Aggregate Optimization Chart

PLANT #: **P-02**

Sample Date: 11/22/21

Concrete Grade: **S2M**

Contractor: _____

Dates Test Represents: 11/23/2021 through 11/29/2021

MDOT No.: _____

Agg. Class	Pit #	Source	Weight (SSD)	ft ³	Specific Gravity	% Contribution
6AA	71-47	Presque Isle	1450	8.87	2.62	47.5
26A	71-47	Presque Isle	350	2.14	2.62	11.5
2NS	63-115	Ray Rd	1250	7.56	2.65	41.0
Total Wt			3050	18.57		100.0

<----- Verify this number is 100%




Superior Materials, LLC
 30701 W. 10 Mile Rd.
 Suite 500
 Farmington Hills, MI 48336

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	97.7	100.0	100.0	98.9	1.1	1.1
3/4"	65.1	100.0	100.0	83.4	15.5	16.6
1/2"	30.0	95.0	100.0	66.1	17.3	33.9
3/8"	11.1	82.1	100.0	55.7	10.5	44.3
#4	2.6	16.7	96.6	42.7	12.9	57.3
#8	2.0	4.7	78.7	33.7	9.0	66.3
#16	1.9	2.4	61.7	26.5	7.3	73.5
#30	1.9	1.9	46.1	20.0	6.5	80.0
#50	1.8	1.7	27.8	12.4	7.6	87.6
#100	1.7	1.5	6.4	3.6	8.8	96.4
LBW	1.0	1.1	0.9	1.0	2.6	99.0

*Maximum % Retained must be above the 3/8" sieve.
 *Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation Batch Plant Gradations Aggregate Supplier Gradations

Coarseness Factor: 67 **Workability Factor:** 34

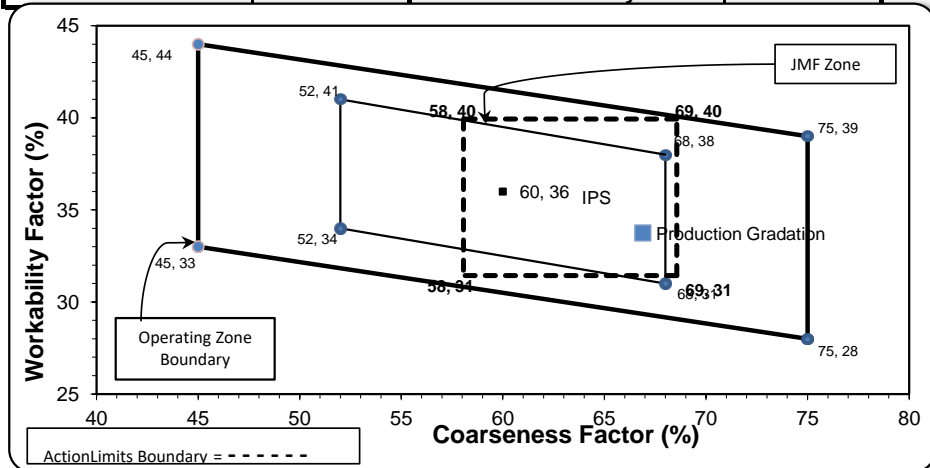

Initial Production Sample (IPS)

Coarseness Factor: 63
Workability Factor: 36

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	100.0	0.0	0.0
3/4"	95.6	4.4	4.4
1/2"	73.1	22.6	26.9
3/8"	59.3	13.8	40.7
#4	42.8	16.5	57.2
#8	35.7	7.1	64.3
#16	28.9	6.8	71.1
#30	20.7	8.2	79.3
#50	9.9	10.8	90.1
#100	2.1	7.8	97.9
LBW	0.9	1.2	99.1

PREPARED BY:
 SM, LLC Technical Service

Approved By:
