

# Aggregate Optimization Chart

## Production Gradation Report

**PLANT #:** **P-101**

Sample Date: 1/17/22

Concrete Grade: **DM**

Contractor: \_\_\_\_\_

Dates Test Represents: 1/18/2022 through 1/24/2022

MDOT No.: \_\_\_\_\_

Agg. Class	Pit #	Source	Weight (SSD)	ft <sup>3</sup>	Specific Gravity	% Contribution
6AA	71-47	Presque Isle	1500	9.17	2.62	51.5
26A	71-47	Presque Isle	260	1.59	2.62	8.9
2NS	75-051	Mid-Michigan	1150	6.93	2.66	39.5
<b>Total Wt</b>			<b>2910</b>	<b>17.69</b>		<b>100.0</b>

<----- Verify this number is 100%



**Superior Materials, LLC**  
 30701 W. 10 Mile Rd.  
 Suite 500  
 Farmington Hills, MI 48336

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	95.8	100.0	100.0	97.8	2.2	2.2
3/4"	76.3	100.0	100.0	87.8	10.1	12.2
1/2"	35.6	97.3	100.0	66.6	21.2	33.4
3/8"	18.1	88.2	100.0	56.7	9.8	43.3
#4	2.3	19.5	98.5	41.9	14.9	58.1
#8	1.6	4.6	83.3	34.2	7.7	65.8
#16	1.4	2.0	68.3	27.9	6.3	72.1
#30	1.4	1.6	53.3	21.9	6.0	78.1
#50	1.3	1.5	29.2	12.3	9.6	87.7
#100	1.3	1.4	7.3	3.7	8.7	96.3
LBW	1.2	1.3	0.6	1.0	2.7	99.0


\*Maximum % Retained must be above the 3/8" sieve.  
 \*Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation  Batch Plant Gradations  Aggregate Supplier Gradations

Adjusted WF Initial Production Sample (IPS)

<b>Coarseness Factor:</b>	<b>66</b>	<b>Workability Factor:</b>	<b>34</b>	<b>Adjusted WF</b>	<b>36.7</b>
---------------------------	-----------	----------------------------	-----------	--------------------	-------------

<b>Coarseness Factor:</b>	<b>62</b>
<b>Workability Factor:</b>	<b>35</b>

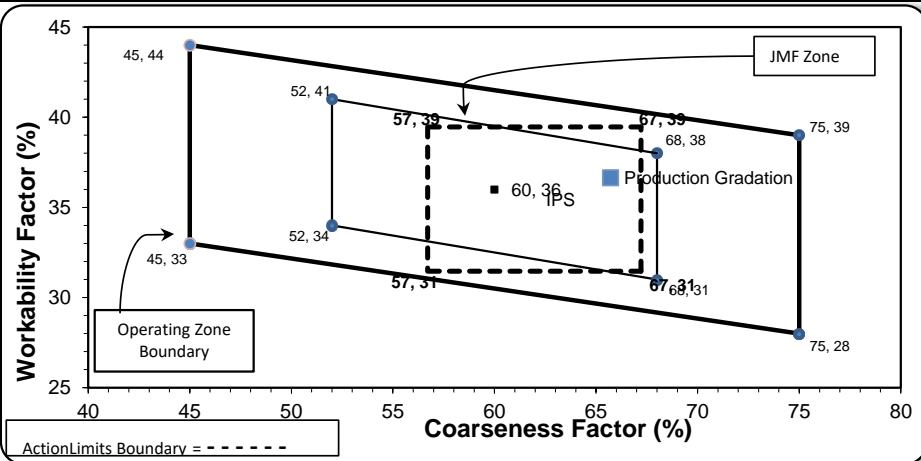

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	100.0	0.0	0.0
3/4"	95.0	5.0	5.0
1/2"	70.5	24.5	29.5
3/8"	60.0	10.5	40.0
#4	44.4	15.6	55.6
#8	35.5	9.0	64.5
#16	28.5	7.0	71.5
#30	21.5	7.0	78.5
#50	10.2	11.3	89.8
#100	3.1	7.1	96.9
LBW	1.3	1.8	98.7

PREPARED BY:  
 SM, LLC Technical Service

Approved By:

# Aggregate Optimization Chart

**PLANT #:** **P-102**

Sample Date: 1/17/22

Concrete Grade: **DM**

Contractor: \_\_\_\_\_

Dates Test Represents: 1/18/2022 through 1/24/2022

MDOT No.: \_\_\_\_\_

Agg. Class	Pit #	Source	Weight (SSD)	ft <sup>3</sup>	Specific Gravity	% Contribution
6AA	58-003	Stoneco	1400	8.34	2.69	47.4
26A	58-003	Stoneco	405	2.41	2.69	13.7
2NS	63-114	Highland	1150	6.95	2.65	38.9
<b>Total Wt</b>			<b>2955</b>	<b>17.71</b>		<b>100.0</b>

<----- Verify this number is 100%



**Superior Materials, LLC**  
 30701 W. 10 Mile Rd.  
 Suite 500  
 Farmington Hills, MI 48336

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	100.0	100.0	100.0	100.0	0.0	0.0
3/4"	81.4	100.0	100.0	91.2	8.8	8.8
1/2"	44.3	98.9	100.0	73.5	17.7	26.5
3/8"	19.2	70.9	100.0	57.7	15.7	42.3
#4	1.8	9.3	99.4	40.8	16.9	59.2
#8	1.0	3.4	87.6	35.0	5.8	65.0
#16	0.8	2.1	69.9	27.9	7.2	72.1
#30	0.6	1.8	47.5	19.0	8.9	81.0
#50	0.5	1.7	18.9	7.8	11.2	92.2
#100	0.4	1.5	2.8	1.5	6.3	98.5
LBW	0.3	1.4	0.4	0.5	1.0	99.5


\*Maximum % Retained must be above the 3/8" sieve.  
 \*Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation  Batch Plant Gradations  Aggregate Supplier Gradations

Adjusted WF Initial Production Sample (IPS)

<b>Coarseness Factor:</b>	<b>65</b>	<b>Workability Factor:</b>	<b>35</b>	<b>37.5</b>
---------------------------	-----------	----------------------------	-----------	-------------

<b>Coarseness Factor:</b>	<b>61</b>
<b>Workability Factor:</b>	<b>36</b>

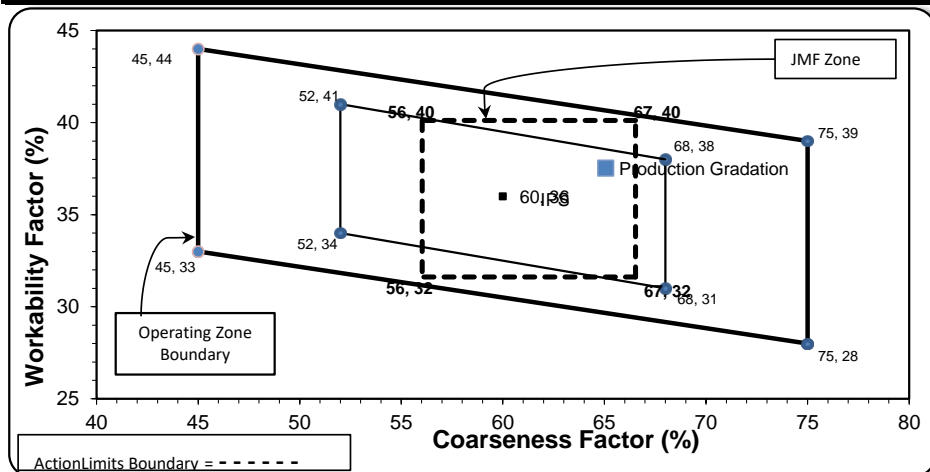

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	99.3	0.7	0.7
3/4"	89.2	10.1	10.8
1/2"	70.7	18.5	29.3
3/8"	60.7	10.0	39.3
#4	44.4	16.3	55.6
#8	35.9	8.5	64.1
#16	27.3	8.6	72.7
#30	19.1	8.2	80.9
#50	7.4	11.7	92.6
#100	1.9	5.6	98.1
LBW	0.7	1.2	99.3

PREPARED BY:  
 SM, LLC Technical Service

Approved By:

# Aggregate Optimization Chart

**PLANT #:** **P-32**

Sample Date: 1/17/22

Concrete Grade: **DM**

Contractor: \_\_\_\_\_

Dates Test Represents: 1/18/2022 through 1/24/2022

MDOT No.: \_\_\_\_\_

Agg. Class	Pit #	Source	Weight (SSD)	ft <sup>3</sup>	Specific Gravity	% Contribution
6AA	71-47	Presque Isle	1555	9.51	2.62	53.5
26A	71-47	Presque Isle	200	1.22	2.62	6.9
2NS	95-013	Smelter Bay	1150	6.95	2.65	39.6
<b>Total Wt</b>			<b>2905</b>	<b>17.69</b>		<b>100.0</b>

<----- Verify this number is 100%



**Superior Materials, LLC**  
 30701 W. 10 Mile Rd.  
 Suite 500  
 Farmington Hills, MI 48336

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	96.0	100.0	100.0	97.9	2.1	2.1
3/4"	75.0	100.0	100.0	86.6	11.2	13.4
1/2"	38.5	98.5	100.0	67.0	19.6	33.0
3/8"	24.5	89.7	100.0	58.9	8.1	41.1
#4	6.3	29.8	96.8	43.7	15.1	56.3
#8	3.0	9.4	84.5	35.7	8.0	64.3
#16	2.5	4.5	68.5	28.8	6.9	71.2
#30	2.3	3.3	49.1	20.9	7.9	79.1
#50	2.1	2.9	22.8	10.3	10.5	89.7
#100	1.9	2.6	6.6	3.8	6.5	96.2
LBW	1.5	2.0	1.7	1.6	2.2	98.4


\*Maximum % Retained must be above the 3/8" sieve.  
 \*Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation  Batch Plant Gradations  Aggregate Supplier Gradations

Adjusted WF Initial Production Sample (IPS)

<b>Coarseness Factor:</b>	<b>64</b>	<b>Workability Factor:</b>	<b>36</b>	<b>Adjusted WF</b>	<b>38.2</b>
---------------------------	-----------	----------------------------	-----------	--------------------	-------------

<b>Coarseness Factor:</b>	<b>62</b>
<b>Workability Factor:</b>	<b>36</b>

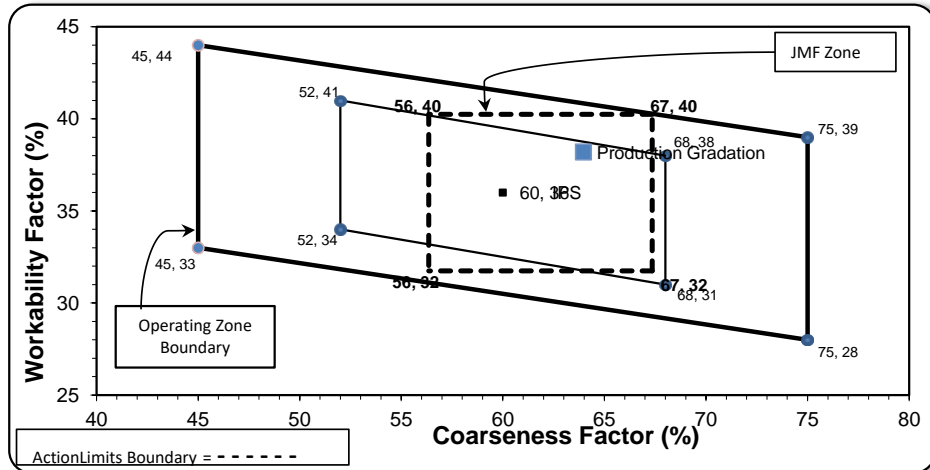

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	100.0	0.0	0.0
3/4"	95.0	5.0	5.0
1/2"	72.3	22.8	27.7
3/8"	60.4	11.8	39.6
#4	42.6	17.8	57.4
#8	36.0	6.6	64.0
#16	29.5	6.5	70.5
#30	20.3	9.2	79.7
#50	9.5	10.8	90.5
#100	3.4	6.1	96.6
LBW	1.3	2.1	98.7

PREPARED BY:  
 SM, LLC Technical Service

Approved By:

# Aggregate Optimization Chart

**PLANT #:** **P-35**

Sample Date: 1/17/22

Concrete Grade: **DM**

Contractor: \_\_\_\_\_

Dates Test Represents: 1/18/2022 through 1/24/2022

MDOT No.: \_\_\_\_\_

Agg. Class	Pit #	Source	Weight (SSD)	ft <sup>3</sup>	Specific Gravity	% Contribution
6AA	58-003	Stoneco	1450	8.64	2.69	49.1
26A	58-003	Stoneco	405	2.41	2.69	13.7
2NS	81-093	Burmeister	1100	6.65	2.65	37.2
<b>Total Wt</b>			<b>2955</b>	<b>17.70</b>		<b>100.0</b>

<----- Verify this number is 100%



**Superior Materials, LLC**  
 30701 W. 10 Mile Rd.  
 Suite 500  
 Farmington Hills, MI 48336

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	100.0	100.0	100.0	100.0	0.0	0.0
3/4"	81.4	100.0	100.0	90.9	9.1	9.1
1/2"	44.3	98.9	100.0	72.5	18.4	27.5
3/8"	19.2	70.9	100.0	56.4	16.2	43.6
#4	1.8	9.3	97.7	38.5	17.8	61.5
#8	1.0	3.4	86.0	33.0	5.6	67.0
#16	0.8	2.1	70.7	27.0	6.0	73.0
#30	0.6	1.8	52.4	20.0	7.0	80.0
#50	0.5	1.7	22.0	8.7	11.4	91.3
#100	0.4	1.5	4.5	2.1	6.6	97.9
LBW	0.3	1.4	1.7	1.0	1.1	99.0


\*Maximum % Retained must be above the 3/8" sieve.  
 \*Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation  Batch Plant Gradations  Aggregate Supplier Gradations

Adjusted WF Initial Production Sample (IPS)

<b>Coarseness Factor:</b>	<b>65</b>	<b>Workability Factor:</b>	<b>33</b>	<b>Adjusted WF</b>	<b>35.5</b>
---------------------------	-----------	----------------------------	-----------	--------------------	-------------

<b>Coarseness Factor:</b>	<b>61</b>
<b>Workability Factor:</b>	<b>36</b>

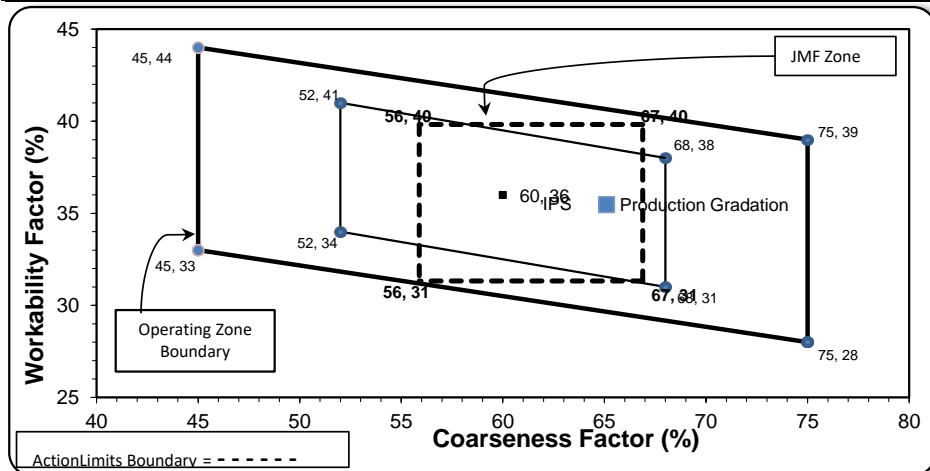

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	99.3	0.7	0.7
3/4"	89.1	10.2	10.9
1/2"	70.5	18.6	29.5
3/8"	60.5	10.0	39.5
#4	44.1	16.4	55.9
#8	35.6	8.5	64.4
#16	27.7	7.9	72.3
#30	20.6	7.1	79.4
#50	8.7	11.8	91.3
#100	1.6	7.1	98.4
LBW	1.1	0.6	98.9

PREPARED BY:  
 SM, LLC Technical Service

Approved By:

# Aggregate Optimization Chart

**PLANT #:** **P-39**

Sample Date: 1/17/22

Concrete Grade: **DM**

Contractor: \_\_\_\_\_

Dates Test Represents: 1/18/2022 through 1/24/2022

MDOT No.: \_\_\_\_\_

Agg. Class	Pit #	Source	Weight (SSD)	ft <sup>3</sup>	Specific Gravity	% Contribution
6AA	71-47	Presque Isle	1605	9.82	2.62	55.2
26A	71-47	Presque Isle	200	1.22	2.62	6.9
2NS	63-92	Grange Hall	1100	6.65	2.65	37.9
<b>Total Wt</b>			<b>2905</b>	<b>17.69</b>		<b>100.0</b>

<----- Verify this number is 100%



**Superior Materials, LLC**  
 30701 W. 10 Mile Rd.  
 Suite 500  
 Farmington Hills, MI 48336

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	95.8	100.0	100.0	97.7	2.3	2.3
3/4"	76.3	100.0	100.0	86.9	10.8	13.1
1/2"	35.6	97.3	100.0	64.2	22.7	35.8
3/8"	18.1	88.2	100.0	53.9	10.3	46.1
#4	2.3	19.5	97.5	39.5	14.4	60.5
#8	1.6	4.6	82.1	32.3	7.2	67.7
#16	1.4	2.0	66.8	26.2	6.1	73.8
#30	1.4	1.6	49.8	19.7	6.5	80.3
#50	1.3	1.5	25.4	10.4	9.3	89.6
#100	1.3	1.4	4.2	2.4	8.0	97.6
LBW	1.2	1.3	0.4	0.9	1.5	99.1


\*Maximum % Retained must be above the 3/8" sieve.  
 \*Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation  Batch Plant Gradations  Aggregate Supplier Gradations

Adjusted WF Initial Production Sample (IPS)

<b>Coarseness Factor:</b>	<b>68</b>	<b>Workability Factor:</b>	<b>32</b>	<b>Adjusted WF</b>	<b>34.8</b>
---------------------------	-----------	----------------------------	-----------	--------------------	-------------

<b>Coarseness Factor:</b>	<b>63</b>
<b>Workability Factor:</b>	<b>36</b>

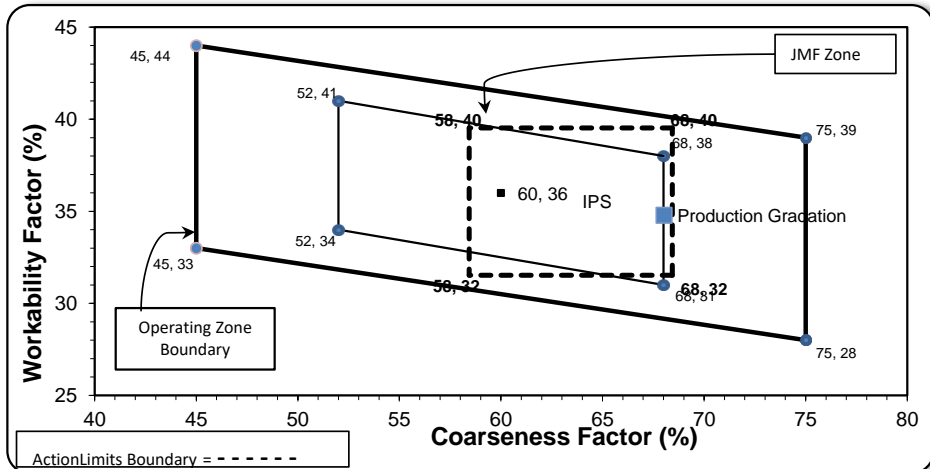

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	100.0	0.0	0.0
3/4"	89.7	10.3	10.3
1/2"	70.3	19.4	29.7
3/8"	59.1	11.2	40.9
#4	42.8	16.3	57.2
#8	35.5	7.3	64.5
#16	29.0	6.5	71.0
#30	21.2	7.7	78.8
#50	9.8	11.5	90.2
#100	3.7	6.1	96.3
LBW	1.2	2.5	98.8

PREPARED BY:  
 SM, LLC Technical Service

Approved By:

# Aggregate Optimization Chart

**PLANT #:** **P-02**

Sample Date: 1/17/22

Concrete Grade: **DM**

Contractor: \_\_\_\_\_

Dates Test Represents: 1/18/2022 through 1/24/2022

MDOT No.: \_\_\_\_\_

Agg. Class	Pit #	Source	Weight (SSD)	ft <sup>3</sup>	Specific Gravity	% Contribution
6AA	71-47	Presque Isle	1605	9.82	2.62	55.2
26A	71-47	Presque Isle	200	1.22	2.62	6.9
2NS	63-115	Ray Rd	1100	6.65	2.65	37.9
<b>Total Wt</b>			<b>2905</b>	<b>17.69</b>		<b>100.0</b>

<----- Verify this number is 100%



**Superior Materials, LLC**  
 30701 W. 10 Mile Rd.  
 Suite 500  
 Farmington Hills, MI 48336

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	96.5	100.0	100.0	98.1	1.9	1.9
3/4"	76.6	100.0	100.0	87.1	11.0	12.9
1/2"	39.7	98.5	100.0	66.6	20.5	33.4
3/8"	20.9	89.7	100.0	55.6	11.0	44.4
#4	3.6	29.8	97.3	40.9	14.7	59.1
#8	2.2	9.4	79.9	32.1	8.8	67.9
#16	2.0	4.5	63.9	25.6	6.5	74.4
#30	1.9	3.3	46.8	19.0	6.6	81.0
#50	1.8	2.9	25.6	10.9	8.1	89.1
#100	1.7	2.6	5.1	3.0	7.8	97.0
LBW	1.3	2.0	0.9	1.2	1.9	98.8


\*Maximum % Retained must be above the 3/8" sieve.  
 \*Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation  Batch Plant Gradations  Aggregate Supplier Gradations

Adjusted WF Initial Production Sample (IPS)

<b>Coarseness Factor:</b>	<b>65</b>	<b>Workability Factor:</b>	<b>32</b>	<b>34.6</b>
---------------------------	-----------	----------------------------	-----------	-------------

<b>Coarseness Factor:</b>	<b>63</b>
<b>Workability Factor:</b>	<b>35</b>

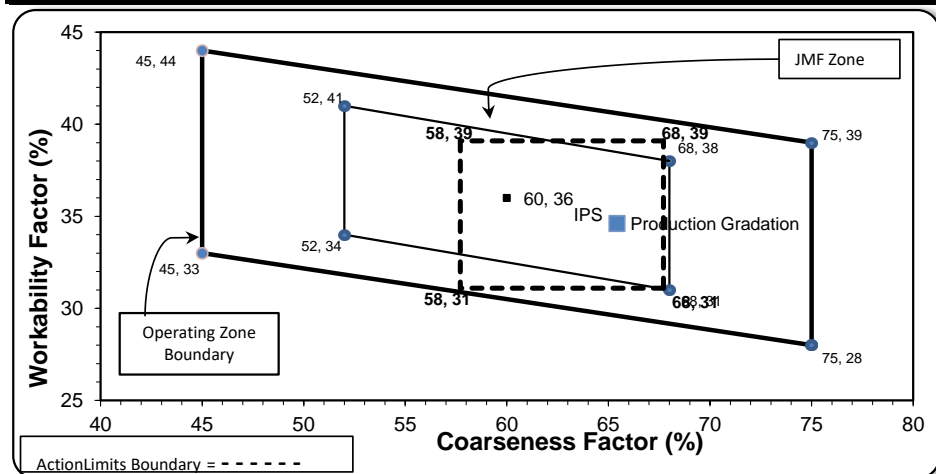

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	100.0	0.0	0.0
3/4"	95.1	4.9	4.9
1/2"	74.6	20.5	25.4
3/8"	59.3	15.3	40.7
#4	42.1	17.2	57.9
#8	35.1	7.1	64.9
#16	29.2	5.9	70.8
#30	21.9	7.3	78.1
#50	9.6	12.4	90.4
#100	2.4	7.2	97.6
LBW	0.9	1.5	99.1

PREPARED BY:  
 SM, LLC Technical Service

Approved By:
