

Aggregate Optimization Chart

PLANT #: **P-101**

Sample Date: 2/21/22

Concrete Grade: **P1M, 3500HP**

Contractor: _____

Dates Test Represents: 2/22/2022 through 2/28/2022

MDOT No.: _____

Agg. Class	Pit #	Source	Weight (SSD)	ft ³	Specific Gravity	% Contribution
CA	71-47	Presque Isle	1070	6.54	2.62	34.9
IA	71-47	Presque Isle	800	4.89	2.62	26.1
2NS	75-051	Mid-Michigan	1200	7.23	2.66	39.1
Total Wt			3070	18.67		100.0

<---- Verify this number is 100%



Superior Materials, LLC
 30701 W. 10 Mile Rd.
 Suite 500
 Farmington Hills, MI 48336

Sieve	CA	IA	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	96.8	100.0	100.0	98.9	1.1	1.1
1"	46.8	100.0	100.0	81.5	17.4	18.5
3/4"	12.2	98.0	100.0	68.9	12.6	31.1
1/2"	3.0	78.8	100.0	60.7	8.2	39.3
3/8"	2.3	53.6	100.0	53.9	6.8	46.1
#4	1.8	8.1	98.5	41.2	12.6	58.8
#8	1.7	2.7	83.3	33.9	7.4	66.1
#16	1.6	1.8	68.3	27.7	6.1	72.3
#30	1.5	1.7	53.3	21.8	5.9	78.2
#50	1.5	1.6	29.2	12.4	9.4	87.6
#100	1.4	1.6	7.3	3.8	8.6	96.2
LBW	1.2	1.4	0.6	1.0	2.7	99.0

*Maximum % Retained must be above the 3/8" sieve.
 *Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.


Production Gradation Batch Plant Gradations Aggregate Supplier Gradations

Coarseness Factor:	70	Workability Factor:	34
---------------------------	-----------	----------------------------	-----------

Initial Production Sample (IPS)

Coarseness Factor:	66
Workability Factor:	35

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	99.6	0.4	0.4
1"	84.3	15.3	15.7
3/4"	74.8	9.6	25.2
1/2"	64.3	10.4	35.7
3/8"	56.8	7.5	43.2
#4	43.0	13.8	57.0
#8	34.9	8.1	65.1
#16	26.4	8.5	73.6
#30	19.9	6.5	80.1
#50	10.4	9.5	89.6
#100	3.4	7.0	96.6
LBW	1.2	2.2	98.8

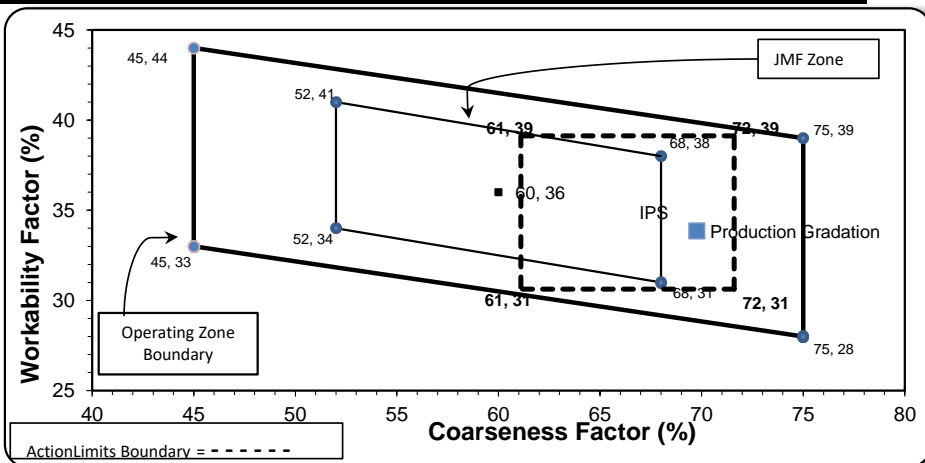

PREPARED BY:
 SM, LLC Technical Service

Approved By:

Aggregate Optimization Chart

PLANT #: **P-102**

Sample Date: 2/21/22

Concrete Grade: **P1M, 3500HP**

Dates Test Represents: 2/22/2022 through 2/28/2022

Contractor: _____

MDOT No.: _____

Agg. Class	Pit #	Source	Weight (SSD)	ft ³	Specific Gravity	% Contribution
CA	58-003	Stoneco	1350	8.04	2.69	43.3
IA	58-003	Stoneco	620	3.69	2.69	19.9
2NS	63-114	Highland	1150	6.95	2.65	36.9
Total Wt			3120	18.69		100.0

<----- Verify this number is 100%




Superior Materials, LLC
 30701 W. 10 Mile Rd.
 Suite 500
 Farmington Hills, MI 48336

Sieve	CA	IA	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	65.6	100.0	100.0	85.1	14.9	14.9
3/4"	35.4	100.0	100.0	72.0	13.1	28.0
1/2"	12.1	95.0	100.0	61.0	11.1	39.0
3/8"	7.9	84.2	100.0	57.0	4.0	43.0
#4	2.9	24.9	99.7	43.0	14.1	57.0
#8	2.1	7.9	88.0	34.9	8.0	65.1
#16	1.7	3.8	71.3	27.8	7.1	72.2
#30	1.6	2.8	49.1	19.3	8.4	80.7
#50	1.5	2.6	20.6	8.8	10.6	91.2
#100	1.3	2.5	3.1	2.2	6.6	97.8
LBW	1.2	2.2	0.3	1.1	1.1	98.9

*Maximum % Retained must be above the 3/8" sieve.
 *Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation Batch Plant Gradations Aggregate Supplier Gradations

Coarseness Factor: **66** **Workability Factor:** **35**

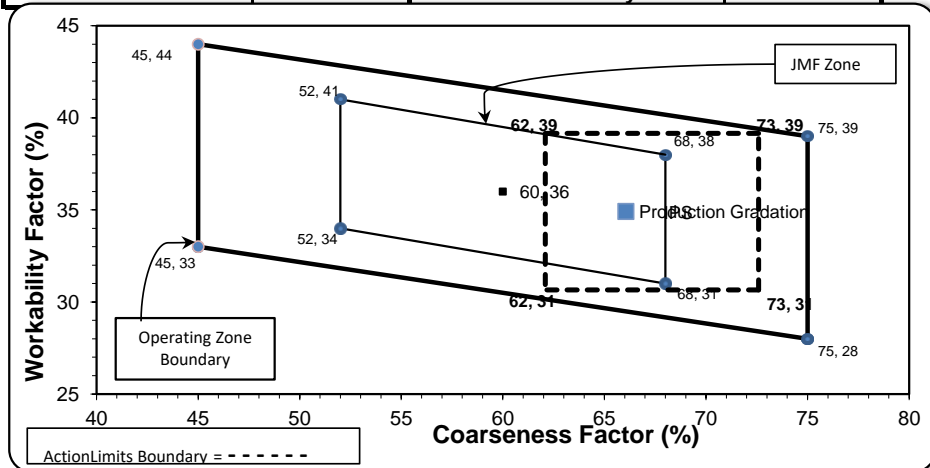

Initial Production Sample (IPS)

Coarseness Factor: **67**
Workability Factor: **35**

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	85.5	14.5	14.5
3/4"	73.4	12.1	26.6
1/2"	61.0	12.4	39.0
3/8"	56.2	4.8	43.8
#4	43.1	13.1	56.9
#8	34.9	8.2	65.1
#16	29.4	5.5	70.6
#30	21.6	7.8	78.4
#50	8.1	13.4	91.9
#100	2.2	5.9	97.8
LBW	1.4	0.8	98.6

PREPARED BY:
 SM, LLC Technical Service

Approved By:

Aggregate Optimization Chart

PLANT #: **P-12**

Sample Date: 2/21/22

Concrete Grade: **P1M, 3500HP**

Dates Test Represents: 2/22/2022 through 2/28/2022

Contractor: _____

MDOT No.: _____



Superior Materials, LLC
30701 W. 10 Mile Rd.
Suite 500
Farmington Hills, MI 48336

Agg. Class	Pit #	Source	Weight (SSD)	ft ³	Specific Gravity	% Contribution
CA	71-47	Presque Isle	1020	6.24	2.62	33.2
IA	71-47	Presque Isle	800	4.89	2.62	26.1
2NS	63-115	Ray Rd	1250	7.56	2.65	40.7
Total Wt			3070	18.69		100.0


<----- Verify this number is 100%

Sieve	CA	IA	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	43.0	100.0	100.0	81.1	18.9	18.9
3/4"	11.9	98.2	100.0	70.3	10.8	29.7
1/2"	3.2	73.9	100.0	61.0	9.2	39.0
3/8"	1.7	48.5	100.0	53.9	7.1	46.1
#4	1.1	10.9	96.5	42.5	11.4	57.5
#8	1.0	4.5	80.6	34.3	8.2	65.7
#16	1.0	3.2	67.6	28.7	5.6	71.3
#30	1.0	2.8	48.2	20.7	8.0	79.3
#50	1.0	2.6	27.0	12.0	8.7	88.0
#100	0.9	2.3	5.2	3.0	9.0	97.0
LBW	0.7	1.7	0.9	1.0	2.0	99.0

*Maximum % Retained must be above the 3/8" sieve.
*Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.
*% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.
*% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation Batch Plant Gradations Aggregate Supplier Gradations

Coarseness Factor:	70	Workability Factor:	34
---------------------------	-----------	----------------------------	-----------

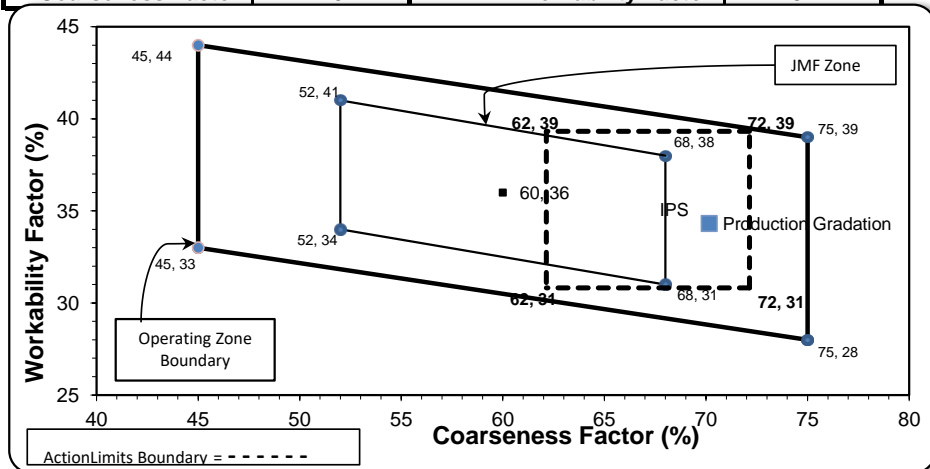

Initial Production Sample (IPS)

Coarseness Factor:	67
Workability Factor:	35

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	99.6	0.4	0.4
1"	83.9	15.7	16.1
3/4"	74.0	9.8	26.0
1/2"	63.7	10.3	36.3
3/8"	56.4	7.3	43.6
#4	43.0	13.4	57.0
#8	35.1	7.9	64.9
#16	29.0	6.1	71.0
#30	20.9	8.0	79.1
#50	8.1	12.8	91.9
#100	1.6	6.5	98.4
LBW	0.9	0.8	99.1

PREPARED BY:
SM, LLC Technical Service

Approved By:

Aggregate Optimization Chart

PLANT #: **P-32**

Sample Date: 2/21/22

Concrete Grade: **P1M, 3500HP**

Dates Test Represents: 2/22/2022 through 2/28/2022

Contractor: _____

MDOT No.: _____

Agg. Class	Pit #	Source	Weight (SSD)	ft ³	Specific Gravity	% Contribution
CA	71-47	Presque Isle	920	5.63	2.62	30.0
IA	71-47	Presque Isle	900	5.50	2.62	29.3
2NS	95-013	Smelter Bay	1250	7.56	2.65	40.7
Total Wt			3070	18.69		100.0

<----- Verify this number is 100%




Superior Materials, LLC
 30701 W. 10 Mile Rd.
 Suite 500
 Farmington Hills, MI 48336

Sieve	CA	IA	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	43.0	100.0	100.0	82.9	17.1	17.1
3/4"	11.9	98.2	100.0	73.1	9.8	26.9
1/2"	3.2	73.9	100.0	63.3	9.7	36.7
3/8"	1.7	48.5	100.0	55.4	7.9	44.6
#4	1.1	10.9	96.3	42.7	12.7	57.3
#8	1.0	4.5	83.1	35.5	7.3	64.5
#16	1.0	3.2	67.4	28.7	6.8	71.3
#30	1.0	2.8	48.7	20.9	7.7	79.1
#50	1.0	2.6	24.5	11.0	9.9	89.0
#100	0.9	2.3	7.4	4.0	7.1	96.0
LBW	0.7	1.7	1.4	1.3	2.7	98.7

*Maximum % Retained must be above the 3/8" sieve.
 *Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation Batch Plant Gradations Aggregate Supplier Gradations

Coarseness Factor: **69** **Workability Factor:** **35**

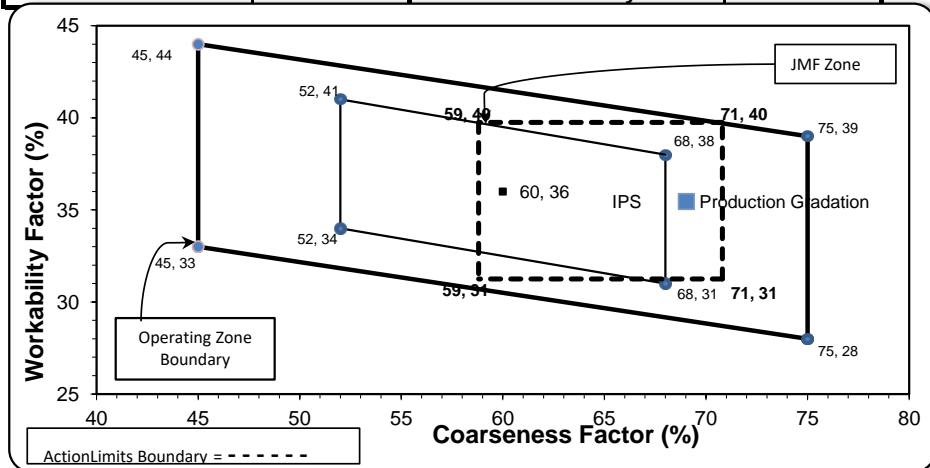

Initial Production Sample (IPS)

Coarseness Factor: **65**
Workability Factor: **36**

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	99.0	0.6	0.6
1"	84.0	15.3	16.0
3/4"	73.5	10.5	26.5
1/2"	65.2	8.2	34.8
3/8"	58.2	7.1	41.8
#4	44.1	14.1	55.9
#8	35.5	8.6	64.5
#16	29.1	6.4	70.9
#30	21.9	7.3	78.1
#50	9.6	12.2	90.4
#100	2.6	7.1	97.4
LBW	1.0	1.6	99.0

PREPARED BY:
 SM, LLC Technical Service

Approved By:

Aggregate Optimization Chart

PLANT #: **P-35**

Sample Date: 2/21/22

Concrete Grade: **P1M, 3500HP**

Dates Test Represents: 2/22/2022 through 2/28/2022

Contractor: _____

MDOT No.: _____



Superior Materials, LLC
 30701 W. 10 Mile Rd.
 Suite 500
 Farmington Hills, MI 48336

Agg. Class	Pit #	Source	Weight (SSD)	ft ³	Specific Gravity	% Contribution
CA	58-003	Stoneco	1380	8.22	2.69	44.2
IA	58-003	Stoneco	620	3.69	2.69	19.9
2NS	81-019	Pleasant Lake	1120	6.77	2.65	35.9
Total Wt			3120	18.69		100.0


<----- Verify this number is 100%

Sieve	CA	IA	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	65.6	100.0	100.0	84.8	15.2	15.2
3/4"	35.4	100.0	100.0	71.4	13.4	28.6
1/2"	12.1	95.0	100.0	60.1	11.3	39.9
3/8"	7.9	84.2	100.0	56.1	4.0	43.9
#4	2.9	24.9	97.7	41.3	14.8	58.7
#8	2.1	7.9	86.0	33.4	7.9	66.6
#16	1.7	3.8	70.7	26.9	6.5	73.1
#30	1.6	2.8	52.4	20.1	6.8	79.9
#50	1.5	2.6	22.0	9.1	11.0	90.9
#100	1.3	2.5	4.5	2.7	6.4	97.3
LBW	1.2	2.2	1.7	1.6	1.1	98.4

*Maximum % Retained must be above the 3/8" sieve.
 *Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation Batch Plant Gradations Aggregate Supplier Gradations

Coarseness Factor:	66	Workability Factor:	33
---------------------------	-----------	----------------------------	-----------

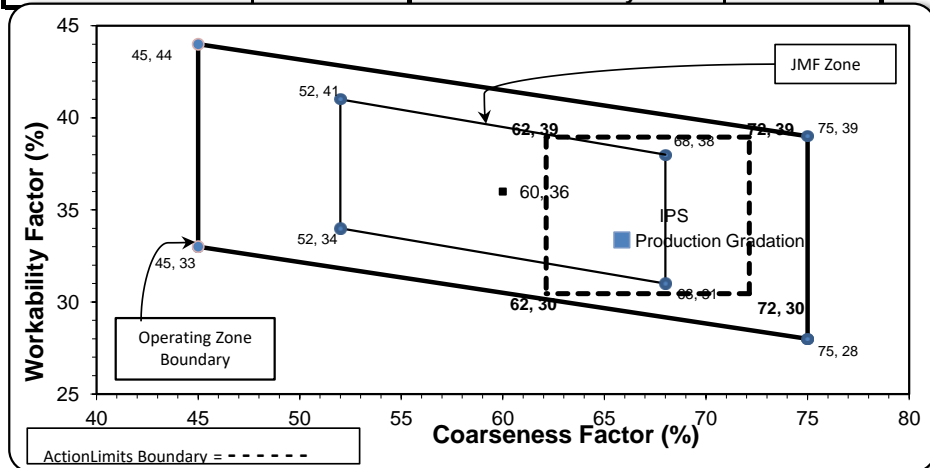

Initial Production Sample (IPS)

Coarseness Factor:	67
Workability Factor:	35

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	86.9	13.1	13.1
3/4"	76.1	10.8	23.9
1/2"	63.7	12.4	36.3
3/8"	56.2	7.5	43.8
#4	43.2	13.0	56.8
#8	34.7	8.5	65.3
#16	27.5	7.2	72.5
#30	20.6	7.0	79.4
#50	9.0	11.6	91.0
#100	2.1	6.9	97.9
LBW	1.0	1.1	99.0

PREPARED BY:
 SM, LLC Technical Service

Approved By:

Aggregate Optimization Chart

PLANT #: **P-39**

Sample Date: 2/21/22

Concrete Grade: **P1M, 3500HP**

Dates Test Represents: 2/22/2022 through 2/28/2022

Contractor: _____

MDOT No.: _____

Agg. Class	Pit #	Source	Weight (SSD)	ft ³	Specific Gravity	% Contribution
CA	71-47	Presque Isle	1070	6.54	2.62	34.9
IA	71-47	Presque Isle	750	4.59	2.62	24.4
2NS	63-92	Grange Hall	1250	7.56	2.65	40.7
Total Wt			3070	18.69		100.0

<----- Verify this number is 100%




Superior Materials, LLC
 30701 W. 10 Mile Rd.
 Suite 500
 Farmington Hills, MI 48336

Sieve	CA	IA	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	96.8	100.0	100.0	98.9	1.1	1.1
1"	46.8	100.0	100.0	81.5	17.4	18.5
3/4"	12.2	98.0	100.0	68.9	12.5	31.1
1/2"	3.0	78.8	100.0	61.0	7.9	39.0
3/8"	2.3	53.6	100.0	54.6	6.4	45.4
#4	1.8	8.1	98.1	42.5	12.1	57.5
#8	1.7	2.7	82.8	35.0	7.6	65.0
#16	1.6	1.8	67.7	28.6	6.4	71.4
#30	1.5	1.7	49.2	21.0	7.6	79.0
#50	1.5	1.6	22.5	10.1	10.9	89.9
#100	1.4	1.6	3.8	2.4	7.6	97.6
LBW	1.2	1.4	0.6	1.0	1.4	99.0

*Maximum % Retained must be above the 3/8" sieve.
 *Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation Batch Plant Gradations Aggregate Supplier Gradations

Coarseness Factor: **70** **Workability Factor:** **35**

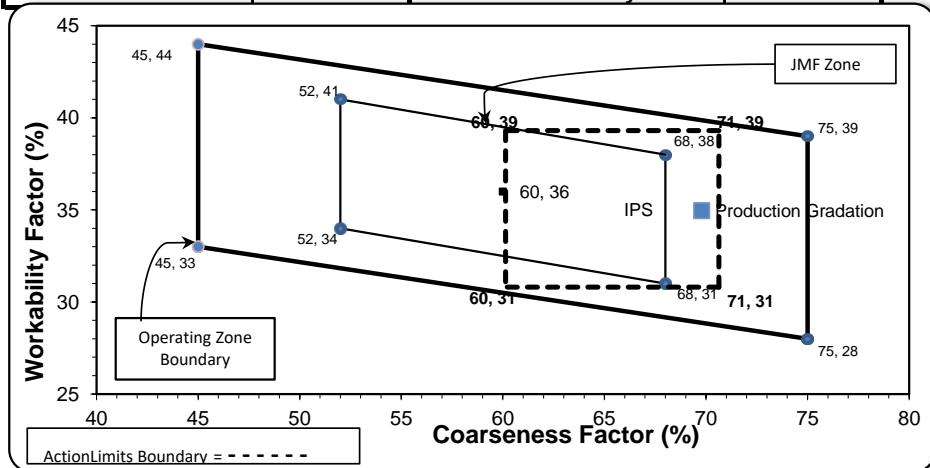

Initial Production Sample (IPS)

Coarseness Factor: 65		Workability Factor: 35	
Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	99.6	0.4	0.4
1"	83.9	15.7	16.1
3/4"	74.1	9.8	25.9
1/2"	64.3	9.7	35.7
3/8"	57.5	6.8	42.5
#4	44.5	13.1	55.5
#8	35.1	9.4	64.9
#16	27.9	7.2	72.1
#30	21.7	6.2	78.3
#50	12.6	9.1	87.4
#100	3.5	9.1	96.5
LBW	1.2	2.4	98.8

PREPARED BY:
 SM, LLC Technical Service

Approved By:

Aggregate Optimization Chart

PLANT #: **P-O2**

Sample Date: 2/21/22

Concrete Grade: **P1M, 3500HP**

Dates Test Represents: 2/22/2022 through 2/28/2022

Contractor: _____

MDOT No.: _____

Agg. Class	Pit #	Source	Weight (SSD)	ft ³	Specific Gravity	% Contribution
CA	71-47	Presque Isle	970	5.93	2.62	31.6
IA	71-47	Presque Isle	850	5.20	2.62	27.7
2NS	63-115	Ray Rd	1250	7.56	2.65	40.7
Total Wt			3070	18.69		100.0

<----- Verify this number is 100%




Superior Materials, LLC
 30701 W. 10 Mile Rd.
 Suite 500
 Farmington Hills, MI 48336

Sieve	CA	IA	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	43.0	100.0	100.0	82.0	18.0	18.0
3/4"	11.9	98.2	100.0	71.7	10.3	28.3
1/2"	3.2	73.9	100.0	62.2	9.5	37.8
3/8"	1.7	48.5	100.0	54.7	7.5	45.3
#4	1.1	10.9	96.5	42.7	12.0	57.3
#8	1.0	4.5	80.6	34.4	8.3	65.6
#16	1.0	3.2	67.6	28.7	5.7	71.3
#30	1.0	2.8	48.2	20.7	8.0	79.3
#50	1.0	2.6	27.0	12.0	8.7	88.0
#100	0.9	2.3	5.2	3.0	9.0	97.0
LBW	0.7	1.7	0.9	1.1	2.0	98.9

*Maximum % Retained must be above the 3/8" sieve.
 *Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation Batch Plant Gradations Aggregate Supplier Gradations

Coarseness Factor: **69** **Workability Factor:** **34**

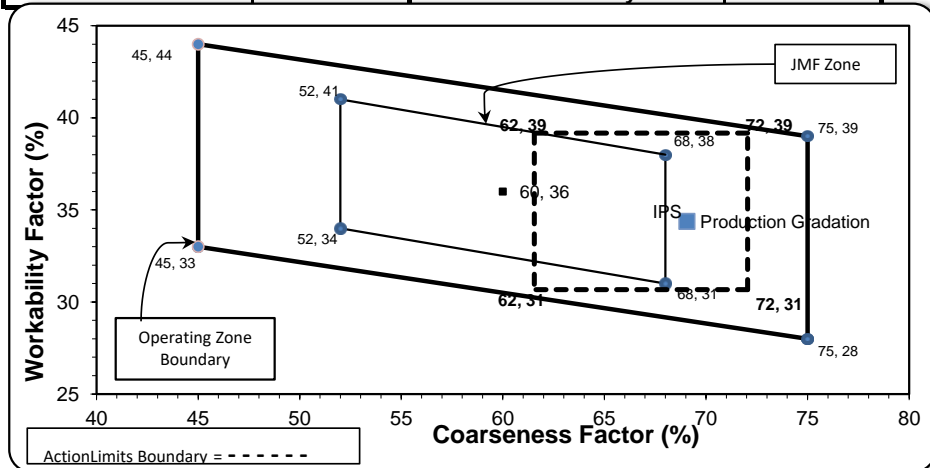

Initial Production Sample (IPS)

Coarseness Factor: **67**
Workability Factor: **35**

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	85.0	15.0	15.0
3/4"	72.3	12.7	27.7
1/2"	64.5	7.8	35.5
3/8"	56.5	8.0	43.5
#4	42.7	13.8	57.3
#8	34.9	7.8	65.1
#16	29.0	5.9	71.0
#30	21.0	8.0	79.0
#50	8.2	12.8	91.8
#100	1.6	6.5	98.4
LBW	0.7	0.9	99.3

PREPARED BY:
 SM, LLC Technical Service

Approved By:
