

# Aggregate Optimization Chart

**PLANT #:** **P-101**

Sample Date: 5/30/22

Concrete Grade: **S2M, 3500HP**

Dates Test Represents: 5/31/2022 through 6/6/2022

Contractor: \_\_\_\_\_

MDOT No.: \_\_\_\_\_

Agg. Class	Pit #	Source	Weight (SSD)	ft <sup>3</sup>	Specific Gravity	% Contribution
6AA	71-47	Presque Isle	1550	9.48	2.62	50.7
26A	71-47	Presque Isle	275	1.68	2.62	9.0
2NS	75-051	Mid Michigan	1230	7.41	2.66	40.3
<b>Total Wt</b>			<b>3055</b>	<b>18.57</b>		<b>100.0</b>

<---- Verify this number is 100%



**Superior Materials, LLC**  
 30701 W. 10 Mile Rd.  
 Suite 500  
 Farmington Hills, MI 48336

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	98.2	100.0	100.0	99.1	0.9	0.9
3/4"	83.3	100.0	100.0	91.5	7.6	8.5
1/2"	46.0	96.2	100.0	72.3	19.3	27.7
3/8"	27.8	85.3	100.0	62.0	10.2	38.0
#4	4.4	23.5	98.8	44.1	17.9	55.9
#8	1.9	7.3	85.0	35.8	8.3	64.2
#16	1.6	3.4	70.4	29.5	6.4	70.5
#30	1.5	2.5	53.3	22.4	7.0	77.6
#50	1.5	2.3	25.5	11.2	11.2	88.8
#100	1.4	2.1	6.4	3.5	7.8	96.5
LBW	1.3	1.9	0.6	1.1	2.4	98.9


\*Maximum % Retained must be above the 3/8" sieve.  
 \*Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation  Batch Plant Gradations  Aggregate Supplier Gradations

<b>Coarseness Factor:</b>	<b>59</b>	<b>Workability Factor:</b>	<b>36</b>
---------------------------	-----------	----------------------------	-----------

Initial Production Sample (IPS)

<b>Coarseness Factor:</b>	<b>64</b>
<b>Workability Factor:</b>	<b>35</b>

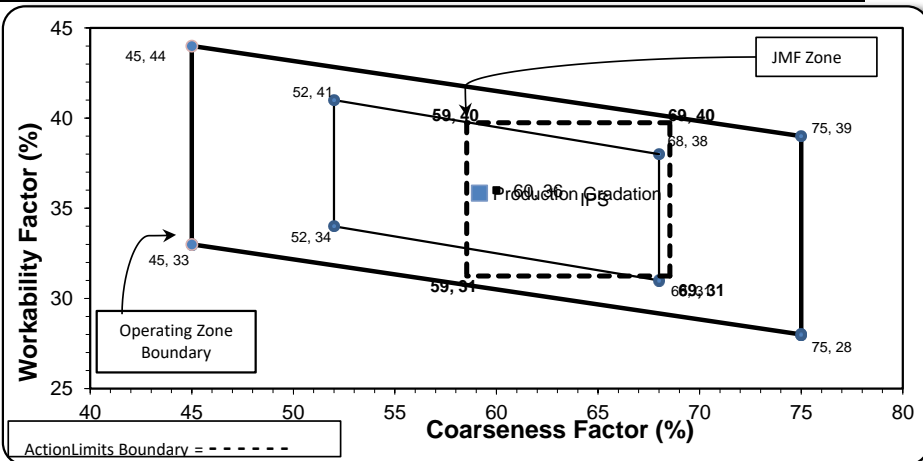

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	100.0	0.0	0.0
3/4"	93.9	6.1	6.1
1/2"	71.4	22.5	28.6
3/8"	59.0	12.4	41.0
#4	45.1	13.9	54.9
#8	35.5	9.6	64.5
#16	28.3	7.2	71.7
#30	21.3	6.9	78.7
#50	11.0	10.3	89.0
#100	3.4	7.6	96.6
LBW	1.1	2.3	98.9

PREPARED BY:  
 SM, LLC Technical Service

Approved By:

# Aggregate Optimization Chart

**PLANT #:** **P-102**

Sample Date: 5/30/22

Concrete Grade: **S2M, 3500HP**

Dates Test Represents: 5/31/2022 through 6/6/2022

Contractor: \_\_\_\_\_

MDOT No.: \_\_\_\_\_

Agg. Class	Pit #	Source	Weight (SSD)	ft <sup>3</sup>	Specific Gravity	% Contribution
6AA	58-003	Stoneco	1600	9.53	2.69	51.6
26A	58-003	Stoneco	300	1.79	2.69	9.7
2NS	81-019	Pleasant Lake	1200	7.26	2.65	38.7
<b>Total Wt</b>			<b>3100</b>	<b>18.58</b>		<b>100.0</b>

<----- Verify this number is 100%




**Superior Materials, LLC**  
 30701 W. 10 Mile Rd.  
 Suite 500  
 Farmington Hills, MI 48336

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	100.0	100.0	100.0	100.0	0.0	0.0
3/4"	78.3	100.0	100.0	88.8	11.2	11.2
1/2"	44.7	99.6	100.0	71.4	17.4	28.6
3/8"	20.2	87.0	100.0	57.6	13.9	42.4
#4	4.1	19.1	97.1	41.6	16.0	58.4
#8	1.5	6.9	80.5	32.6	8.9	67.4
#16	1.3	3.9	63.5	25.6	7.0	74.4
#30	1.1	2.7	46.3	18.8	6.9	81.2
#50	0.9	2.4	23.4	9.8	9.0	90.2
#100	0.9	2.3	8.0	3.8	6.0	96.2
LBW	0.6	2.1	1.7	1.2	2.6	98.8

\*Maximum % Retained must be above the 3/8" sieve.  
 \*Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation  Batch Plant Gradations  Aggregate Supplier Gradations

**Coarseness Factor:** **63**      **Workability Factor:** **33**

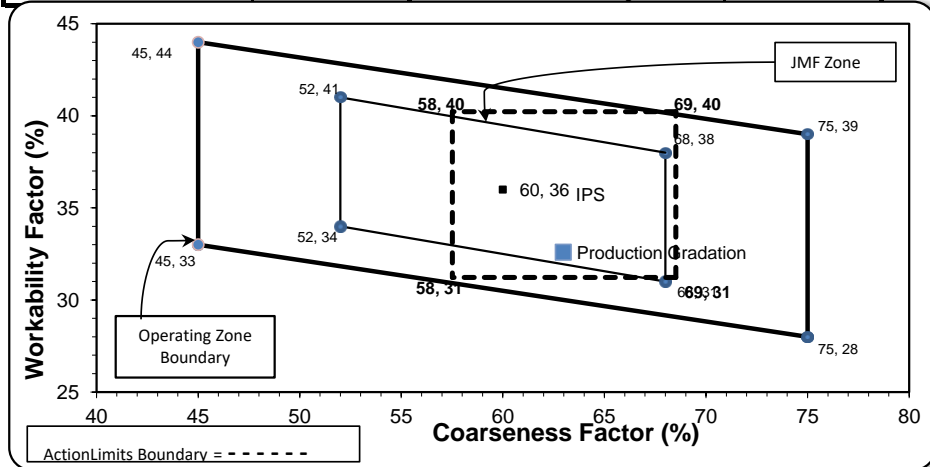

Initial Production Sample (IPS)

**Coarseness Factor:** **63**  
**Workability Factor:** **36**

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	99.2	0.8	0.8
3/4"	90.9	8.3	9.1
1/2"	71.3	19.6	28.7
3/8"	59.5	11.8	40.5
#4	43.8	15.7	56.2
#8	35.7	8.1	64.3
#16	27.0	8.7	73.0
#30	18.6	8.4	81.4
#50	6.8	11.8	93.2
#100	1.4	5.4	98.6
LBW	0.6	0.8	99.4

PREPARED BY:  
 SM, LLC Technical Service

Approved By:

# Aggregate Optimization Chart

**PLANT #:** **P-32**

Sample Date: 5/30/22

Concrete Grade: **S2M, 3500HP**

Dates Test Represents: 5/31/2022 through 6/6/2022

Contractor: \_\_\_\_\_

MDOT No.: \_\_\_\_\_

Agg. Class	Pit #	Source	Weight (SSD)	ft <sup>3</sup>	Specific Gravity	% Contribution
6AA	71-47	Presque Isle	1600	9.79	2.62	52.5
26A	71-47	Presque Isle	220	1.35	2.62	7.2
2NS	95-013	Smelter Bay	1230	7.44	2.65	40.3
<b>Total Wt</b>			<b>3050</b>	<b>18.57</b>		<b>100.0</b>

<----- Verify this number is 100%




**Superior Materials, LLC**  
 30701 W. 10 Mile Rd.  
 Suite 500  
 Farmington Hills, MI 48336

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	97.0	100.0	100.0	98.4	1.6	1.6
3/4"	81.3	100.0	100.0	90.2	8.2	9.8
1/2"	42.6	95.5	100.0	69.6	20.6	30.4
3/8"	23.7	77.9	100.0	58.4	11.2	41.6
#4	5.6	17.9	96.6	43.2	15.2	56.8
#8	3.0	5.8	84.6	36.1	7.1	63.9
#16	2.6	2.8	69.8	29.7	6.4	70.3
#30	2.4	2.1	50.8	21.9	7.8	78.1
#50	2.3	1.9	24.5	11.2	10.7	88.8
#100	2.2	1.7	6.9	4.1	7.2	95.9
LBW	1.7	1.4	1.3	1.5	2.5	98.5

\*Maximum % Retained must be above the 3/8" sieve.  
 \*Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation  Batch Plant Gradations  Aggregate Supplier Gradations

**Coarseness Factor:** **65**      **Workability Factor:** **36**

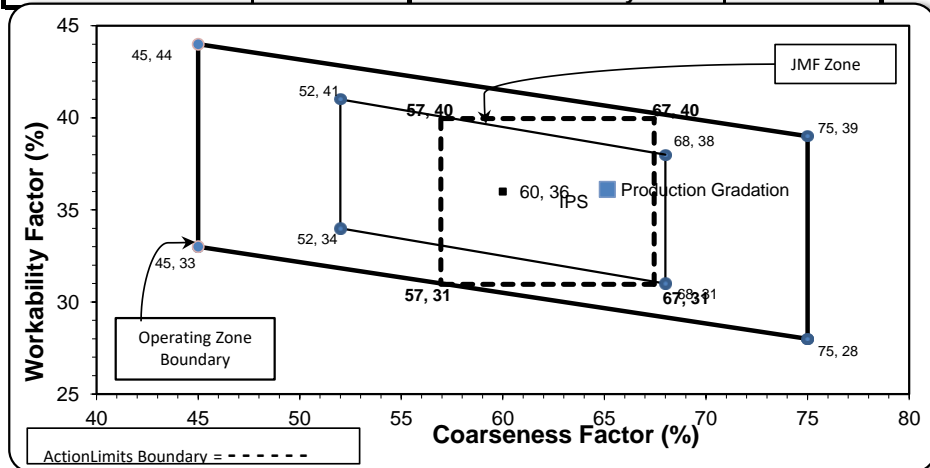

Initial Production Sample (IPS)

**Coarseness Factor:** **62**  
**Workability Factor:** **35**

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	100.0	0.0	0.0
3/4"	94.0	6.0	6.0
1/2"	70.2	23.7	29.8
3/8"	59.9	10.4	40.1
#4	42.7	17.2	57.3
#8	35.5	7.2	64.5
#16	28.4	7.0	71.6
#30	19.2	9.2	80.8
#50	8.9	10.3	91.1
#100	3.1	5.9	96.9
LBW	1.4	1.7	98.6

PREPARED BY:  
 SM, LLC Technical Service

Approved By:

# Aggregate Optimization Chart

**PLANT #:** **P-35**

Sample Date: 5/30/22

Concrete Grade: **S2M, 3500HP**

Dates Test Represents: 5/31/2022 through 6/6/2022

Contractor: \_\_\_\_\_

MDOT No.: \_\_\_\_\_

Agg. Class	Pit #	Source	Weight (SSD)	ft <sup>3</sup>	Specific Gravity	% Contribution
6AA	58-003	Stoneco	1600	9.53	2.69	51.6
26A	58-003	Stoneco	300	1.79	2.69	9.7
2NS	81-019	Pleasant Lake	1200	7.26	2.65	38.7
<b>Total Wt</b>			<b>3100</b>	<b>18.58</b>		<b>100.0</b>

<----- Verify this number is 100%




**Superior Materials, LLC**  
 30701 W. 10 Mile Rd.  
 Suite 500  
 Farmington Hills, MI 48336

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	100.0	100.0	100.0	100.0	0.0	0.0
3/4"	78.3	100.0	100.0	88.8	11.2	11.2
1/2"	44.7	99.6	100.0	71.4	17.4	28.6
3/8"	20.2	87.0	100.0	57.6	13.9	42.4
#4	4.1	19.1	97.1	41.6	16.0	58.4
#8	1.5	6.9	80.5	32.6	8.9	67.4
#16	1.3	3.9	63.5	25.6	7.0	74.4
#30	1.1	2.7	46.3	18.8	6.9	81.2
#50	0.9	2.4	23.4	9.8	9.0	90.2
#100	0.9	2.3	8.0	3.8	6.0	96.2
LBW	0.6	2.1	1.7	1.2	2.6	98.8

\*Maximum % Retained must be above the 3/8" sieve.  
 \*Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation  Batch Plant Gradations  Aggregate Supplier Gradations

<b>Coarseness Factor:</b>	<b>63</b>	<b>Workability Factor:</b>	<b>33</b>
---------------------------	-----------	----------------------------	-----------

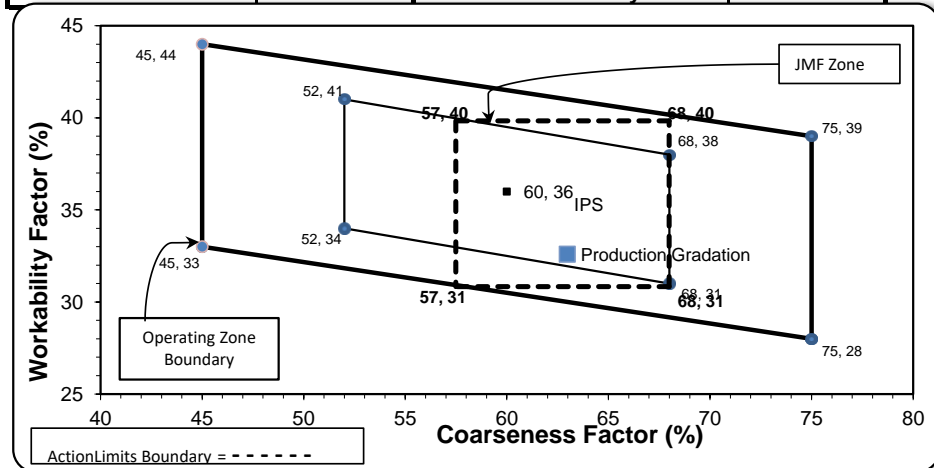

Initial Production Sample (IPS)

<b>Coarseness Factor:</b>	<b>63</b>		
<b>Workability Factor:</b>	<b>35</b>		
Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	99.2	0.8	0.8
3/4"	90.9	8.3	9.1
1/2"	71.3	19.6	28.7
3/8"	59.4	11.9	40.6
#4	43.0	16.5	57.0
#8	35.3	7.6	64.7
#16	28.2	7.1	71.8
#30	21.6	6.6	78.4
#50	9.1	12.5	90.9
#100	1.7	7.4	98.3
LBW	1.1	0.6	98.9

PREPARED BY:  
 SM, LLC Technical Service

Approved By:

# Aggregate Optimization Chart

**PLANT #:** **P-39**

Sample Date: 5/30/22

Concrete Grade: **S2M, 3500HP**

Dates Test Represents: 5/31/2022 through 6/6/2022

Contractor: \_\_\_\_\_

MDOT No.: \_\_\_\_\_

Agg. Class	Pit #	Source	Weight (SSD)	ft <sup>3</sup>	Specific Gravity	% Contribution
6AA	71-47	Presque Isle	1600	9.79	2.62	52.5
26A	71-47	Presque Isle	200	1.22	2.62	6.6
2NS	44-051	Krake Willis Rd	1250	7.56	2.65	41.0
<b>Total Wt</b>			<b>3050</b>	<b>18.57</b>		<b>100.0</b>

<----- Verify this number is 100%




**Superior Materials, LLC**  
 30701 W. 10 Mile Rd.  
 Suite 500  
 Farmington Hills, MI 48336

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	98.2	100.0	100.0	99.1	0.9	0.9
3/4"	83.3	100.0	100.0	91.2	7.8	8.8
1/2"	46.0	96.2	100.0	71.4	19.8	28.6
3/8"	27.8	85.3	100.0	61.2	10.3	38.8
#4	4.4	23.5	96.4	43.4	17.8	56.6
#8	1.9	7.3	80.6	34.5	8.8	65.5
#16	1.6	3.4	66.0	28.1	6.4	71.9
#30	1.5	2.5	50.2	21.5	6.6	78.5
#50	1.5	2.3	27.6	12.2	9.3	87.8
#100	1.4	2.1	9.2	4.6	7.6	95.4
LBW	1.3	1.9	1.6	1.5	3.2	98.5

\*Maximum % Retained must be above the 3/8" sieve.  
 \*Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation  Batch Plant Gradations  Aggregate Supplier Gradations

<b>Coarseness Factor:</b>	<b>59</b>	<b>Workability Factor:</b>	<b>35</b>
---------------------------	-----------	----------------------------	-----------

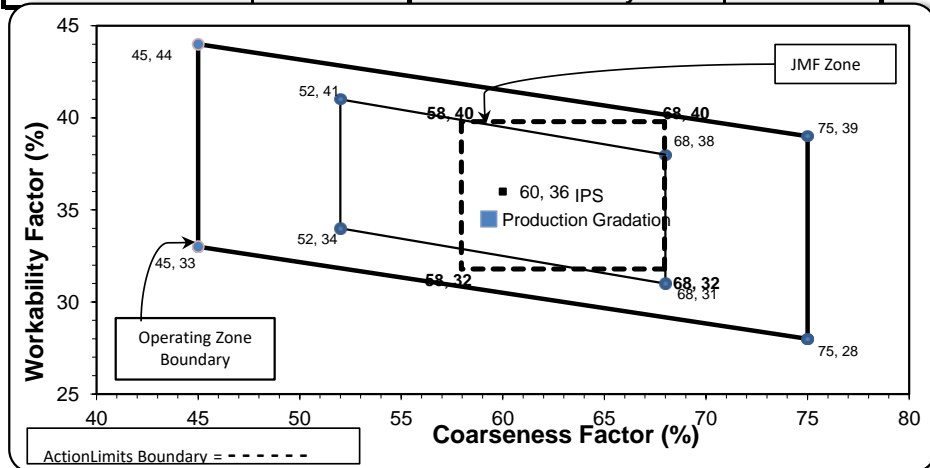

Initial Production Sample (IPS)

<b>Coarseness Factor:</b>	<b>63</b>
<b>Workability Factor:</b>	<b>36</b>

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	100.0	0.0	0.0
3/4"	89.8	10.2	10.2
1/2"	70.7	19.1	29.3
3/8"	59.6	11.1	40.4
#4	43.2	16.4	56.8
#8	35.8	7.4	64.2
#16	29.2	6.6	70.8
#30	21.4	7.8	78.6
#50	9.8	11.6	90.2
#100	3.7	6.1	96.3
LBW	1.2	2.5	98.8

PREPARED BY:  
 SM, LLC Technical Service

Approved By:

# Aggregate Optimization Chart

**PLANT #:** **P-O2**

Sample Date: 5/30/22

Concrete Grade: **S2M, 3500HP**

Dates Test Represents: 5/31/2022 through 6/6/2022

Contractor: \_\_\_\_\_

MDOT No.: \_\_\_\_\_

Agg. Class	Pit #	Source	Weight (SSD)	ft <sup>3</sup>	Specific Gravity	% Contribution
6AA	71-47	Presque Isle	1550	9.48	2.62	50.8
26A	71-47	Presque Isle	250	1.53	2.62	8.2
2NS	63-115	Ray Rd	1250	7.56	2.65	41.0
<b>Total Wt</b>			<b>3050</b>	<b>18.57</b>		<b>100.0</b>

<----- Verify this number is 100%




**Superior Materials, LLC**  
 30701 W. 10 Mile Rd.  
 Suite 500  
 Farmington Hills, MI 48336

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	98.8	100.0	100.0	99.4	0.6	0.6
3/4"	87.9	100.0	100.0	93.9	5.5	6.1
1/2"	43.8	95.5	100.0	71.1	22.8	28.9
3/8"	23.7	77.9	100.0	59.4	11.7	40.6
#4	5.2	17.9	96.5	43.7	15.8	56.3
#8	3.0	5.8	78.6	34.2	9.4	65.8
#16	2.5	2.8	61.6	26.7	7.5	73.3
#30	2.3	2.1	46.1	20.2	6.5	79.8
#50	2.2	1.9	25.4	11.7	8.6	88.3
#100	2.0	1.7	5.2	3.3	8.4	96.7
LBW	1.5	1.4	0.9	1.2	2.0	98.8

\*Maximum % Retained must be above the 3/8" sieve.  
 \*Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation  Batch Plant Gradations  Aggregate Supplier Gradations

<b>Coarseness Factor:</b>	<b>62</b>	<b>Workability Factor:</b>	<b>34</b>
---------------------------	-----------	----------------------------	-----------

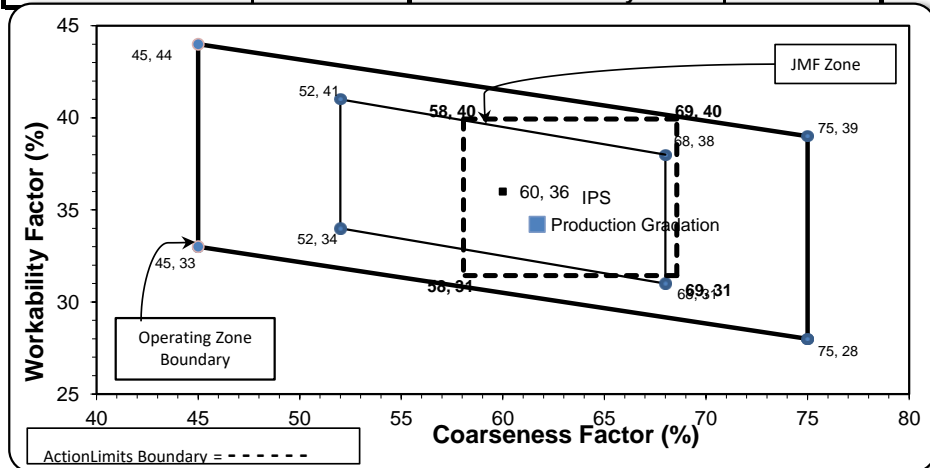

Initial Production Sample (IPS)

<b>Coarseness Factor:</b>	<b>63</b>		
<b>Workability Factor:</b>	<b>36</b>		
Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	100.0	0.0	0.0
3/4"	95.6	4.4	4.4
1/2"	73.1	22.6	26.9
3/8"	59.3	13.8	40.7
#4	42.8	16.5	57.2
#8	35.7	7.1	64.3
#16	28.9	6.8	71.1
#30	20.7	8.2	79.3
#50	9.9	10.8	90.1
#100	2.1	7.8	97.9
LBW	0.9	1.2	99.1

PREPARED BY:  
 SM, LLC Technical Service

Approved By:
