

# Aggregate Optimization Chart

**PLANT #:** **P-101**

Sample Date: 6/20/22

Concrete Grade: **S2M, 3500HP**

Dates Test Represents: 6/21/2022 through 6/27/2022

Contractor: \_\_\_\_\_

MDOT No.: \_\_\_\_\_

Agg. Class	Pit #	Source	Weight (SSD)	ft <sup>3</sup>	Specific Gravity	% Contribution
6AA	71-47	Presque Isle	1625	9.94	2.62	53.2
26A	71-47	Presque Isle	200	1.22	2.62	6.5
2NS	75-051	Mid Michigan	1230	7.41	2.66	40.3
<b>Total Wt</b>			<b>3055</b>	<b>18.57</b>		<b>100.0</b>

<---- Verify this number is 100%



**Superior Materials, LLC**  
 30701 W. 10 Mile Rd.  
 Suite 500  
 Farmington Hills, MI 48336

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	97.3	100.0	100.0	98.6	1.4	1.4
3/4"	82.7	100.0	100.0	90.8	7.8	9.2
1/2"	41.6	97.6	100.0	68.8	22.0	31.2
3/8"	20.1	85.7	100.0	56.6	12.2	43.4
#4	3.5	24.8	98.8	43.3	13.3	56.7
#8	2.1	7.0	83.4	35.2	8.1	64.8
#16	1.7	3.6	66.9	28.1	7.1	71.9
#30	1.6	2.9	49.8	21.1	7.0	78.9
#50	1.5	2.6	24.3	10.8	10.3	89.2
#100	1.4	2.4	6.5	3.5	7.2	96.5
LBW	1.3	2.2	0.9	1.2	2.3	98.8


\*Maximum % Retained must be above the 3/8" sieve.  
 \*Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation  Batch Plant Gradations  Aggregate Supplier Gradations

<b>Coarseness Factor:</b>	<b>67</b>	<b>Workability Factor:</b>	<b>35</b>
---------------------------	-----------	----------------------------	-----------

Initial Production Sample (IPS)

<b>Coarseness Factor:</b>		<b>64</b>	
<b>Workability Factor:</b>		<b>35</b>	
Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	100.0	0.0	0.0
3/4"	93.9	6.1	6.1
1/2"	71.4	22.5	28.6
3/8"	59.0	12.4	41.0
#4	45.1	13.9	54.9
#8	35.5	9.6	64.5
#16	28.3	7.2	71.7
#30	21.3	6.9	78.7
#50	11.0	10.3	89.0
#100	3.4	7.6	96.6
LBW	1.1	2.3	98.9

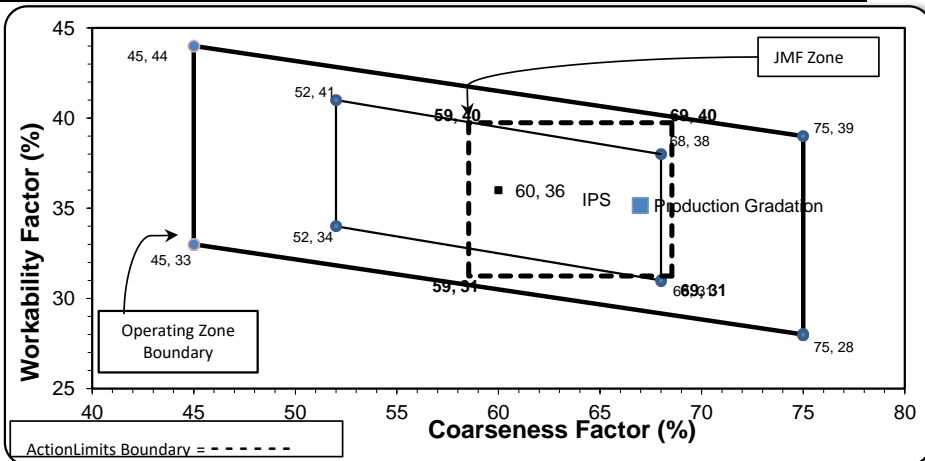

PREPARED BY:  
 SM, LLC Technical Service

Approved By:

# Aggregate Optimization Chart

**PLANT #:** **P-102**

Sample Date: 6/20/22

Concrete Grade: **S2M, 3500HP**

Dates Test Represents: 6/21/2022 through 6/27/2022

Contractor: \_\_\_\_\_

MDOT No.: \_\_\_\_\_

Agg. Class	Pit #	Source	Weight (SSD)	ft <sup>3</sup>	Specific Gravity	% Contribution
6AA	58-003	Stoneco	1650	9.83	2.69	53.2
26A	58-003	Stoneco	250	1.49	2.69	8.1
2NS	81-019	Pleasant Lake	1200	7.26	2.65	38.7
<b>Total Wt</b>			<b>3100</b>	<b>18.58</b>		<b>100.0</b>

<----- Verify this number is 100%




**Superior Materials, LLC**  
 30701 W. 10 Mile Rd.  
 Suite 500  
 Farmington Hills, MI 48336

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	100.0	100.0	100.0	100.0	0.0	0.0
3/4"	80.7	100.0	100.0	89.7	10.3	10.3
1/2"	47.5	99.6	100.0	72.0	17.7	28.0
3/8"	28.1	75.8	100.0	59.8	12.2	40.2
#4	5.1	13.4	99.4	42.3	17.5	57.7
#8	1.8	4.6	81.4	32.8	9.4	67.2
#16	1.3	2.9	63.2	25.4	7.4	74.6
#30	1.0	2.5	45.3	18.3	7.1	81.7
#50	1.0	2.2	22.7	9.5	8.8	90.5
#100	0.9	2.0	7.3	3.5	6.0	96.5
LBW	0.8	1.8	1.4	1.1	2.4	98.9

\*Maximum % Retained must be above the 3/8" sieve.  
 \*Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation  Batch Plant Gradations  Aggregate Supplier Gradations

**Coarseness Factor:** **60**      **Workability Factor:** **33**

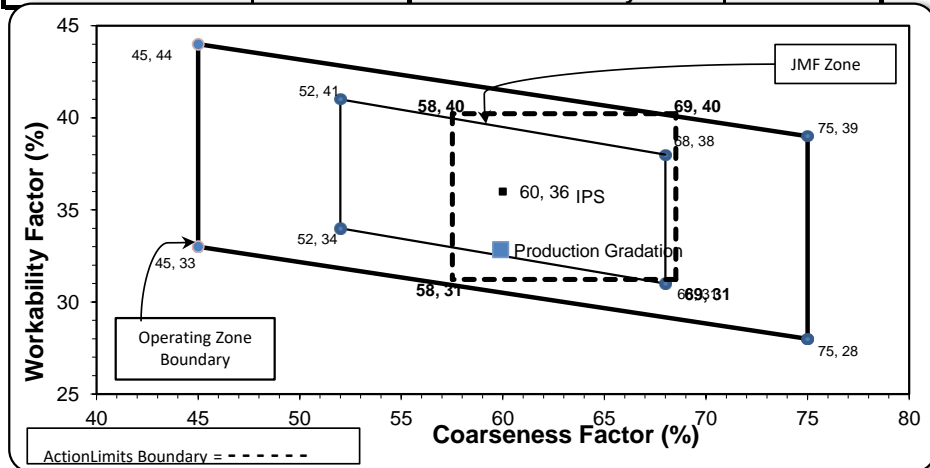

Initial Production Sample (IPS)

**Coarseness Factor:** **63**  
**Workability Factor:** **36**

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	99.2	0.8	0.8
3/4"	90.9	8.3	9.1
1/2"	71.3	19.6	28.7
3/8"	59.5	11.8	40.5
#4	43.8	15.7	56.2
#8	35.7	8.1	64.3
#16	27.0	8.7	73.0
#30	18.6	8.4	81.4
#50	6.8	11.8	93.2
#100	1.4	5.4	98.6
LBW	0.6	0.8	99.4

PREPARED BY:  
 SM, LLC Technical Service

Approved By:

# Aggregate Optimization Chart

**PLANT #:** **P-32**

Sample Date: 6/20/22

Concrete Grade: **S2M, 3500HP**

Dates Test Represents: 6/21/2022 through 6/27/2022

Contractor: \_\_\_\_\_

MDOT No.: \_\_\_\_\_



**Superior Materials, LLC**  
 30701 W. 10 Mile Rd.  
 Suite 500  
 Farmington Hills, MI 48336

Agg. Class	Pit #	Source	Weight (SSD)	ft <sup>3</sup>	Specific Gravity	% Contribution
6AA	71-47	Presque Isle	1400	8.56	2.62	45.9
26A	71-47	Presque Isle	420	2.57	2.62	13.8
2NS	95-013	Smelter Bay	1230	7.44	2.65	40.3
<b>Total Wt</b>			<b>3050</b>	<b>18.57</b>		<b>100.0</b>


<----- Verify this number is 100%

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	97.6	100.0	100.0	98.9	1.1	1.1
3/4"	83.6	100.0	100.0	92.5	6.4	7.5
1/2"	35.2	93.3	100.0	69.3	23.1	30.7
3/8"	15.6	81.7	100.0	58.7	10.6	41.3
#4	3.0	24.3	95.5	43.2	15.5	56.8
#8	2.1	7.7	82.9	35.5	7.8	64.5
#16	1.9	3.5	68.2	28.9	6.6	71.1
#30	1.8	2.5	48.9	20.9	8.0	79.1
#50	1.7	2.2	23.6	10.6	10.3	89.4
#100	1.6	2.0	6.4	3.6	7.0	96.4
LBW	1.2	1.7	0.6	1.0	2.6	99.0

\*Maximum % Retained must be above the 3/8" sieve.  
 \*Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation  Batch Plant Gradations  Aggregate Supplier Gradations

**Coarseness Factor:** **64**      **Workability Factor:** **35**

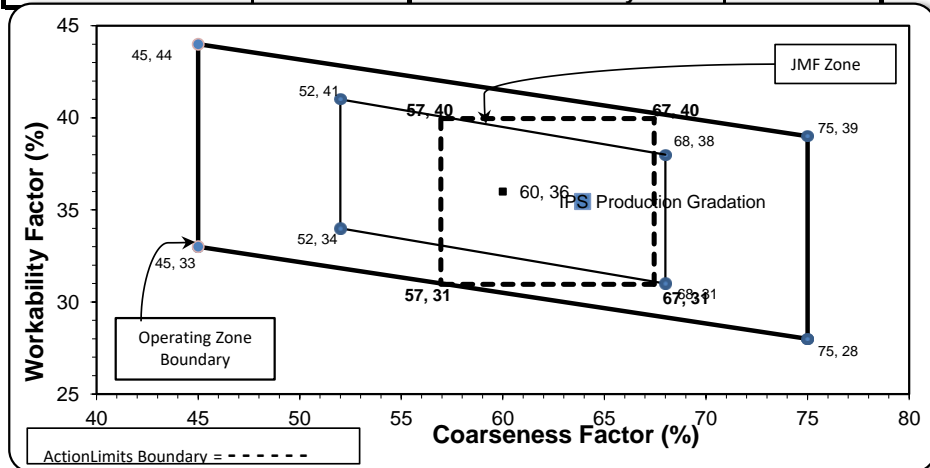

Initial Production Sample (IPS)

**Coarseness Factor:** **62**  
**Workability Factor:** **35**

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	100.0	0.0	0.0
3/4"	94.0	6.0	6.0
1/2"	70.2	23.7	29.8
3/8"	59.9	10.4	40.1
#4	42.7	17.2	57.3
#8	35.5	7.2	64.5
#16	28.4	7.0	71.6
#30	19.2	9.2	80.8
#50	8.9	10.3	91.1
#100	3.1	5.9	96.9
LBW	1.4	1.7	98.6

PREPARED BY:  
 SM, LLC Technical Service

Approved By:

# Aggregate Optimization Chart

**PLANT #:** **P-35**

Sample Date: 6/20/22

Concrete Grade: **S2M, 3500HP**

Dates Test Represents: 6/21/2022 through 6/27/2022

Contractor: \_\_\_\_\_

MDOT No.: \_\_\_\_\_

Agg. Class	Pit #	Source	Weight (SSD)	ft <sup>3</sup>	Specific Gravity	% Contribution
6AA	58-003	Stoneco	1650	9.83	2.69	53.2
26A	58-003	Stoneco	250	1.49	2.69	8.1
2NS	81-019	Pleasant Lake	1200	7.26	2.65	38.7
<b>Total Wt</b>			<b>3100</b>	<b>18.58</b>		<b>100.0</b>

<----- Verify this number is 100%




**Superior Materials, LLC**  
 30701 W. 10 Mile Rd.  
 Suite 500  
 Farmington Hills, MI 48336

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	100.0	100.0	100.0	100.0	0.0	0.0
3/4"	80.7	100.0	100.0	89.7	10.3	10.3
1/2"	47.5	99.6	100.0	72.0	17.7	28.0
3/8"	28.1	75.8	100.0	59.8	12.2	40.2
#4	5.1	13.4	99.4	42.3	17.5	57.7
#8	1.8	4.6	81.4	32.8	9.4	67.2
#16	1.3	2.9	63.2	25.4	7.4	74.6
#30	1.0	2.5	45.3	18.3	7.1	81.7
#50	1.0	2.2	22.7	9.5	8.8	90.5
#100	0.9	2.0	7.3	3.5	6.0	96.5
LBW	0.8	1.8	1.4	1.1	2.4	98.9

\*Maximum % Retained must be above the 3/8" sieve.  
 \*Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation  Batch Plant Gradations  Aggregate Supplier Gradations

**Coarseness Factor:** **60**      **Workability Factor:** **33**

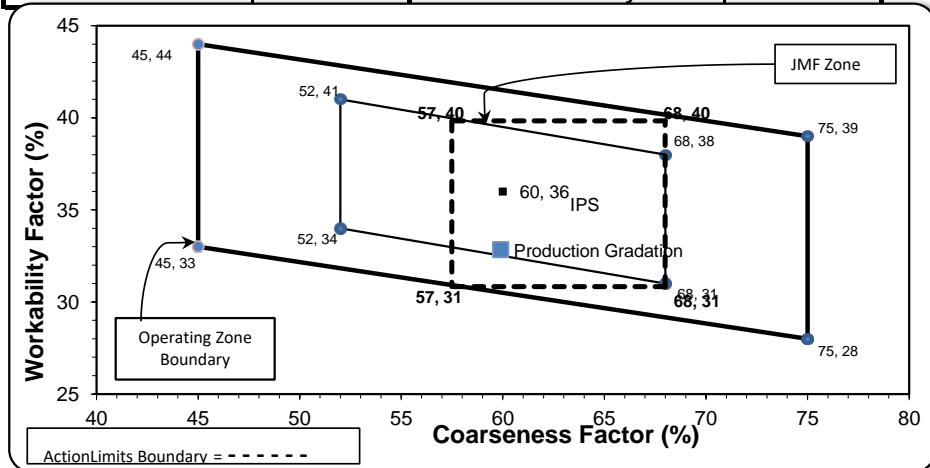

Initial Production Sample (IPS)

**Coarseness Factor:** **63**  
**Workability Factor:** **35**

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	99.2	0.8	0.8
3/4"	90.9	8.3	9.1
1/2"	71.3	19.6	28.7
3/8"	59.4	11.9	40.6
#4	43.0	16.5	57.0
#8	35.3	7.6	64.7
#16	28.2	7.1	71.8
#30	21.6	6.6	78.4
#50	9.1	12.5	90.9
#100	1.7	7.4	98.3
LBW	1.1	0.6	98.9

PREPARED BY:  
 SM, LLC Technical Service

Approved By:

# Aggregate Optimization Chart

**PLANT #:** **P-39**

Sample Date: 6/20/22

Concrete Grade: **S2M, 3500HP**

Dates Test Represents: 6/21/2022 through 6/27/2022

Contractor: \_\_\_\_\_

MDOT No.: \_\_\_\_\_

Agg. Class	Pit #	Source	Weight (SSD)	ft <sup>3</sup>	Specific Gravity	% Contribution
6AA	71-47	Presque Isle	1600	9.79	2.62	52.5
26A	71-47	Presque Isle	200	1.22	2.62	6.6
2NS	44-051	Krake Willis Rd	1250	7.56	2.65	41.0
<b>Total Wt</b>			<b>3050</b>	<b>18.57</b>		<b>100.0</b>

<----- Verify this number is 100%




**Superior Materials, LLC**  
 30701 W. 10 Mile Rd.  
 Suite 500  
 Farmington Hills, MI 48336

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	97.3	100.0	100.0	98.6	1.4	1.4
3/4"	82.7	100.0	100.0	90.9	7.7	9.1
1/2"	41.6	97.6	100.0	69.2	21.7	30.8
3/8"	20.1	85.7	100.0	57.1	12.1	42.9
#4	3.5	24.8	96.3	42.9	14.2	57.1
#8	2.1	7.0	80.1	34.4	8.5	65.6
#16	1.7	3.6	63.8	27.3	7.1	72.7
#30	1.6	2.9	45.8	19.8	7.5	80.2
#50	1.5	2.6	21.2	9.6	10.2	90.4
#100	1.4	2.4	7.0	3.8	5.9	96.2
LBW	1.3	2.2	1.4	1.4	2.4	98.6

\*Maximum % Retained must be above the 3/8" sieve.  
 \*Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation  Batch Plant Gradations  Aggregate Supplier Gradations

**Coarseness Factor:** **65**      **Workability Factor:** **34**

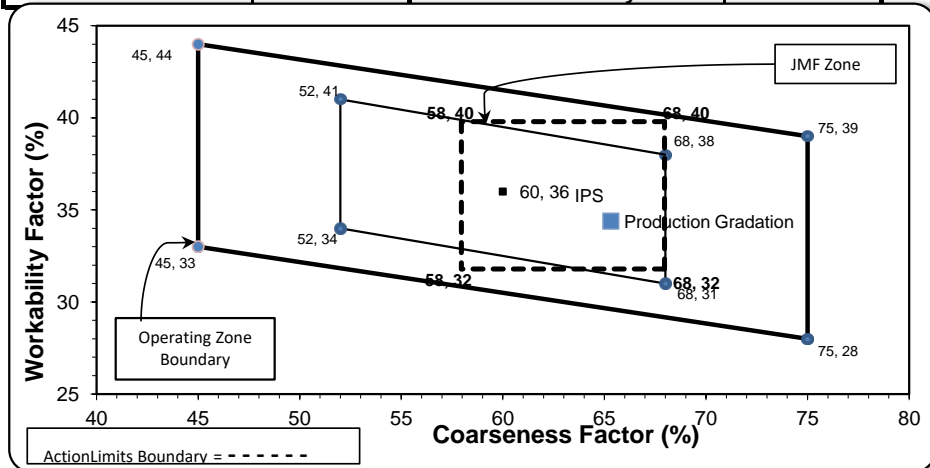

Initial Production Sample (IPS)

**Coarseness Factor:** **63**  
**Workability Factor:** **36**

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	100.0	0.0	0.0
3/4"	89.8	10.2	10.2
1/2"	70.7	19.1	29.3
3/8"	59.6	11.1	40.4
#4	43.2	16.4	56.8
#8	35.8	7.4	64.2
#16	29.2	6.6	70.8
#30	21.4	7.8	78.6
#50	9.8	11.6	90.2
#100	3.7	6.1	96.3
LBW	1.2	2.5	98.8

PREPARED BY:  
 SM, LLC Technical Service

Approved By:

# Aggregate Optimization Chart

**PLANT #:** P-02

Sample Date: 6/20/22

Concrete Grade: **S2M, 3500HP**

Dates Test Represents: 6/21/2022 through 6/27/2022

Contractor: \_\_\_\_\_

MDOT No.: \_\_\_\_\_



**Superior Materials, LLC**  
 30701 W. 10 Mile Rd.  
 Suite 500  
 Farmington Hills, MI 48336

Agg. Class	Pit #	Source	Weight (SSD)	ft <sup>3</sup>	Specific Gravity	% Contribution
6AA	71-47	Presque Isle	1500	9.17	2.62	49.2
26A	71-47	Presque Isle	300	1.83	2.62	9.8
2NS	63-115	Ray Rd	1250	7.56	2.65	41.0
<b>Total Wt</b>			<b>3050</b>	<b>18.57</b>		<b>100.0</b>


<----- Verify this number is 100%

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	99.4	100.0	100.0	99.7	0.3	0.3
3/4"	82.2	100.0	100.0	91.2	8.5	8.8
1/2"	44.0	93.3	100.0	71.8	19.4	28.2
3/8"	22.1	81.7	100.0	59.9	11.9	40.1
#4	4.7	24.3	97.3	44.6	15.3	55.4
#8	2.7	7.7	82.0	35.7	8.9	64.3
#16	2.3	3.5	65.0	28.1	7.6	71.9
#30	2.2	2.5	47.9	21.0	7.2	79.0
#50	2.1	2.2	25.0	11.5	9.5	88.5
#100	2.0	2.0	5.3	3.4	8.1	96.6
LBW	1.6	1.7	0.9	1.3	2.0	98.7

\*Maximum % Retained must be above the 3/8" sieve.  
 \*Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation  Batch Plant Gradations  Aggregate Supplier Gradations

<b>Coarseness Factor:</b>	<b>62</b>	<b>Workability Factor:</b>	<b>36</b>
---------------------------	-----------	----------------------------	-----------

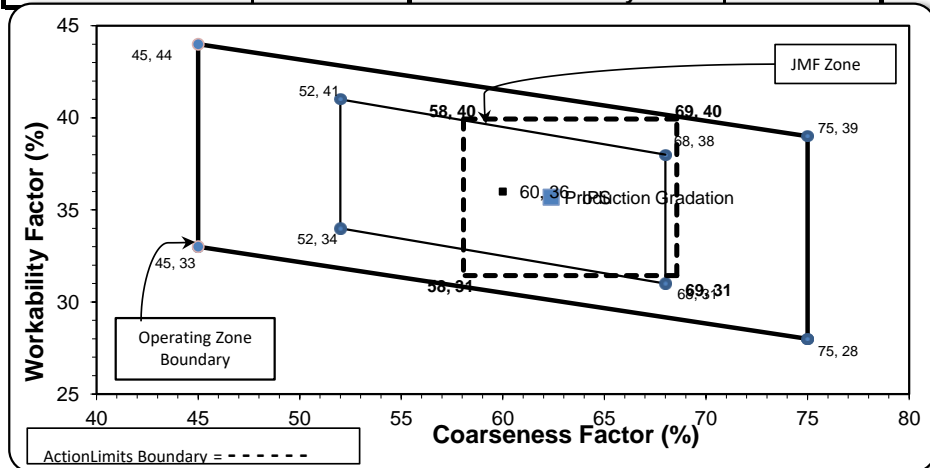

Initial Production Sample (IPS)

<b>Coarseness Factor:</b>	<b>63</b>		
<b>Workability Factor:</b>	<b>36</b>		
Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	100.0	0.0	0.0
3/4"	95.6	4.4	4.4
1/2"	73.1	22.6	26.9
3/8"	59.3	13.8	40.7
#4	42.8	16.5	57.2
#8	35.7	7.1	64.3
#16	28.9	6.8	71.1
#30	20.7	8.2	79.3
#50	9.9	10.8	90.1
#100	2.1	7.8	97.9
LBW	0.9	1.2	99.1

PREPARED BY:  
 SM, LLC Technical Service

Approved By:
