

Aggregate Optimization Chart

PLANT #: **P-101**

Sample Date: 9/26/22

Concrete Grade: **P1M, 3500HP**

Dates Test Represents: 9/27/2022 through 10/3/2022

Contractor: _____

MDOT No.: _____

Agg. Class	Pit #	Source	Weight (SSD)	ft ³	Specific Gravity	% Contribution
CA	71-47	Presque Isle	1070	6.54	2.62	34.9
IA	71-47	Presque Isle	800	4.89	2.62	26.1
2NS	75-051	Mid Michigan	1200	7.23	2.66	39.1
Total Wt			3070	18.67		100.0

<---- Verify this number is 100%



Superior Materials, LLC
 30701 W. 10 Mile Rd.
 Suite 500
 Farmington Hills, MI 48336

Sieve	CA	IA	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	98.7	100.0	100.0	99.5	0.5	0.5
1"	47.5	100.0	100.0	81.7	17.8	18.3
3/4"	12.4	98.5	100.0	69.1	12.6	30.9
1/2"	3.0	83.2	100.0	61.8	7.3	38.2
3/8"	2.0	63.7	100.0	56.4	5.4	43.6
#4	1.6	17.3	99.0	43.8	12.6	56.2
#8	1.4	4.5	84.3	34.6	9.2	65.4
#16	1.4	2.7	67.7	27.7	7.0	72.3
#30	1.3	2.3	49.4	20.4	7.3	79.6
#50	1.2	2.1	22.4	9.7	10.6	90.3
#100	1.1	1.9	6.0	3.2	6.5	96.8
LBW	0.9	1.7	1.0	1.1	2.1	98.9

*Maximum % Retained must be above the 3/8" sieve.
 *Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.


Production Gradation Batch Plant Gradations Aggregate Supplier Gradations

Coarseness Factor:	67	Workability Factor:	35
---------------------------	-----------	----------------------------	-----------

Initial Production Sample (IPS)

Coarseness Factor:	66
Workability Factor:	35

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	99.6	0.4	0.4
1"	84.3	15.3	15.7
3/4"	74.8	9.6	25.2
1/2"	64.3	10.4	35.7
3/8"	56.8	7.5	43.2
#4	43.0	13.8	57.0
#8	34.9	8.1	65.1
#16	26.4	8.5	73.6
#30	19.9	6.5	80.1
#50	10.4	9.5	89.6
#100	3.4	7.0	96.6
LBW	1.2	2.2	98.8

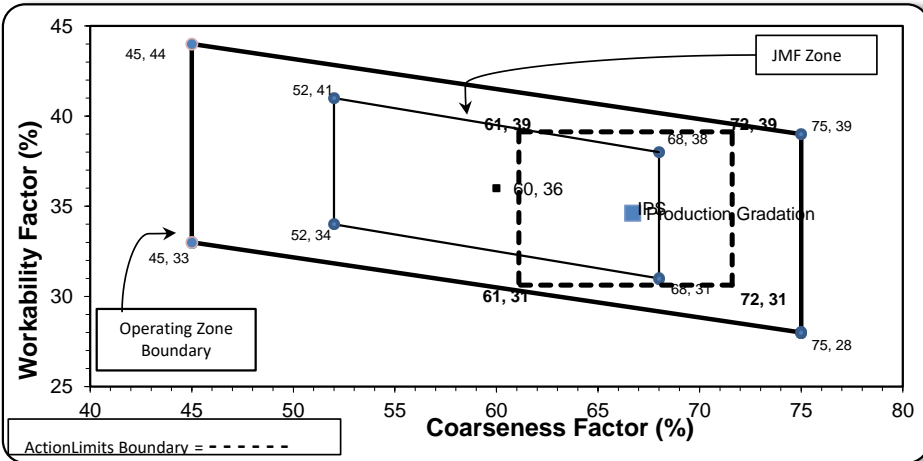

PREPARED BY:
 SM, LLC Technical Service

Approved By:

Aggregate Optimization Chart

PLANT #: **P-102**

Sample Date: 9/26/22

Concrete Grade: **P1M, 3500HP**

Dates Test Represents: 9/27/2022 through 10/3/2022

Contractor: _____

MDOT No.: _____

Agg. Class	Pit #	Source	Weight (SSD)	ft ³	Specific Gravity	% Contribution
CA	58-003	Stoneco	1370	8.16	2.69	43.9
IA	58-003	Stoneco	550	3.28	2.69	17.6
2NS	81-019	Pleasant Lake	1200	7.26	2.65	38.5
Total Wt			3120	18.70		100.0

<----- Verify this number is 100%




Superior Materials, LLC
 30701 W. 10 Mile Rd.
 Suite 500
 Farmington Hills, MI 48336

Sieve	CA	IA	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	61.7	100.0	100.0	83.2	16.8	16.8
3/4"	35.4	100.0	100.0	71.6	11.5	28.4
1/2"	13.0	92.2	100.0	60.4	11.2	39.6
3/8"	7.3	74.6	100.0	54.8	5.6	45.2
#4	2.6	19.4	98.8	42.6	12.3	57.4
#8	1.7	4.6	81.9	33.1	9.5	66.9
#16	1.5	2.5	61.8	24.9	8.2	75.1
#30	1.3	1.9	44.5	18.0	6.8	82.0
#50	1.2	1.6	20.0	8.5	9.5	91.5
#100	1.2	1.5	5.6	2.9	5.6	97.1
LBW	1.0	1.3	0.8	1.0	2.0	99.0

*Maximum % Retained must be above the 3/8" sieve.
 *Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation Batch Plant Gradations Aggregate Supplier Gradations

Coarseness Factor:	67	Workability Factor:	33
---------------------------	-----------	----------------------------	-----------

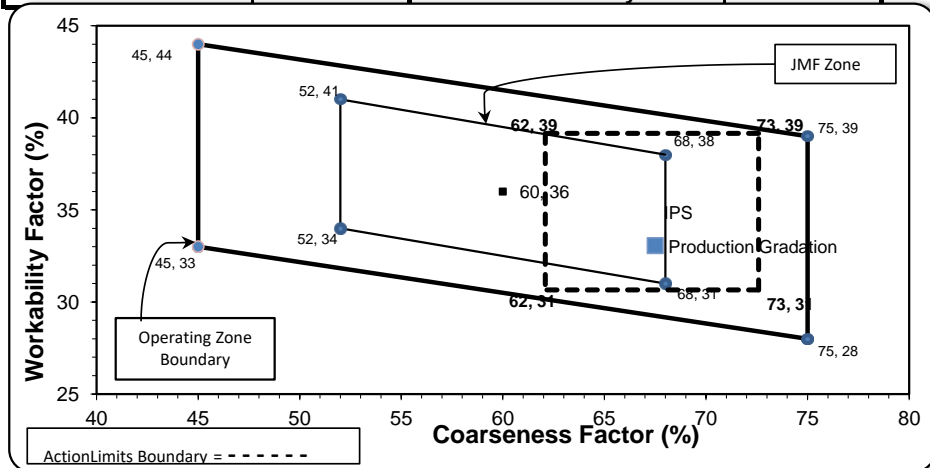

Initial Production Sample (IPS)

Coarseness Factor:	67		
Workability Factor:	35		
Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	85.5	14.5	14.5
3/4"	73.4	12.1	26.6
1/2"	61.0	12.4	39.0
3/8"	56.2	4.8	43.8
#4	43.1	13.1	56.9
#8	34.9	8.2	65.1
#16	29.4	5.5	70.6
#30	21.6	7.8	78.4
#50	8.1	13.4	91.9
#100	2.2	5.9	97.8
LBW	1.4	0.8	98.6

PREPARED BY:
 SM, LLC Technical Service

Approved By:

Aggregate Optimization Chart

PLANT #: **P-103**

Sample Date: 9/26/22

Concrete Grade: **P1M, 3500HP**

Dates Test Represents: 9/27/2022 through 10/3/2022

Contractor: _____

MDOT No.: _____

Agg. Class	Pit #	Source	Weight (SSD)	ft ³	Specific Gravity	% Contribution
CA	58-003	Stoneco	1370	8.16	2.69	43.9
IA	58-003	Stoneco	550	3.28	2.69	17.6
2NS	81-019	Pleasant Lake	1200	7.26	2.65	38.5
Total Wt			3120	18.70		100.0

<----- Verify this number is 100%




Superior Materials, LLC
 30701 W. 10 Mile Rd.
 Suite 500
 Farmington Hills, MI 48336

Sieve	CA	IA	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	61.7	100.0	100.0	83.2	16.8	16.8
3/4"	35.4	100.0	100.0	71.6	11.5	28.4
1/2"	13.0	92.2	100.0	60.4	11.2	39.6
3/8"	7.3	74.6	100.0	54.8	5.6	45.2
#4	2.6	19.4	98.8	42.6	12.3	57.4
#8	1.7	4.6	81.9	33.1	9.5	66.9
#16	1.5	2.5	61.8	24.9	8.2	75.1
#30	1.3	1.9	44.5	18.0	6.8	82.0
#50	1.2	1.6	20.0	8.5	9.5	91.5
#100	1.2	1.5	5.6	2.9	5.6	97.1
LBW	1.0	1.3	0.8	1.0	2.0	99.0

*Maximum % Retained must be above the 3/8" sieve.
 *Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation Batch Plant Gradations Aggregate Supplier Gradations

Coarseness Factor:	67	Workability Factor:	33
---------------------------	-----------	----------------------------	-----------

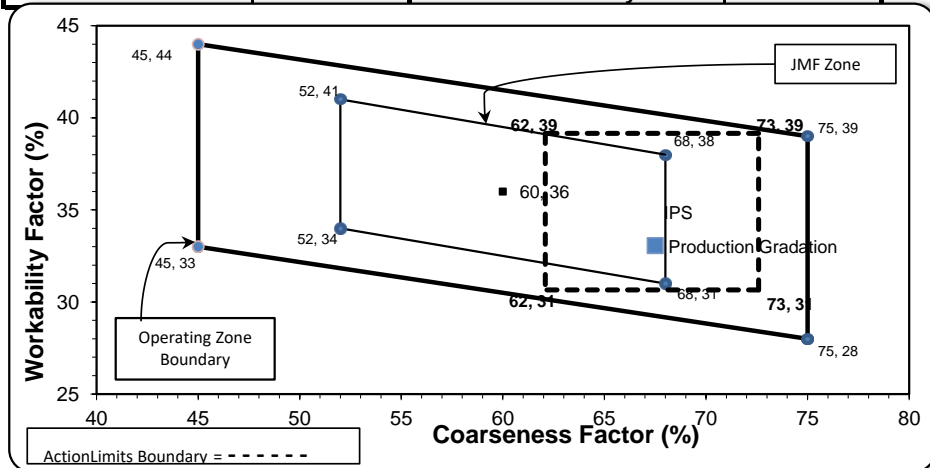

Initial Production Sample (IPS)

Coarseness Factor:	67		
Workability Factor:	35		
Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	85.5	14.5	14.5
3/4"	73.4	12.1	26.6
1/2"	61.0	12.4	39.0
3/8"	56.2	4.8	43.8
#4	43.1	13.1	56.9
#8	34.9	8.2	65.1
#16	29.4	5.5	70.6
#30	21.6	7.8	78.4
#50	8.1	13.4	91.9
#100	2.2	5.9	97.8
LBW	1.4	0.8	98.6

PREPARED BY:
 SM, LLC Technical Service

Approved BY:

Aggregate Optimization Chart

PLANT #: **P-14**

Sample Date: 9/26/22

Concrete Grade: **P1M, 3500HP**

Dates Test Represents: 9/27/2022 through 10/3/2022

Contractor: _____

MDOT No.: _____

Agg. Class	Pit #	Source	Weight (SSD)	ft ³	Specific Gravity	% Contribution
CA	58-003	Stoneco	1370	8.16	2.69	43.9
IA	58-003	Stoneco	550	3.28	2.69	17.6
2NS	19-55	Schlegel	1200	7.20	2.67	38.5
Total Wt			3120	18.64		100.0

<----- Verify this number is 100%




Builders Redi-Mix
 30701 W. 10 Mile Rd.
 Suite 500
 Farmington Hills, MI 48336

Sieve	CA	IA	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	61.7	100.0	100.0	83.2	16.8	16.8
3/4"	35.4	100.0	100.0	71.6	11.5	28.4
1/2"	13.0	92.2	100.0	60.4	11.2	39.6
3/8"	7.3	74.6	100.0	54.8	5.6	45.2
#4	2.6	19.4	100.0	43.0	11.8	57.0
#8	1.7	4.6	91.3	36.7	6.4	63.3
#16	1.5	2.5	71.6	28.6	8.0	71.4
#30	1.3	1.9	47.8	19.3	9.3	80.7
#50	1.2	1.6	15.8	6.9	12.4	93.1
#100	1.2	1.5	3.2	2.0	4.9	98.0
LBW	1.0	1.3	0.5	0.9	1.2	99.1

*Maximum % Retained must be above the 3/8" sieve.
 *Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation Batch Plant Gradations Aggregate Supplier Gradations

Coarseness Factor:	71	Workability Factor:	37
---------------------------	-----------	----------------------------	-----------

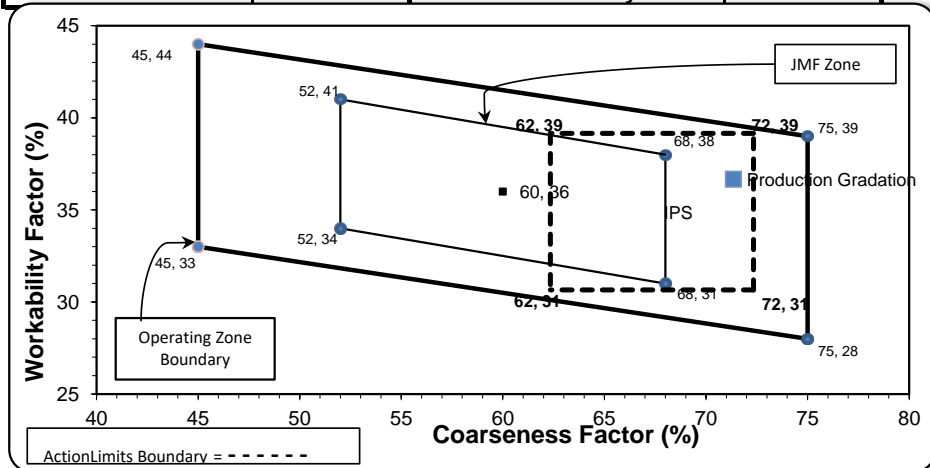

Initial Production Sample (IPS)

Coarseness Factor:	67		
Workability Factor:	35		
Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	85.5	14.5	14.5
3/4"	73.4	12.1	26.6
1/2"	61.0	12.4	39.0
3/8"	56.2	4.8	43.8
#4	43.1	13.1	56.9
#8	34.9	8.2	65.1
#16	29.4	5.5	70.6
#30	21.6	7.8	78.4
#50	8.1	13.4	91.9
#100	2.2	5.9	97.8
LBW	1.4	0.8	98.6

PREPARED BY:
 SM, LLC Technical Service

Approved By:

Aggregate Optimization Chart

PLANT #: **P-12**

Sample Date: 9/26/22

Concrete Grade: **P1M, 3500HP**

Contractor: _____

Dates Test Represents: 9/27/2022 through 10/3/2022

MDOT No.: _____

Agg. Class	Pit #	Source	Weight (SSD)	ft ³	Specific Gravity	% Contribution
CA	71-47	Presque Isle	1020	6.24	2.62	33.2
IA	71-47	Presque Isle	800	4.89	2.62	26.1
2NS	63-115	Ray Rd	1250	7.56	2.65	40.7
Total Wt			3070	18.69		100.0

<----- Verify this number is 100%




Superior Materials, LLC
 30701 W. 10 Mile Rd.
 Suite 500
 Farmington Hills, MI 48336

Sieve	CA	IA	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	94.7	100.0	100.0	98.2	1.8	1.8
1"	53.3	100.0	100.0	84.5	13.8	15.5
3/4"	18.2	99.1	100.0	72.6	11.9	27.4
1/2"	6.9	83.0	100.0	64.6	7.9	35.4
3/8"	5.7	61.9	100.0	58.7	5.9	41.3
#4	3.8	17.8	96.8	45.3	13.4	54.7
#8	3.1	5.3	80.5	35.2	10.1	64.8
#16	2.9	3.5	64.7	28.2	7.0	71.8
#30	2.7	3.1	48.7	21.5	6.7	78.5
#50	2.6	2.9	26.2	12.3	9.2	87.7
#100	2.4	2.7	6.4	4.1	8.2	95.9
LBW	1.9	2.4	0.9	1.6	2.5	98.4

*Maximum % Retained must be above the 3/8" sieve.
 *Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation Batch Plant Gradations Aggregate Supplier Gradations

Coarseness Factor:	64	Workability Factor:	35
---------------------------	-----------	----------------------------	-----------

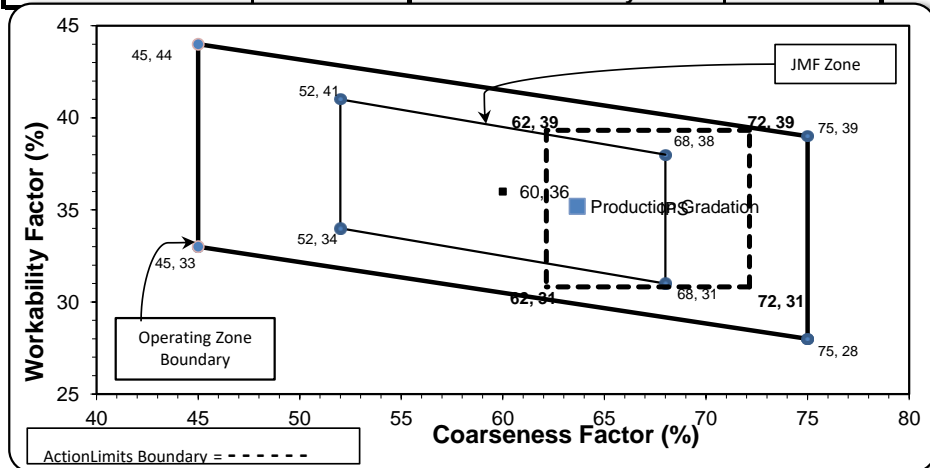

Initial Production Sample (IPS)

Coarseness Factor:	67		
Workability Factor:	35		
Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	99.6	0.4	0.4
1"	83.9	15.7	16.1
3/4"	74.0	9.8	26.0
1/2"	63.7	10.3	36.3
3/8"	56.4	7.3	43.6
#4	43.0	13.4	57.0
#8	35.1	7.9	64.9
#16	29.0	6.1	71.0
#30	20.9	8.0	79.1
#50	8.1	12.8	91.9
#100	1.6	6.5	98.4
LBW	0.9	0.8	99.1

PREPARED BY:
 SM, LLC Technical Service

Approved By:

Aggregate Optimization Chart

PLANT #: **P-32**

Sample Date: 9/26/22

Concrete Grade: **P1M, 3500HP**

Dates Test Represents: 9/27/2022 through 10/3/2022

Contractor: _____

MDOT No.: _____

Agg. Class	Pit #	Source	Weight (SSD)	ft ³	Specific Gravity	% Contribution
CA	71-47	Presque Isle	1050	6.42	2.62	34.2
IA	71-47	Presque Isle	770	4.71	2.62	25.1
2NS	95-013	Smelter Bay	1250	7.56	2.65	40.7
Total Wt			3070	18.69		100.0

<----- Verify this number is 100%




Superior Materials, LLC
 30701 W. 10 Mile Rd.
 Suite 500
 Farmington Hills, MI 48336

Sieve	CA	IA	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	94.7	100.0	100.0	98.2	1.8	1.8
1"	53.3	100.0	100.0	84.0	14.2	16.0
3/4"	18.2	99.1	100.0	71.8	12.2	28.2
1/2"	6.9	83.0	100.0	63.9	7.9	36.1
3/8"	5.7	61.9	100.0	58.2	5.7	41.8
#4	3.8	17.8	95.9	44.8	13.4	55.2
#8	3.1	5.3	83.6	36.4	8.4	63.6
#16	2.9	3.5	69.2	30.0	6.4	70.0
#30	2.7	3.1	50.4	22.2	7.8	77.8
#50	2.6	2.9	24.3	11.5	10.7	88.5
#100	2.4	2.7	6.9	4.3	7.2	95.7
LBW	1.9	2.4	1.3	1.8	2.5	98.2

*Maximum % Retained must be above the 3/8" sieve.
 *Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation Batch Plant Gradations Aggregate Supplier Gradations

Coarseness Factor: **66** **Workability Factor:** **36**

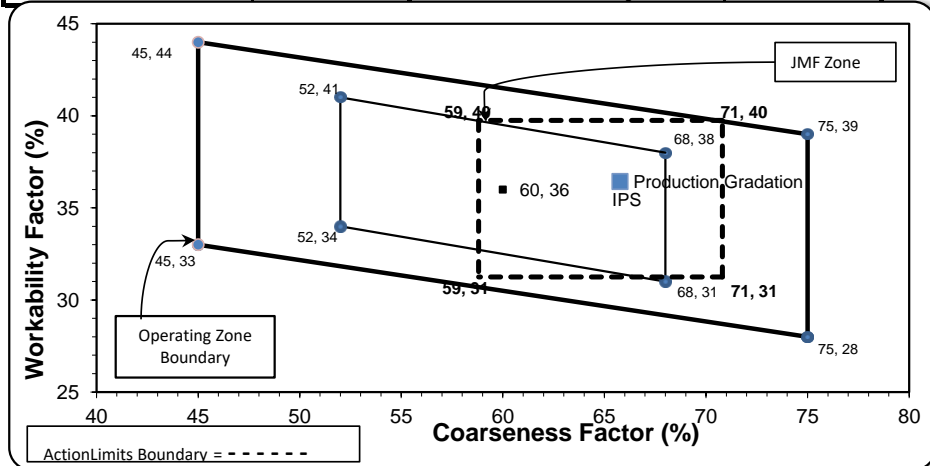

Initial Production Sample (IPS)

Coarseness Factor: **65**
Workability Factor: **36**

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	99.0	0.6	0.6
1"	84.0	15.3	16.0
3/4"	73.5	10.5	26.5
1/2"	65.2	8.2	34.8
3/8"	58.2	7.1	41.8
#4	44.1	14.1	55.9
#8	35.5	8.6	64.5
#16	29.1	6.4	70.9
#30	21.9	7.3	78.1
#50	9.6	12.2	90.4
#100	2.6	7.1	97.4
LBW	1.0	1.6	99.0

PREPARED BY:
 SM, LLC Technical Service

Approved By:

Aggregate Optimization Chart

PLANT #: **P-35**

Sample Date: 9/26/22

Concrete Grade: **P1M, 3500HP**

Dates Test Represents: 9/27/2022 through 10/3/2022

Contractor: _____

MDOT No.: _____

Agg. Class	Pit #	Source	Weight (SSD)	ft ³	Specific Gravity	% Contribution
CA	58-003	Stoneco	1370	8.16	2.69	43.9
IA	58-003	Stoneco	550	3.28	2.69	17.6
2NS	81-019	Pleasant Lake	1200	7.26	2.65	38.5
Total Wt			3120	18.70		100.0

<----- Verify this number is 100%




Superior Materials, LLC
 30701 W. 10 Mile Rd.
 Suite 500
 Farmington Hills, MI 48336

Sieve	CA	IA	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	61.7	100.0	100.0	83.2	16.8	16.8
3/4"	35.4	100.0	100.0	71.6	11.5	28.4
1/2"	13.0	92.2	100.0	60.4	11.2	39.6
3/8"	7.3	74.6	100.0	54.8	5.6	45.2
#4	2.6	19.4	98.8	42.6	12.3	57.4
#8	1.7	4.6	81.9	33.1	9.5	66.9
#16	1.5	2.5	61.8	24.9	8.2	75.1
#30	1.3	1.9	44.5	18.0	6.8	82.0
#50	1.2	1.6	20.0	8.5	9.5	91.5
#100	1.2	1.5	5.6	2.9	5.6	97.1
LBW	1.0	1.3	0.8	1.0	2.0	99.0

*Maximum % Retained must be above the 3/8" sieve.
 *Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation Batch Plant Gradations Aggregate Supplier Gradations

Coarseness Factor: **67** **Workability Factor:** **33**

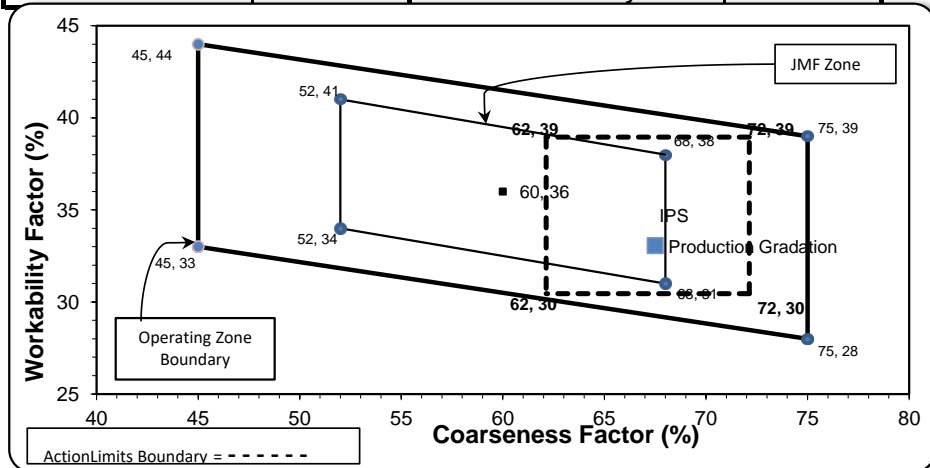

Initial Production Sample (IPS)

Coarseness Factor: **67**
Workability Factor: **35**

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	86.9	13.1	13.1
3/4"	76.1	10.8	23.9
1/2"	63.7	12.4	36.3
3/8"	56.2	7.5	43.8
#4	43.2	13.0	56.8
#8	34.7	8.5	65.3
#16	27.5	7.2	72.5
#30	20.6	7.0	79.4
#50	9.0	11.6	91.0
#100	2.1	6.9	97.9
LBW	1.0	1.1	99.0

PREPARED BY:
 SM, LLC Technical Service

Approved By:

Aggregate Optimization Chart

PLANT #: **P-36**

Sample Date: 9/26/22

Concrete Grade: **P1M, 3500HP**

Dates Test Represents: 9/27/2022 through 10/3/2022

Contractor: _____

MDOT No.: _____



Superior Materials, LLC
 30701 W. 10 Mile Rd.
 Suite 500
 Farmington Hills, MI 48336

Agg. Class	Pit #	Source	Weight (SSD)	ft ³	Specific Gravity	% Contribution
CA	71-47	Presque Isle	1050	6.42	2.62	34.2
IA	71-47	Presque Isle	820	5.02	2.62	26.7
2NS	63-92	Grange Hall	1200	7.26	2.65	39.1
Total Wt			3070	18.70		100.0


<----- Verify this number is 100%

Sieve	CA	IA	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	94.7	100.0	100.0	98.2	1.8	1.8
1"	53.3	100.0	100.0	84.0	14.2	16.0
3/4"	18.2	99.1	100.0	71.8	12.2	28.2
1/2"	6.9	83.0	100.0	63.6	8.2	36.4
3/8"	5.7	61.9	100.0	57.6	6.0	42.4
#4	3.8	17.8	97.3	44.1	13.5	55.9
#8	3.1	5.3	81.5	34.3	9.8	65.7
#16	2.9	3.5	66.5	27.9	6.4	72.1
#30	2.7	3.1	48.5	20.7	7.2	79.3
#50	2.6	2.9	20.2	9.6	11.1	90.4
#100	2.4	2.7	3.6	2.9	6.6	97.1
LBW	1.9	2.4	0.4	1.4	1.5	98.6

*Maximum % Retained must be above the 3/8" sieve.
 *Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation Batch Plant Gradations Aggregate Supplier Gradations

Coarseness Factor: **65** **Workability Factor:** **34**

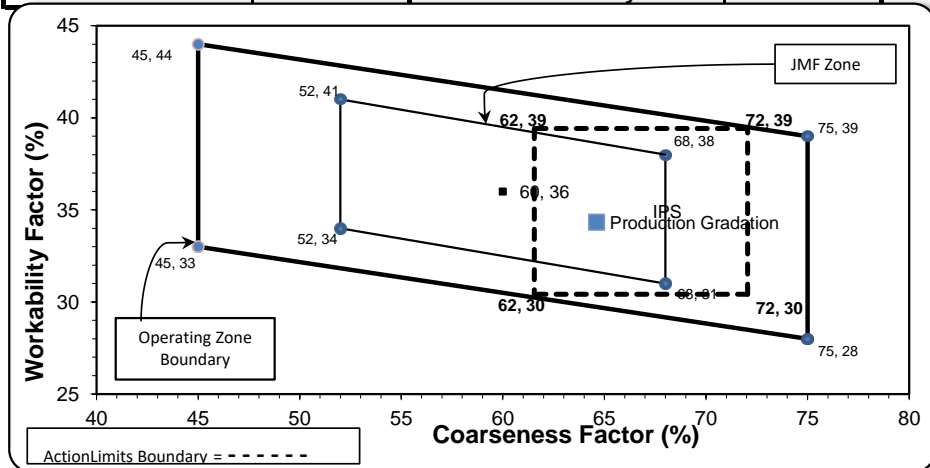

Initial Production Sample (IPS)

Coarseness Factor: **67**
Workability Factor: **35**

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	85.0	15.0	15.0
3/4"	72.1	12.9	27.9
1/2"	64.5	7.6	35.5
3/8"	56.5	8.0	43.5
#4	42.7	13.8	57.3
#8	34.9	7.8	65.1
#16	29.0	5.9	71.0
#30	21.0	8.0	79.0
#50	8.2	12.8	91.8
#100	1.6	6.5	98.4
LBW	0.7	0.9	99.3

PREPARED BY:
 SM, LLC Technical Service

Approved By:

Aggregate Optimization Chart

PLANT #: **P-39**

Sample Date: 9/26/22

Concrete Grade: **P1M, 3500HP**

Dates Test Represents: 9/27/2022 through 10/3/2022

Contractor: _____

MDOT No.: _____

Agg. Class	Pit #	Source	Weight (SSD)	ft ³	Specific Gravity	% Contribution
CA	71-47	Presque Isle	1020	6.24	2.62	33.2
IA	71-47	Presque Isle	800	4.89	2.62	26.1
2NS	44-051	Krake Willis Rd	1250	7.56	2.65	40.7
Total Wt			3070	18.69		100.0

<----- Verify this number is 100%




Superior Materials, LLC
 30701 W. 10 Mile Rd.
 Suite 500
 Farmington Hills, MI 48336

Sieve	CA	IA	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	98.7	100.0	100.0	99.6	0.4	0.4
1"	47.5	100.0	100.0	82.6	17.0	17.4
3/4"	12.4	98.5	100.0	70.5	12.1	29.5
1/2"	3.0	83.2	100.0	63.4	7.1	36.6
3/8"	2.0	63.7	100.0	58.0	5.4	42.0
#4	1.6	17.3	96.2	44.2	13.8	55.8
#8	1.4	4.5	80.6	34.5	9.8	65.5
#16	1.4	2.7	65.9	28.0	6.5	72.0
#30	1.3	2.3	50.9	21.8	6.2	78.2
#50	1.2	2.1	27.6	12.2	9.6	87.8
#100	1.1	1.9	8.4	4.3	7.9	95.7
LBW	0.9	1.7	1.6	1.4	2.9	98.6

*Maximum % Retained must be above the 3/8" sieve.
 *Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation Batch Plant Gradations Aggregate Supplier Gradations

Coarseness Factor:	64	Workability Factor:	34
---------------------------	-----------	----------------------------	-----------

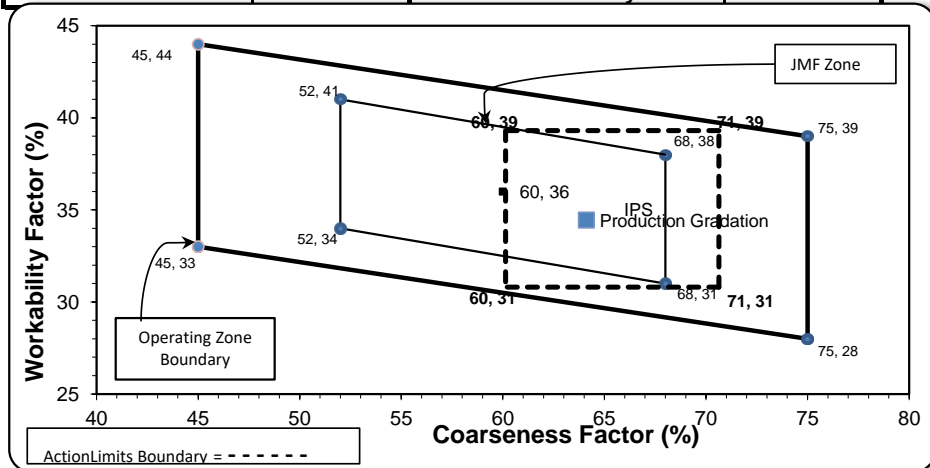

Initial Production Sample (IPS)

Coarseness Factor:	65
Workability Factor:	35

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	99.6	0.4	0.4
1"	83.9	15.7	16.1
3/4"	74.1	9.8	25.9
1/2"	64.3	9.7	35.7
3/8"	57.5	6.8	42.5
#4	44.5	13.1	55.5
#8	35.1	9.4	64.9
#16	27.9	7.2	72.1
#30	21.7	6.2	78.3
#50	12.6	9.1	87.4
#100	3.5	9.1	96.5
LBW	1.2	2.4	98.8

PREPARED BY:
 SM, LLC Technical Service

Approved By:

Aggregate Optimization Chart

PLANT #: **P-O2**

Sample Date: 9/26/22

Concrete Grade: **P1M, 3500HP**

Dates Test Represents: 9/27/2022 through 10/3/2022

Contractor: _____

MDOT No.: _____

Agg. Class	Pit #	Source	Weight (SSD)	ft ³	Specific Gravity	% Contribution
CA	71-47	Presque Isle	1050	6.42	2.62	34.2
IA	71-47	Presque Isle	770	4.71	2.62	25.1
2NS	63-115	Ray Rd	1250	7.56	2.65	40.7
Total Wt			3070	18.69		100.0

<----- Verify this number is 100%




Superior Materials, LLC
 30701 W. 10 Mile Rd.
 Suite 500
 Farmington Hills, MI 48336

Sieve	CA	IA	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	94.7	100.0	100.0	98.2	1.8	1.8
1"	53.3	100.0	100.0	84.0	14.2	16.0
3/4"	18.2	99.1	100.0	71.8	12.2	28.2
1/2"	6.9	83.0	100.0	63.9	7.9	36.1
3/8"	5.7	61.9	100.0	58.2	5.7	41.8
#4	3.8	17.8	96.8	45.2	13.0	54.8
#8	3.1	5.3	80.5	35.2	10.0	64.8
#16	2.9	3.5	64.7	28.2	7.0	71.8
#30	2.7	3.1	48.7	21.5	6.7	78.5
#50	2.6	2.9	26.2	12.3	9.2	87.7
#100	2.4	2.7	6.4	4.1	8.2	95.9
LBW	1.9	2.4	0.9	1.6	2.5	98.4

*Maximum % Retained must be above the 3/8" sieve.
 *Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation Batch Plant Gradations Aggregate Supplier Gradations

Coarseness Factor: **64** **Workability Factor:** **35**

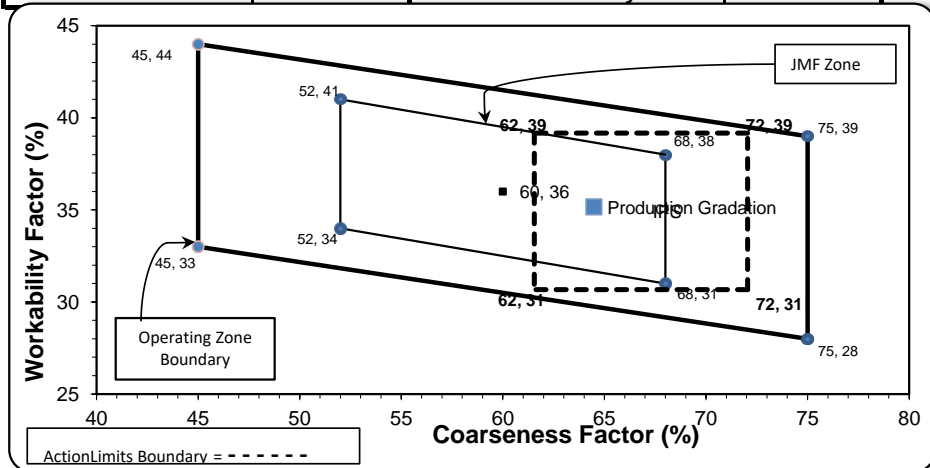

Initial Production Sample (IPS)

Coarseness Factor: **67**
Workability Factor: **35**

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	85.0	15.0	15.0
3/4"	72.3	12.7	27.7
1/2"	64.5	7.8	35.5
3/8"	56.5	8.0	43.5
#4	42.7	13.8	57.3
#8	34.9	7.8	65.1
#16	29.0	5.9	71.0
#30	21.0	8.0	79.0
#50	8.2	12.8	91.8
#100	1.6	6.5	98.4
LBW	0.7	0.9	99.3

PREPARED BY:
 SM, LLC Technical Service

Approved By:
