

Aggregate Optimization Chart

PLANT #: **P-101**

Sample Date: 12/12/22

Concrete Grade: **P1M, 3500HP**

Dates Test Represents: 12/13/2022 through 12/19/2022

Contractor: _____

MDOT No.: _____

Agg. Class	Pit #	Source	Weight (SSD)	ft ³	Specific Gravity	% Contribution
CA	71-47	Presque Isle	1070	6.54	2.62	34.9
IA	71-47	Presque Isle	800	4.89	2.62	26.1
2NS	75-051	Mid Michigan	1200	7.23	2.66	39.1
Total Wt			3070	18.67		100.0

<---- Verify this number is 100%



Superior Materials, LLC
 30701 W. 10 Mile Rd.
 Suite 500
 Farmington Hills, MI 48336

Sieve	CA	IA	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	98.7	100.0	100.0	99.5	0.5	0.5
1"	47.5	100.0	100.0	81.7	17.8	18.3
3/4"	12.4	98.5	100.0	69.1	12.6	30.9
1/2"	3.0	83.2	100.0	61.8	7.3	38.2
3/8"	2.0	63.7	100.0	56.4	5.4	43.6
#4	1.6	17.3	98.0	43.4	13.0	56.6
#8	1.4	4.5	83.0	34.1	9.3	65.9
#16	1.4	2.7	68.3	27.9	6.2	72.1
#30	1.3	2.3	52.0	21.4	6.5	78.6
#50	1.2	2.1	27.1	11.6	9.8	88.4
#100	1.1	1.9	8.4	4.2	7.4	95.8
LBW	0.9	1.7	1.7	1.4	2.7	98.6

*Maximum % Retained must be above the 3/8" sieve.
 *Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation Batch Plant Gradations Aggregate Supplier Gradations


Coarseness Factor: **66** **Workability Factor:** **34**

Initial Production Sample (IPS)

Coarseness Factor: **66**

Workability Factor: **35**

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	99.6	0.4	0.4
1"	84.3	15.3	15.7
3/4"	74.8	9.6	25.2
1/2"	64.3	10.4	35.7
3/8"	56.8	7.5	43.2
#4	43.0	13.8	57.0
#8	34.9	8.1	65.1
#16	26.4	8.5	73.6
#30	19.9	6.5	80.1
#50	10.4	9.5	89.6
#100	3.4	7.0	96.6
LBW	1.2	2.2	98.8

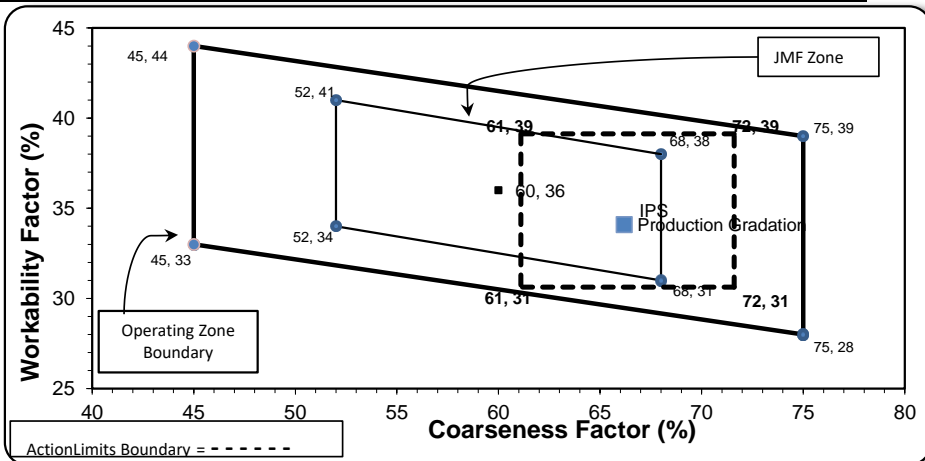

PREPARED BY:
 SM, LLC Technical Service

Approved By:

Aggregate Optimization Chart

PLANT #: **P-102**

Sample Date: 12/12/22

Concrete Grade: **P1M, 3500HP**

Dates Test Represents: 12/13/2022 through 12/19/2022

Contractor: _____

MDOT No.: _____

Agg. Class	Pit #	Source	Weight (SSD)	ft ³	Specific Gravity	% Contribution
CA	58-003	Stoneco	1370	8.16	2.69	43.9
IA	58-003	Stoneco	550	3.28	2.69	17.6
2NS	81-019	Pleasant Lake	1200	7.26	2.65	38.5
Total Wt			3120	18.70		100.0

<----- Verify this number is 100%




Superior Materials, LLC
 30701 W. 10 Mile Rd.
 Suite 500
 Farmington Hills, MI 48336

Sieve	CA	IA	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	67.6	100.0	100.0	85.8	14.2	14.2
3/4"	39.1	100.0	100.0	73.3	12.5	26.7
1/2"	13.0	92.9	100.0	60.5	12.7	39.5
3/8"	4.8	74.6	100.0	53.7	6.8	46.3
#4	3.7	22.0	97.9	43.2	10.6	56.8
#8	2.2	6.4	83.2	34.1	9.1	65.9
#16	2.6	4.2	66.3	27.4	6.7	72.6
#30	2.2	3.2	48.0	20.0	7.4	80.0
#50	2.1	2.8	23.4	10.4	9.6	89.6
#100	2.0	2.5	6.6	3.9	6.6	96.1
LBW	1.3	2.0	1.7	1.6	2.3	98.4

*Maximum % Retained must be above the 3/8" sieve.
 *Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation Batch Plant Gradations Aggregate Supplier Gradations

Coarseness Factor: **70** **Workability Factor:** **34**

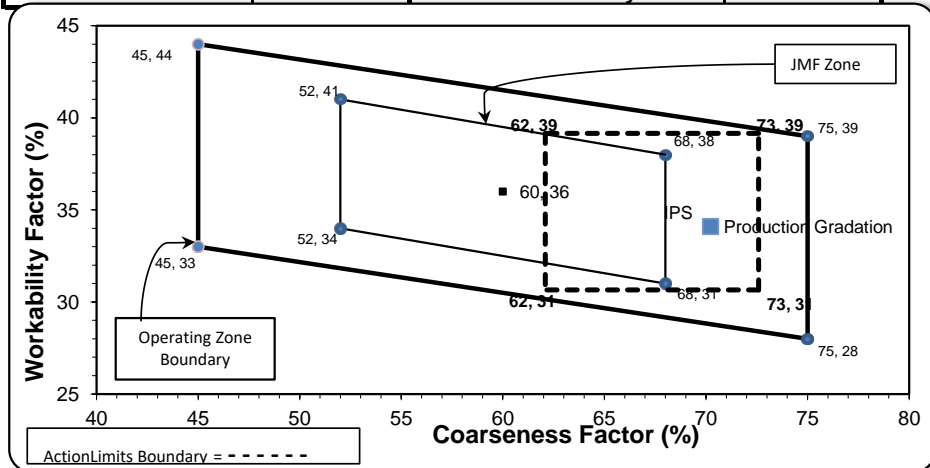

Initial Production Sample (IPS)

Coarseness Factor: **67**
Workability Factor: **35**

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	85.5	14.5	14.5
3/4"	73.4	12.1	26.6
1/2"	61.0	12.4	39.0
3/8"	56.2	4.8	43.8
#4	43.1	13.1	56.9
#8	34.9	8.2	65.1
#16	29.4	5.5	70.6
#30	21.6	7.8	78.4
#50	8.1	13.4	91.9
#100	2.2	5.9	97.8
LBW	1.4	0.8	98.6

PREPARED BY:
 SM, LLC Technical Service

Approved By:

Aggregate Optimization Chart

PLANT #: **P-103**

Sample Date: 12/12/22

Concrete Grade: **P1M, 3500HP**

Dates Test Represents: 12/13/2022 through 12/19/2022

Contractor: _____

MDOT No.: _____

Agg. Class	Pit #	Source	Weight (SSD)	ft ³	Specific Gravity	% Contribution
CA	58-003	Stoneco	1370	8.16	2.69	43.9
IA	58-003	Stoneco	550	3.28	2.69	17.6
2NS	81-019	Pleasant Lake	1200	7.26	2.65	38.5
Total Wt			3120	18.70		100.0

<----- Verify this number is 100%




Superior Materials, LLC
 30701 W. 10 Mile Rd.
 Suite 500
 Farmington Hills, MI 48336

Sieve	CA	IA	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	67.6	100.0	100.0	85.8	14.2	14.2
3/4"	39.1	100.0	100.0	73.3	12.5	26.7
1/2"	13.0	92.9	100.0	60.5	12.7	39.5
3/8"	4.8	74.6	100.0	53.7	6.8	46.3
#4	3.7	22.0	97.9	43.2	10.6	56.8
#8	2.2	6.4	83.2	34.1	9.1	65.9
#16	2.6	4.2	66.3	27.4	6.7	72.6
#30	2.2	3.2	48.0	20.0	7.4	80.0
#50	2.1	2.8	23.4	10.4	9.6	89.6
#100	2.0	2.5	6.6	3.9	6.6	96.1
LBW	1.3	2.0	1.7	1.6	2.3	98.4

*Maximum % Retained must be above the 3/8" sieve.
 *Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation Batch Plant Gradations Aggregate Supplier Gradations

Coarseness Factor:	70	Workability Factor:	34
---------------------------	-----------	----------------------------	-----------

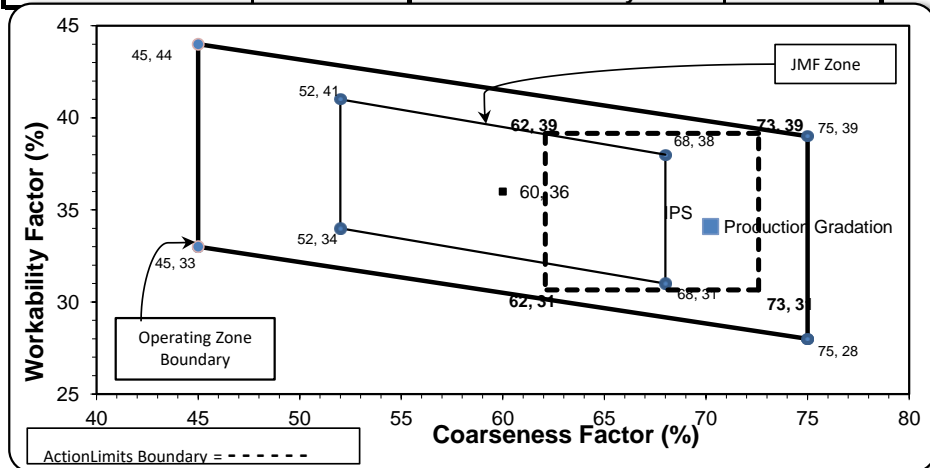

Initial Production Sample (IPS)

Coarseness Factor:	67
Workability Factor:	35

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	85.5	14.5	14.5
3/4"	73.4	12.1	26.6
1/2"	61.0	12.4	39.0
3/8"	56.2	4.8	43.8
#4	43.1	13.1	56.9
#8	34.9	8.2	65.1
#16	29.4	5.5	70.6
#30	21.6	7.8	78.4
#50	8.1	13.4	91.9
#100	2.2	5.9	97.8
LBW	1.4	0.8	98.6

PREPARED BY:
 SM, LLC Technical Service

Approved BY:

Aggregate Optimization Chart

PLANT #: P-14

Sample Date: 12/12/22

Concrete Grade: **P1M, 3500HP**

Dates Test Represents: 12/13/2022 through 12/19/2022

Contractor: _____

MDOT No.: _____

Agg. Class	Pit #	Source	Weight (SSD)	ft ³	Specific Gravity	% Contribution
CA	58-003	Stoneco	1300	7.74	2.69	41.7
IA	58-003	Stoneco	620	3.69	2.69	19.9
2NS	19-55	Schlegel	1200	7.20	2.67	38.5
Total Wt			3120	18.64		100.0

<----- Verify this number is 100%




Builders Redi-Mix
 30701 W. 10 Mile Rd.
 Suite 500
 Farmington Hills, MI 48336

Sieve	CA	IA	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	67.6	100.0	100.0	86.5	13.5	13.5
3/4"	39.1	100.0	100.0	74.6	11.9	25.4
1/2"	13.0	92.9	100.0	62.3	12.3	37.7
3/8"	4.8	74.6	100.0	55.3	7.1	44.7
#4	3.7	22.0	99.9	44.3	10.9	55.7
#8	2.2	6.4	90.1	36.8	7.5	63.2
#16	2.6	4.2	69.4	28.6	8.2	71.4
#30	2.2	3.2	44.5	18.7	9.9	81.3
#50	2.1	2.8	14.3	6.9	11.7	93.1
#100	2.0	2.5	2.7	2.4	4.6	97.6
LBW	1.3	2.0	0.2	1.0	1.4	99.0

*Maximum % Retained must be above the 3/8" sieve.
 *Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation Batch Plant Gradations Aggregate Supplier Gradations

Coarseness Factor:	71	Workability Factor:	37
---------------------------	-----------	----------------------------	-----------

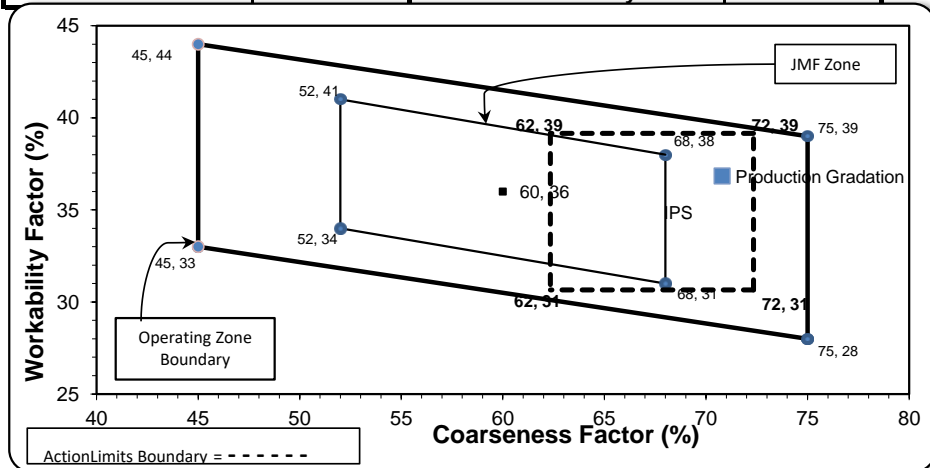

Initial Production Sample (IPS)

Coarseness Factor:	67		
Workability Factor:	35		
Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	85.5	14.5	14.5
3/4"	73.4	12.1	26.6
1/2"	61.0	12.4	39.0
3/8"	56.2	4.8	43.8
#4	43.1	13.1	56.9
#8	34.9	8.2	65.1
#16	29.4	5.5	70.6
#30	21.6	7.8	78.4
#50	8.1	13.4	91.9
#100	2.2	5.9	97.8
LBW	1.4	0.8	98.6

PREPARED BY:
 SM, LLC Technical Service

Approved By:

Aggregate Optimization Chart

PLANT #: P-12

Sample Date: 12/12/22

Concrete Grade: **P1M, 3500HP**

Dates Test Represents: 12/13/2022 through 12/19/2022

Contractor: _____

MDOT No.: _____

Agg. Class	Pit #	Source	Weight (SSD)	ft ³	Specific Gravity	% Contribution
CA	71-47	Presque Isle	1020	6.24	2.62	33.2
IA	71-47	Presque Isle	800	4.89	2.62	26.1
2NS	63-115	Ray Rd	1250	7.56	2.65	40.7
Total Wt			3070	18.69		100.0

<----- Verify this number is 100%




Superior Materials, LLC
 30701 W. 10 Mile Rd.
 Suite 500
 Farmington Hills, MI 48336

Sieve	CA	IA	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	96.8	100.0	100.0	98.9	1.1	1.1
1"	44.4	100.0	100.0	81.5	17.4	18.5
3/4"	22.1	98.9	100.0	73.8	7.7	26.2
1/2"	11.4	78.2	100.0	64.9	8.9	35.1
3/8"	7.5	53.7	100.0	57.2	7.7	42.8
#4	3.3	9.9	96.9	43.1	14.1	56.9
#8	2.6	3.6	81.0	34.8	8.3	65.2
#16	2.4	2.6	65.7	28.2	6.6	71.8
#30	2.2	2.4	50.0	21.7	6.5	78.3
#50	2.1	2.2	26.4	12.0	9.7	88.0
#100	1.9	2.1	4.2	2.9	9.1	97.1
LBW	1.5	1.7	0.6	1.2	1.7	98.8

*Maximum % Retained must be above the 3/8" sieve.
 *Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation Batch Plant Gradations Aggregate Supplier Gradations

Coarseness Factor: 66 **Workability Factor:** 35

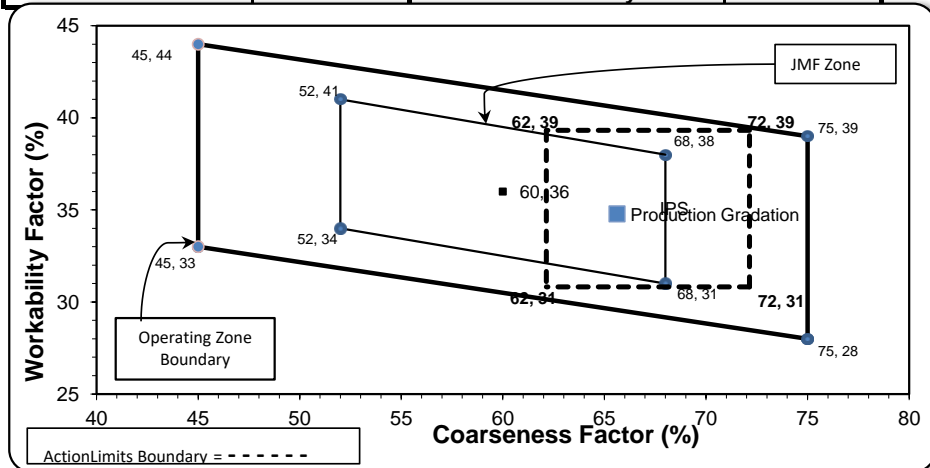

Initial Production Sample (IPS)

Coarseness Factor: 67
Workability Factor: 35

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	99.6	0.4	0.4
1"	83.9	15.7	16.1
3/4"	74.0	9.8	26.0
1/2"	63.7	10.3	36.3
3/8"	56.4	7.3	43.6
#4	43.0	13.4	57.0
#8	35.1	7.9	64.9
#16	29.0	6.1	71.0
#30	20.9	8.0	79.1
#50	8.1	12.8	91.9
#100	1.6	6.5	98.4
LBW	0.9	0.8	99.1

PREPARED BY:
 SM, LLC Technical Service

Approved By:

Aggregate Optimization Chart

PLANT #: 11

Sample Date: 12/12/22

Concrete Grade: **P1M, 3500HP**

Dates Test Represents: 12/13/2022 through 12/19/2022

Contractor: _____

MDOT No.: _____

Agg. Class	Pit #	Source	Weight (SSD)	ft ³	Specific Gravity	% Contribution
CA	71-47	Presque Isle	970	5.93	2.62	31.6
IA	71-47	Presque Isle	850	5.20	2.62	27.7
2NS	95-013	Smelter Bay	1250	7.56	2.65	40.7
Total Wt			3070	18.69		100.0

<----- Verify this number is 100%




Superior Materials, LLC
 30701 W. 10 Mile Rd.
 Suite 500
 Farmington Hills, MI 48336

Sieve	CA	IA	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	96.8	100.0	100.0	99.0	1.0	1.0
1"	44.4	100.0	100.0	82.4	16.6	17.6
3/4"	22.1	98.9	100.0	75.1	7.4	24.9
1/2"	11.4	78.2	100.0	66.0	9.1	34.0
3/8"	7.5	53.7	100.0	58.0	8.0	42.0
#4	3.3	9.9	98.4	43.8	14.1	56.2
#8	2.6	3.6	84.2	36.1	7.7	63.9
#16	2.4	2.6	67.9	29.1	7.0	70.9
#30	2.2	2.4	49.9	21.7	7.4	78.3
#50	2.1	2.2	24.6	11.3	10.4	88.7
#100	1.9	2.1	7.3	4.2	7.1	95.8
LBW	1.5	1.7	1.8	1.7	2.5	98.3

*Maximum % Retained must be above the 3/8" sieve.
 *Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation Batch Plant Gradations Aggregate Supplier Gradations

Coarseness Factor: 66 **Workability Factor:** 36

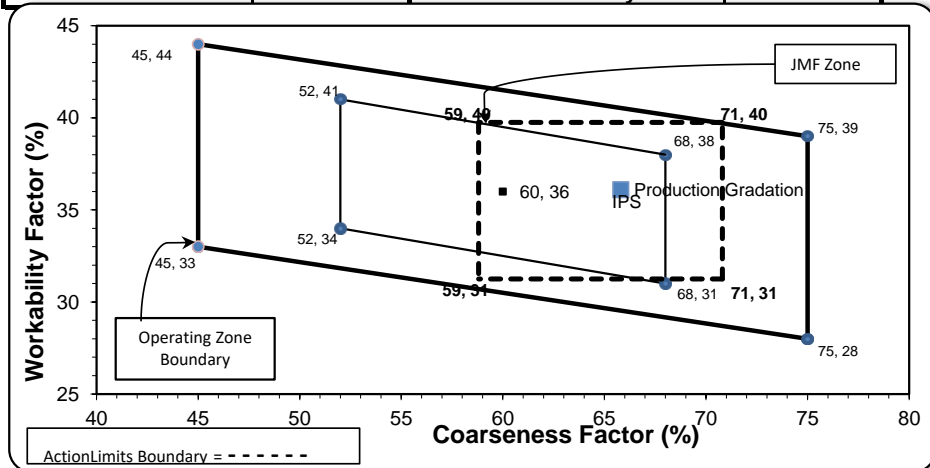

Initial Production Sample (IPS)

Coarseness Factor: <u>65</u>		Workability Factor: <u>36</u>	
Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	99.0	0.6	0.6
1"	84.0	15.3	16.0
3/4"	73.5	10.5	26.5
1/2"	65.2	8.2	34.8
3/8"	58.2	7.1	41.8
#4	44.1	14.1	55.9
#8	35.5	8.6	64.5
#16	29.1	6.4	70.9
#30	21.9	7.3	78.1
#50	9.6	12.2	90.4
#100	2.6	7.1	97.4
LBW	1.0	1.6	99.0

PREPARED BY:
 SM, LLC Technical Service

Approved By:

Aggregate Optimization Chart

PLANT #: **P-32**

Sample Date: 12/12/22

Concrete Grade: **P1M, 3500HP**

Dates Test Represents: 12/13/2022 through 12/19/2022

Contractor: _____

MDOT No.: _____

Agg. Class	Pit #	Source	Weight (SSD)	ft ³	Specific Gravity	% Contribution
CA	71-47	Presque Isle	970	5.93	2.62	31.6
IA	71-47	Presque Isle	850	5.20	2.62	27.7
2NS	95-013	Smelter Bay	1250	7.56	2.65	40.7
Total Wt			3070	18.69		100.0

<----- Verify this number is 100%




Superior Materials, LLC
 30701 W. 10 Mile Rd.
 Suite 500
 Farmington Hills, MI 48336

Sieve	CA	IA	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	96.8	100.0	100.0	99.0	1.0	1.0
1"	44.4	100.0	100.0	82.4	16.6	17.6
3/4"	22.1	98.9	100.0	75.1	7.4	24.9
1/2"	11.4	78.2	100.0	66.0	9.1	34.0
3/8"	7.5	53.7	100.0	58.0	8.0	42.0
#4	3.3	9.9	98.4	43.8	14.1	56.2
#8	2.6	3.6	84.2	36.1	7.7	63.9
#16	2.4	2.6	67.9	29.1	7.0	70.9
#30	2.2	2.4	49.9	21.7	7.4	78.3
#50	2.1	2.2	24.6	11.3	10.4	88.7
#100	1.9	2.1	7.3	4.2	7.1	95.8
LBW	1.5	1.7	1.8	1.7	2.5	98.3

*Maximum % Retained must be above the 3/8" sieve.
 *Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation Batch Plant Gradations Aggregate Supplier Gradations

Coarseness Factor: **66** **Workability Factor:** **36**

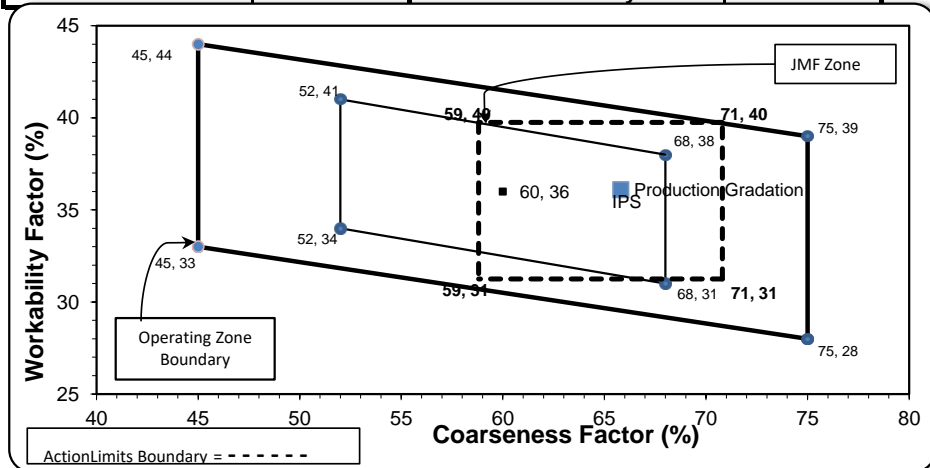

Initial Production Sample (IPS)

Coarseness Factor: **65**
Workability Factor: **36**

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	99.0	0.6	0.6
1"	84.0	15.3	16.0
3/4"	73.5	10.5	26.5
1/2"	65.2	8.2	34.8
3/8"	58.2	7.1	41.8
#4	44.1	14.1	55.9
#8	35.5	8.6	64.5
#16	29.1	6.4	70.9
#30	21.9	7.3	78.1
#50	9.6	12.2	90.4
#100	2.6	7.1	97.4
LBW	1.0	1.6	99.0

PREPARED BY:
 SM, LLC Technical Service

Approved By:

Aggregate Optimization Chart

PLANT #: **P-35**

Sample Date: 12/12/22

Concrete Grade: **P1M, 3500HP**

Dates Test Represents: 12/13/2022 through 12/19/2022

Contractor: _____

MDOT No.: _____

Agg. Class	Pit #	Source	Weight (SSD)	ft ³	Specific Gravity	% Contribution
CA	58-003	Stoneco	1370	8.16	2.69	43.9
IA	58-003	Stoneco	550	3.28	2.69	17.6
2NS	81-019	Pleasant Lake	1200	7.26	2.65	38.5
Total Wt			3120	18.70		100.0

<----- Verify this number is 100%




Superior Materials, LLC
 30701 W. 10 Mile Rd.
 Suite 500
 Farmington Hills, MI 48336

Sieve	CA	IA	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	67.6	100.0	100.0	85.8	14.2	14.2
3/4"	39.1	100.0	100.0	73.3	12.5	26.7
1/2"	13.0	92.9	100.0	60.5	12.7	39.5
3/8"	4.8	74.6	100.0	53.7	6.8	46.3
#4	3.7	22.0	97.9	43.2	10.6	56.8
#8	2.2	6.4	83.2	34.1	9.1	65.9
#16	2.6	4.2	66.3	27.4	6.7	72.6
#30	2.2	3.2	48.0	20.0	7.4	80.0
#50	2.1	2.8	23.4	10.4	9.6	89.6
#100	2.0	2.5	6.6	3.9	6.6	96.1
LBW	1.3	2.0	1.7	1.6	2.3	98.4

*Maximum % Retained must be above the 3/8" sieve.
 *Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation Batch Plant Gradations Aggregate Supplier Gradations

Coarseness Factor: **70** **Workability Factor:** **34**

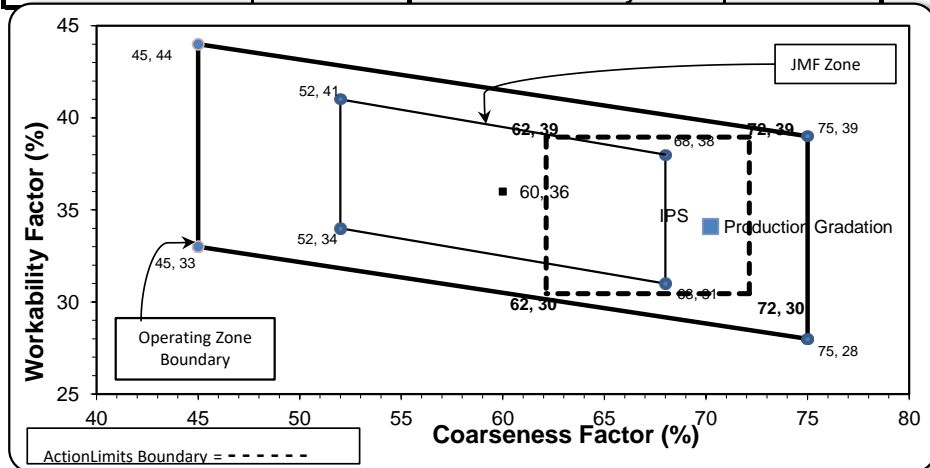

Initial Production Sample (IPS)

Coarseness Factor: **67**
Workability Factor: **35**

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	86.9	13.1	13.1
3/4"	76.1	10.8	23.9
1/2"	63.7	12.4	36.3
3/8"	56.2	7.5	43.8
#4	43.2	13.0	56.8
#8	34.7	8.5	65.3
#16	27.5	7.2	72.5
#30	20.6	7.0	79.4
#50	9.0	11.6	91.0
#100	2.1	6.9	97.9
LBW	1.0	1.1	99.0

PREPARED BY:
 SM, LLC Technical Service

Approved By:

Aggregate Optimization Chart

PLANT #: **P-36**

Sample Date: 12/12/22

Concrete Grade: **P1M, 3500HP**

Dates Test Represents: 12/13/2022 through 12/19/2022

Contractor: _____

MDOT No.: _____

Agg. Class	Pit #	Source	Weight (SSD)	ft ³	Specific Gravity	% Contribution
CA	71-47	Presque Isle	1000	6.12	2.62	32.6
IA	71-47	Presque Isle	870	5.32	2.62	28.3
2NS	63-92	Grange Hall	1200	7.26	2.65	39.1
Total Wt			3070	18.70		100.0

<----- Verify this number is 100%




Superior Materials, LLC
 30701 W. 10 Mile Rd.
 Suite 500
 Farmington Hills, MI 48336

Sieve	CA	IA	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	96.8	100.0	100.0	99.0	1.0	1.0
1"	44.4	100.0	100.0	81.9	17.1	18.1
3/4"	22.1	98.9	100.0	74.3	7.6	25.7
1/2"	11.4	78.2	100.0	65.0	9.4	35.0
3/8"	7.5	53.7	100.0	56.7	8.2	43.3
#4	3.3	9.9	97.6	42.0	14.7	58.0
#8	2.6	3.6	84.6	34.9	7.1	65.1
#16	2.4	2.6	69.6	28.7	6.2	71.3
#30	2.2	2.4	51.0	21.3	7.4	78.7
#50	2.1	2.2	23.0	10.3	11.0	89.7
#100	1.9	2.1	3.5	2.6	7.7	97.4
LBW	1.5	1.7	0.7	1.2	1.3	98.8

*Maximum % Retained must be above the 3/8" sieve.
 *Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation Batch Plant Gradations Aggregate Supplier Gradations

Coarseness Factor:	66	Workability Factor:	35
---------------------------	-----------	----------------------------	-----------

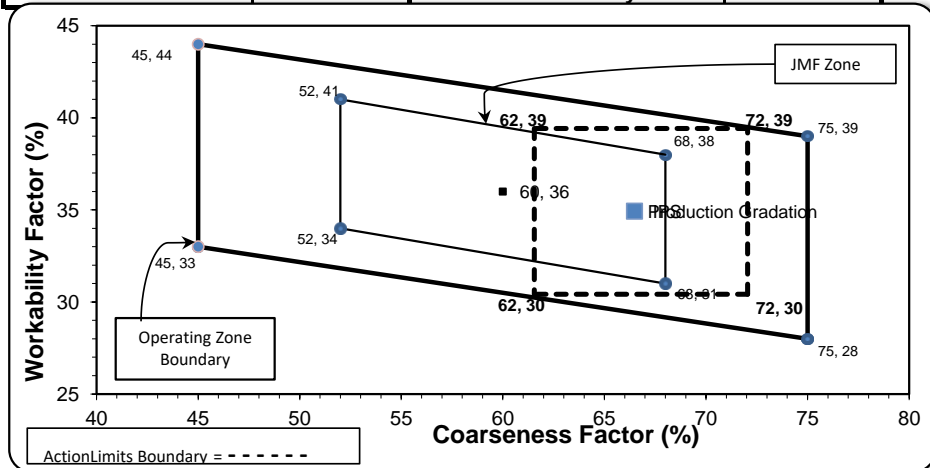

Initial Production Sample (IPS)

Coarseness Factor:	67
Workability Factor:	35

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	85.0	15.0	15.0
3/4"	72.1	12.9	27.9
1/2"	64.5	7.6	35.5
3/8"	56.5	8.0	43.5
#4	42.7	13.8	57.3
#8	34.9	7.8	65.1
#16	29.0	5.9	71.0
#30	21.0	8.0	79.0
#50	8.2	12.8	91.8
#100	1.6	6.5	98.4
LBW	0.7	0.9	99.3

PREPARED BY:
 SM, LLC Technical Service

Approved By:

Aggregate Optimization Chart

PLANT #: **P-39**

Sample Date: 12/12/22

Concrete Grade: **P1M, 3500HP**

Dates Test Represents: 12/13/2022 through 12/19/2022

Contractor: _____

MDOT No.: _____

Agg. Class	Pit #	Source	Weight (SSD)	ft ³	Specific Gravity	% Contribution
CA	71-47	Presque Isle	1020	6.24	2.62	33.2
IA	71-47	Presque Isle	800	4.89	2.62	26.1
2NS	44-051	Krake Willis Rd	1250	7.56	2.65	40.7
Total Wt			3070	18.69		100.0

<----- Verify this number is 100%




Superior Materials, LLC
 30701 W. 10 Mile Rd.
 Suite 500
 Farmington Hills, MI 48336

Sieve	CA	IA	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	98.7	100.0	100.0	99.6	0.4	0.4
1"	47.5	100.0	100.0	82.6	17.0	17.4
3/4"	12.4	98.5	100.0	70.5	12.1	29.5
1/2"	3.0	83.2	100.0	63.4	7.1	36.6
3/8"	2.0	63.7	100.0	58.0	5.4	42.0
#4	1.6	17.3	96.2	44.2	13.8	55.8
#8	1.4	4.5	80.4	34.4	9.8	65.6
#16	1.4	2.7	65.2	27.7	6.7	72.3
#30	1.3	2.3	49.4	21.1	6.6	78.9
#50	1.2	2.1	24.3	10.8	10.3	89.2
#100	1.1	1.9	9.0	4.5	6.3	95.5
LBW	0.9	1.7	0.8	1.1	3.5	98.9

*Maximum % Retained must be above the 3/8" sieve.
 *Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation Batch Plant Gradations Aggregate Supplier Gradations

Coarseness Factor:	64	Workability Factor:	34
---------------------------	-----------	----------------------------	-----------

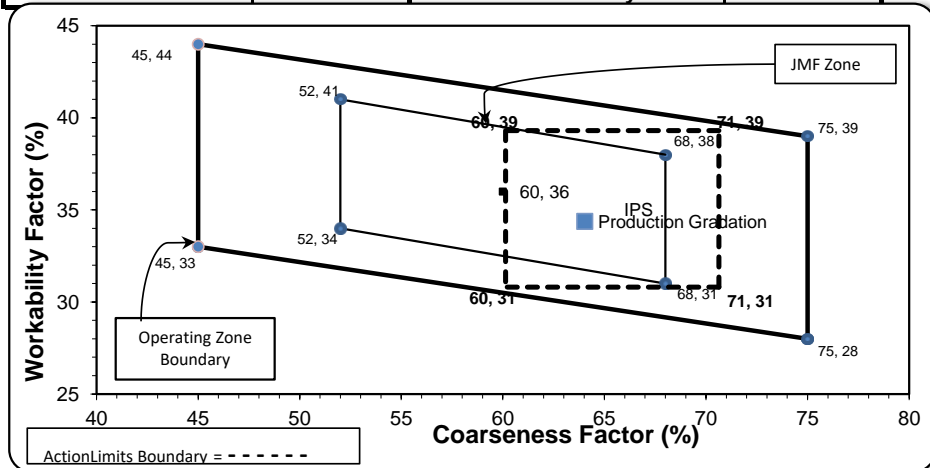

Initial Production Sample (IPS)

Coarseness Factor:	65
Workability Factor:	35

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	99.6	0.4	0.4
1"	83.9	15.7	16.1
3/4"	74.1	9.8	25.9
1/2"	64.3	9.7	35.7
3/8"	57.5	6.8	42.5
#4	44.5	13.1	55.5
#8	35.1	9.4	64.9
#16	27.9	7.2	72.1
#30	21.7	6.2	78.3
#50	12.6	9.1	87.4
#100	3.5	9.1	96.5
LBW	1.2	2.4	98.8

PREPARED BY:
 SM, LLC Technical Service

Approved By:

Aggregate Optimization Chart

PLANT #: **P-02**

Sample Date: 12/12/22

Concrete Grade: **P1M, 3500HP**

Dates Test Represents: 12/13/2022 through 12/19/2022

Contractor: _____

MDOT No.: _____

Agg. Class	Pit #	Source	Weight (SSD)	ft ³	Specific Gravity	% Contribution
CA	71-47	Presque Isle	1020	6.24	2.62	33.2
IA	71-47	Presque Isle	800	4.89	2.62	26.1
2NS	63-115	Ray Rd	1250	7.56	2.65	40.7
Total Wt			3070	18.69		100.0

<----- Verify this number is 100%




Superior Materials, LLC
 30701 W. 10 Mile Rd.
 Suite 500
 Farmington Hills, MI 48336

Sieve	CA	IA	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	96.8	100.0	100.0	98.9	1.1	1.1
1"	44.4	100.0	100.0	81.5	17.4	18.5
3/4"	22.1	98.9	100.0	73.8	7.7	26.2
1/2"	11.4	78.2	100.0	64.9	8.9	35.1
3/8"	7.5	53.7	100.0	57.2	7.7	42.8
#4	3.3	9.9	96.9	43.1	14.1	56.9
#8	2.6	3.6	81.0	34.8	8.3	65.2
#16	2.4	2.6	65.7	28.2	6.6	71.8
#30	2.2	2.4	50.0	21.7	6.5	78.3
#50	2.1	2.2	26.4	12.0	9.7	88.0
#100	1.9	2.1	4.2	2.9	9.1	97.1
LBW	1.5	1.7	0.6	1.2	1.7	98.8

*Maximum % Retained must be above the 3/8" sieve.
 *Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 8% for the 1" sieve when a 2" max. size (nom. Max. 1.5") aggregate is used.

Production Gradation Batch Plant Gradations Aggregate Supplier Gradations

Coarseness Factor: **66** **Workability Factor:** **35**

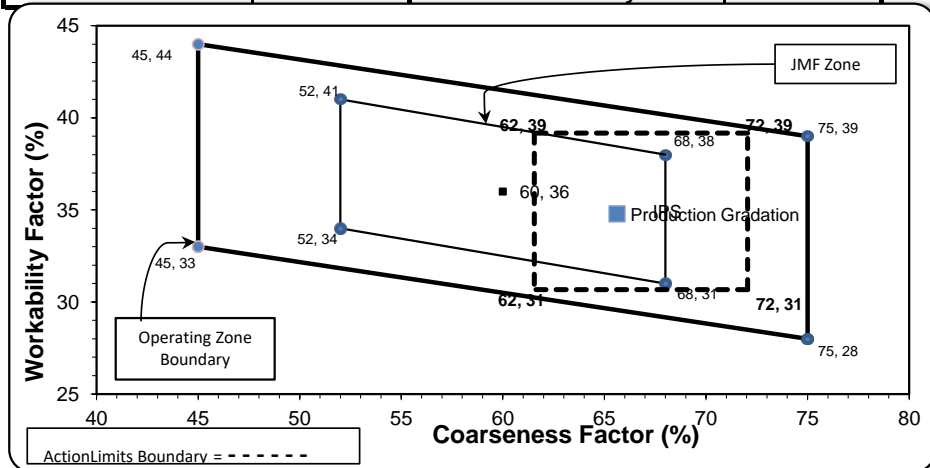

Initial Production Sample (IPS)

Coarseness Factor: **67**
Workability Factor: **35**

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	85.0	15.0	15.0
3/4"	72.3	12.7	27.7
1/2"	64.5	7.8	35.5
3/8"	56.5	8.0	43.5
#4	42.7	13.8	57.3
#8	34.9	7.8	65.1
#16	29.0	5.9	71.0
#30	21.0	8.0	79.0
#50	8.2	12.8	91.8
#100	1.6	6.5	98.4
LBW	0.7	0.9	99.3

PREPARED BY:
 SM, LLC Technical Service

Approved By:
