

Aggregate Optimization Chart

PLANT #: **P-102**

Sample Date: 9/2/24

Concrete Grade: **S2M, 3500HP**

Contractor: _____

Dates Test Represents: 9/3/2024 through 9/9/2024

MDOT No.: _____

Agg. Class	Pit #	Source	Weight (SSD)	ft ³	Specific Gravity	% Contribution
6AA	58-003	Stoneco	1600	9.53	2.69	51.6
26A	58-003	Stoneco	300	1.79	2.69	9.7
2NS	63-114	Highland	1200	7.26	2.65	38.7
Total Wt			3100	18.58		100.0

<----- Verify this number is 100%




Superior Materials, LLC
 30701 W. 10 Mile Rd.
 Suite 500
 Farmington Hills, MI 48336

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	100.0	100.0	100.0	100.0	0.0	0.0
3/4"	82.8	100.0	100.0	91.1	8.9	8.9
1/2"	41.4	98.6	100.0	69.6	21.5	30.4
3/8"	19.9	87.6	100.0	57.5	12.2	42.5
#4	2.8	14.6	99.0	41.2	16.3	58.8
#8	1.4	4.8	85.9	34.4	6.7	65.6
#16	1.0	3.0	69.7	27.8	6.7	72.2
#30	1.0	2.3	51.8	20.8	7.0	79.2
#50	0.9	2.1	23.7	9.8	10.9	90.2
#100	0.9	2.0	4.7	2.5	7.4	97.5
LBW	0.7	1.8	1.1	1.0	1.5	99.0

*Maximum % Retained must be above the 3/8" sieve.
 *Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 4% for the 3/4" sieve when a 1.5" max. size (nom. Max. 1.0") aggregate is used.

Production Gradation Batch Plant Gradations Aggregate Supplier Gradations

Coarseness Factor: **65** **Workability Factor:** **34**

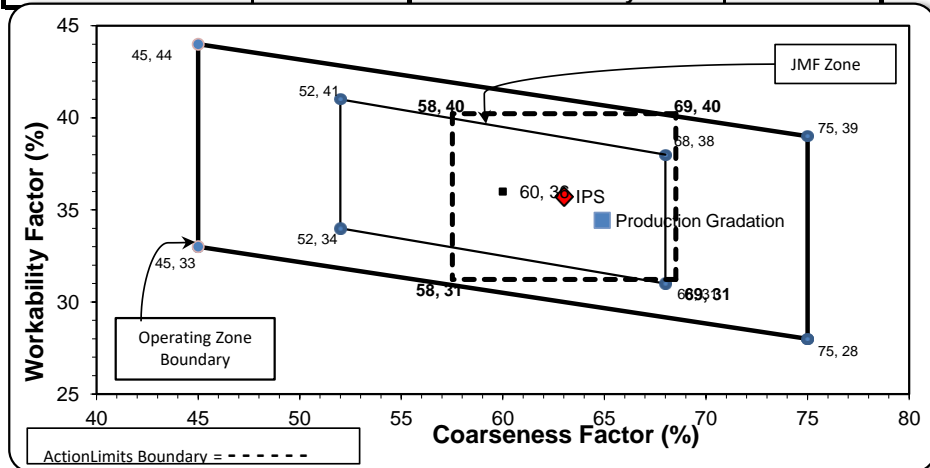

Initial Production Sample (IPS)

Coarseness Factor: **63**
Workability Factor: **36**

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	99.2	0.8	0.8
3/4"	90.9	8.3	9.1
1/2"	71.3	19.6	28.7
3/8"	59.5	11.8	40.5
#4	43.8	15.7	56.2
#8	35.7	8.1	64.3
#16	27.0	8.7	73.0
#30	18.6	8.4	81.4
#50	6.8	11.8	93.2
#100	1.4	5.4	98.6
LBW	0.6	0.8	99.4

PREPARED BY:
 SM, LLC Technical Service

Approved By:

Aggregate Optimization Chart

PLANT #: **P-103**

Sample Date: 9/2/24

Concrete Grade: **S2M, 3500HP**

Dates Test Represents: 9/3/2024 through 9/9/2024

Contractor: _____

MDOT No.: _____

Agg. Class	Pit #	Source	Weight (SSD)	ft ³	Specific Gravity	% Contribution
6AA	58-003	Stoneco	1600	9.53	2.69	51.6
26A	58-003	Stoneco	300	1.79	2.69	9.7
2NS	63-114	Highland	1200	7.26	2.65	38.7
Total Wt			3100	18.58		100.0

<----- Verify this number is 100%




Superior Materials, LLC
 30701 W. 10 Mile Rd.
 Suite 500
 Farmington Hills, MI 48336

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	100.0	100.0	100.0	100.0	0.0	0.0
3/4"	82.8	100.0	100.0	91.1	8.9	8.9
1/2"	41.4	98.6	100.0	69.6	21.5	30.4
3/8"	19.9	87.6	100.0	57.5	12.2	42.5
#4	2.8	14.6	99.0	41.2	16.3	58.8
#8	1.4	4.8	85.9	34.4	6.7	65.6
#16	1.0	3.0	69.7	27.8	6.7	72.2
#30	1.0	2.3	51.8	20.8	7.0	79.2
#50	0.9	2.1	23.7	9.8	10.9	90.2
#100	0.9	2.0	4.7	2.5	7.4	97.5
LBW	0.7	1.8	1.1	1.0	1.5	99.0

*Maximum % Retained must be above the 3/8" sieve.
 *Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 4% for the 3/4" sieve when a 1.5" max. size (nom. Max. 1.0") aggregate is used.

Production Gradation Batch Plant Gradations Aggregate Supplier Gradations

Coarseness Factor: **65** Workability Factor: **34**

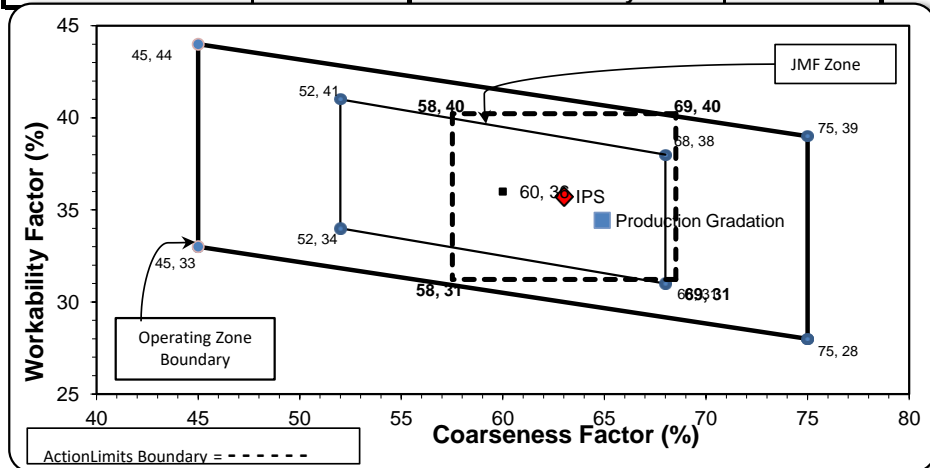

Initial Production Sample (IPS)

Coarseness Factor: **63**
 Workability Factor: **36**

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	99.2	0.8	0.8
3/4"	90.9	8.3	9.1
1/2"	71.3	19.6	28.7
3/8"	59.5	11.8	40.5
#4	43.8	15.7	56.2
#8	35.7	8.1	64.3
#16	27.0	8.7	73.0
#30	18.6	8.4	81.4
#50	6.8	11.8	93.2
#100	1.4	5.4	98.6
LBW	0.6	0.8	99.4

PREPARED BY:
 SM, LLC Technical Service

Approved BY:

Aggregate Optimization Chart

PLANT #: 12

Sample Date: 9/2/24

Concrete Grade: **S2M, 3500HP**

Dates Test Represents: 9/3/2024 through 9/9/2024

Contractor: _____

MDOT No.: _____

Agg. Class	Pit #	Source	Weight (SSD)	ft ³	Specific Gravity	% Contribution
6AA	71-47	Presque Isle	1520	9.30	2.62	49.8
26A	71-47	Presque Isle	300	1.83	2.62	9.8
2NS	63-115	Ray Rd	1230	7.44	2.65	40.3
Total Wt			3050	18.57		100.0

<----- Verify this number is 100%




Superior Materials, LLC
 30701 W. 10 Mile Rd.
 Suite 500
 Farmington Hills, MI 48336

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	94.8	100.0	100.0	97.4	2.6	2.6
3/4"	71.9	100.0	100.0	86.0	11.4	14.0
1/2"	28.0	94.6	100.0	63.6	22.4	36.4
3/8"	14.2	81.1	100.0	55.4	8.2	44.6
#4	3.0	14.1	96.9	42.0	13.4	58.0
#8	1.8	3.2	79.3	33.2	8.8	66.8
#16	1.7	1.9	62.9	26.4	6.8	73.6
#30	1.6	1.7	47.5	20.1	6.3	79.9
#50	1.6	1.6	26.3	11.6	8.6	88.4
#100	1.5	1.6	6.9	3.7	7.9	96.3
LBW	1.3	1.4	0.8	1.1	2.6	98.9

*Maximum % Retained must be above the 3/8" sieve.
 *Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 4% for the 3/4" sieve when a 1.5" max. size (nom. Max. 1.0") aggregate is used.

Production Gradation Batch Plant Gradations Aggregate Supplier Gradations

Coarseness Factor: 67 **Workability Factor:** 33

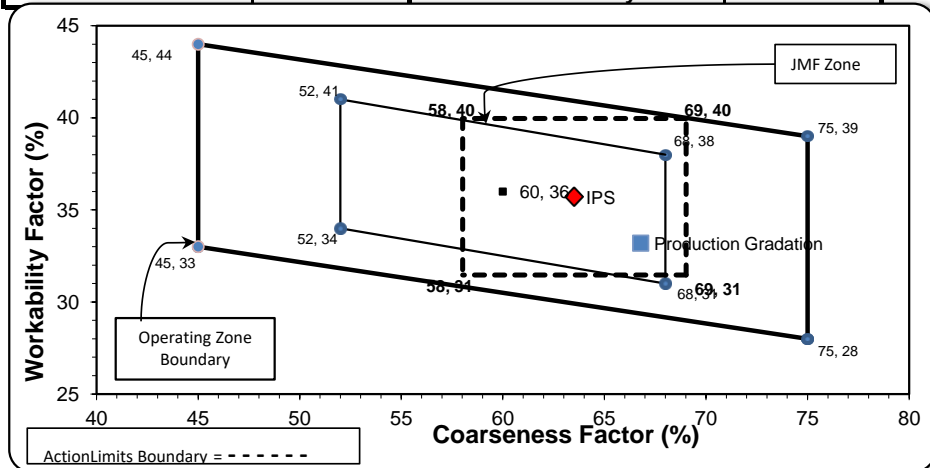

Initial Production Sample (IPS)

Coarseness Factor: 64
Workability Factor: 36

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	99.2	0.8	0.8
3/4"	90.9	8.3	9.1
1/2"	71.3	19.6	28.7
3/8"	59.2	12.1	40.8
#4	41.5	17.7	58.5
#8	35.7	5.8	64.3
#16	27.9	7.9	72.1
#30	18.3	9.5	81.7
#50	7.3	11.0	92.7
#100	2.0	5.3	98.0
LBW	0.9	1.1	99.1

PREPARED BY:
 SM, LLC Technical Service

Approved By:

Aggregate Optimization Chart

PLANT #: p11

Sample Date: 9/2/24

Concrete Grade: **S2M, 3500HP**

Dates Test Represents: 9/3/2024 through 9/9/2024

Contractor: _____

MDOT No.: _____

Agg. Class	Pit #	Source	Weight (SSD)	ft ³	Specific Gravity	% Contribution
6AA	71-47	Presque Isle	1520	9.30	2.62	49.8
26A	71-47	Presque Isle	300	1.83	2.62	9.8
2NS	63-115	Ray Rd	1230	7.44	2.65	40.3
Total Wt			3050	18.57		100.0

<----- Verify this number is 100%




Superior Materials, LLC
 30701 W. 10 Mile Rd.
 Suite 500
 Farmington Hills, MI 48336

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	94.8	100.0	100.0	97.4	2.6	2.6
3/4"	71.9	100.0	100.0	86.0	11.4	14.0
1/2"	28.0	94.6	100.0	63.6	22.4	36.4
3/8"	14.2	81.1	100.0	55.4	8.2	44.6
#4	3.0	14.1	96.9	42.0	13.4	58.0
#8	1.8	3.2	79.3	33.2	8.8	66.8
#16	1.7	1.9	62.9	26.4	6.8	73.6
#30	1.6	1.7	47.5	20.1	6.3	79.9
#50	1.6	1.6	26.3	11.6	8.6	88.4
#100	1.5	1.6	6.9	3.7	7.9	96.3
LBW	1.3	1.4	0.8	1.1	2.6	98.9

*Maximum % Retained must be above the 3/8" sieve.
 *Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 4% for the 3/4" sieve when a 1.5" max. size (nom. Max. 1.0") aggregate is used.

Production Gradation Batch Plant Gradations Aggregate Supplier Gradations

Coarseness Factor: 67 **Workability Factor:** 33

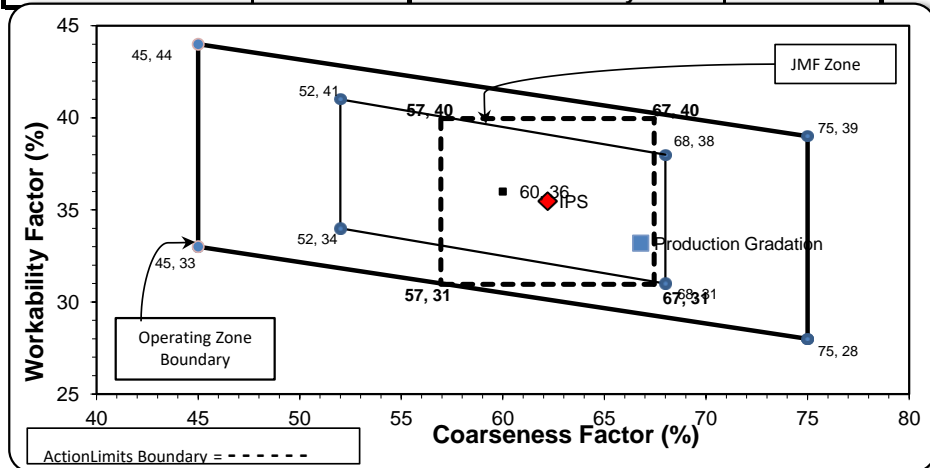

Initial Production Sample (IPS)

Coarseness Factor: 62
Workability Factor: 35

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	100.0	0.0	0.0
3/4"	94.0	6.0	6.0
1/2"	70.2	23.7	29.8
3/8"	59.9	10.4	40.1
#4	42.7	17.2	57.3
#8	35.5	7.2	64.5
#16	28.4	7.0	71.6
#30	19.2	9.2	80.8
#50	8.9	10.3	91.1
#100	3.1	5.9	96.9
LBW	1.4	1.7	98.6

PREPARED BY:
 SM, LLC Technical Service

Approved By:

Aggregate Optimization Chart

PLANT #: **P-35**

Sample Date: 9/2/24

Concrete Grade: **S2M, 3500HP**

Contractor: _____

Dates Test Represents: 9/3/2024 through 9/9/2024

MDOT No.: _____

Agg. Class	Pit #	Source	Weight (SSD)	ft ³	Specific Gravity	% Contribution
6AA	58-003	Stoneco	1600	9.53	2.69	51.6
26A	58-003	Stoneco	300	1.79	2.69	9.7
2NS	81-019	Pleasant Lake	1200	7.26	2.65	38.7
Total Wt			3100	18.58		100.0

<----- Verify this number is 100%




Superior Materials, LLC
 30701 W. 10 Mile Rd.
 Suite 500
 Farmington Hills, MI 48336

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	100.0	100.0	100.0	100.0	0.0	0.0
3/4"	82.8	100.0	100.0	91.1	8.9	8.9
1/2"	41.4	98.6	100.0	69.6	21.5	30.4
3/8"	19.9	87.6	100.0	57.5	12.2	42.5
#4	2.8	14.6	97.3	40.5	16.9	59.5
#8	1.4	4.8	83.4	33.5	7.1	66.5
#16	1.0	3.0	63.7	25.5	8.0	74.5
#30	1.0	2.3	42.9	17.3	8.1	82.7
#50	0.9	2.1	21.7	9.1	8.3	90.9
#100	0.9	2.0	4.8	2.5	6.6	97.5
LBW	0.7	1.8	0.6	0.8	1.7	99.2

*Maximum % Retained must be above the 3/8" sieve.
 *Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 4% for the 3/4" sieve when a 1.5" max. size (nom. Max. 1.0") aggregate is used.

Production Gradation Batch Plant Gradations Aggregate Supplier Gradations

Coarseness Factor:	64	Workability Factor:	33
---------------------------	-----------	----------------------------	-----------

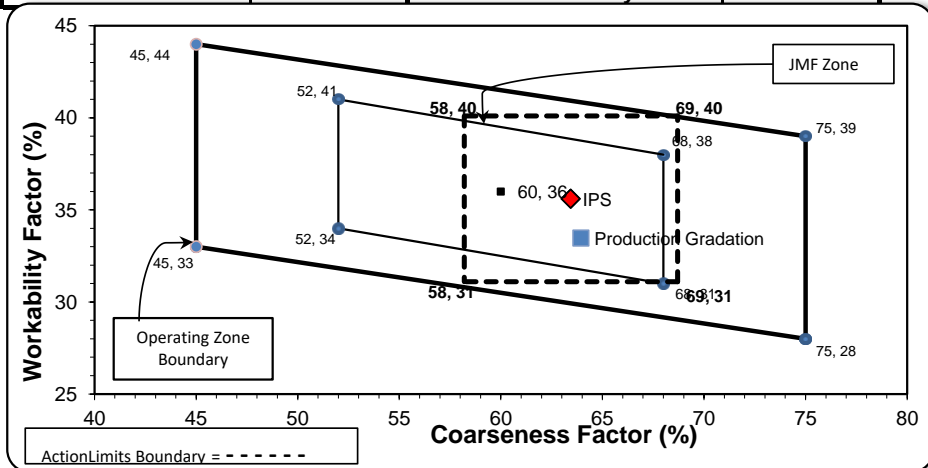

Initial Production Sample (IPS)

Coarseness Factor:	63		
Workability Factor:	36		
Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	100.0	0.0	0.0
3/4"	93.1	6.9	6.9
1/2"	70.0	23.1	30.0
3/8"	59.1	10.9	40.9
#4	46.0	13.1	54.0
#8	35.6	10.4	64.4
#16	27.2	8.4	72.8
#30	19.8	7.4	80.2
#50	10.1	9.7	89.9
#100	2.5	7.6	97.5
LBW	0.9	1.6	99.1

PREPARED BY:
 SM, LLC Technical Service

Approved By:

Aggregate Optimization Chart

PLANT #: **P-38**

Sample Date: 9/2/24

Concrete Grade: **S2M, 3500HP**

Dates Test Represents: 9/3/2024 through 9/9/2024

Contractor: _____

MDOT No.: _____

Agg. Class	Pit #	Source	Weight (SSD)	ft ³	Specific Gravity	% Contribution
6AA	58-003	Stoneco	1600	9.53	2.69	51.6
26A	58-003	Stoneco	300	1.79	2.69	9.7
2NS	81-019	Pleasant Lake	1200	7.26	2.65	38.7
Total Wt			3100	18.58		100.0

<----- Verify this number is 100%




Superior Materials, LLC
 30701 W. 10 Mile Rd.
 Suite 500
 Farmington Hills, MI 48336

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	100.0	100.0	100.0	100.0	0.0	0.0
3/4"	82.8	100.0	100.0	91.1	8.9	8.9
1/2"	41.4	98.6	100.0	69.6	21.5	30.4
3/8"	19.9	87.6	100.0	57.5	12.2	42.5
#4	2.8	14.6	97.3	40.5	16.9	59.5
#8	1.4	4.8	83.4	33.5	7.1	66.5
#16	1.0	3.0	63.7	25.5	8.0	74.5
#30	1.0	2.3	42.9	17.3	8.1	82.7
#50	0.9	2.1	21.7	9.1	8.3	90.9
#100	0.9	2.0	4.8	2.5	6.6	97.5
LBW	0.7	1.8	0.6	0.8	1.7	99.2

*Maximum % Retained must be above the 3/8" sieve.
 *Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 4% for the 3/4" sieve when a 1.5" max. size (nom. Max. 1.0") aggregate is used.

Production Gradation Batch Plant Gradations Aggregate Supplier Gradations

Coarseness Factor:	64	Workability Factor:	33
---------------------------	-----------	----------------------------	-----------

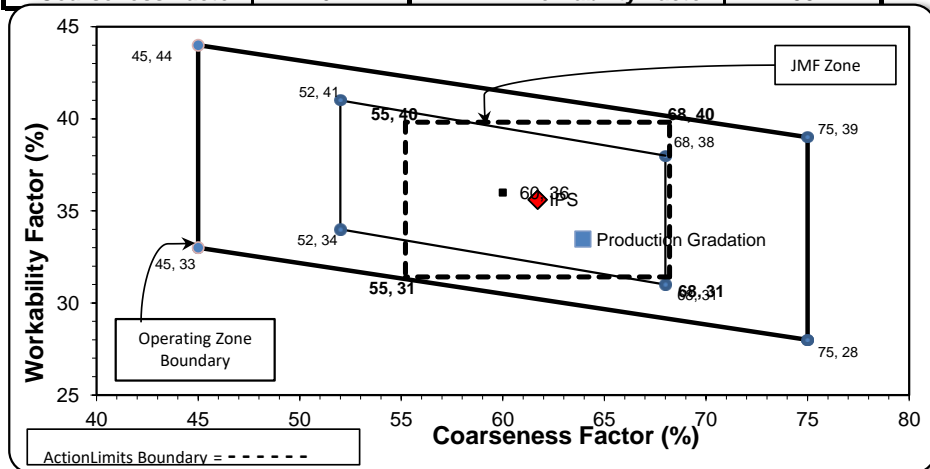

Initial Production Sample (IPS)

Coarseness Factor:	62		
Workability Factor:	36		
Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	99.2	0.8	0.8
3/4"	91.1	8.1	8.9
1/2"	72.0	19.1	28.0
3/8"	60.3	11.7	39.7
#4	43.4	16.9	56.6
#8	35.6	7.8	64.4
#16	28.4	7.2	71.6
#30	21.8	6.7	78.2
#50	9.1	12.6	90.9
#100	1.7	7.4	98.3
LBW	1.1	0.6	98.9

PREPARED BY:
 SM, LLC Technical Service

Approved By:

Aggregate Optimization Chart

PLANT #: **P-02**

Sample Date: 9/2/24

Concrete Grade: **S2M, 3500HP**

Contractor: _____

Dates Test Represents: 9/3/2024 through 9/9/2024

MDOT No.: _____

Agg. Class	Pit #	Source	Weight (SSD)	ft ³	Specific Gravity	% Contribution
6AA	71-47	Presque Isle	1520	9.30	2.62	49.8
26A	71-47	Presque Isle	300	1.83	2.62	9.8
2NS	63-115	Ray Rd	1230	7.44	2.65	40.3
Total Wt			3050	18.57		100.0

<----- Verify this number is 100%




Superior Materials, LLC
 30701 W. 10 Mile Rd.
 Suite 500
 Farmington Hills, MI 48336

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	94.8	100.0	100.0	97.4	2.6	2.6
3/4"	71.9	100.0	100.0	86.0	11.4	14.0
1/2"	28.0	94.6	100.0	63.6	22.4	36.4
3/8"	14.2	81.1	100.0	55.4	8.2	44.6
#4	3.0	14.1	96.9	42.0	13.4	58.0
#8	1.8	3.2	79.3	33.2	8.8	66.8
#16	1.7	1.9	62.9	26.4	6.8	73.6
#30	1.6	1.7	47.5	20.1	6.3	79.9
#50	1.6	1.6	26.3	11.6	8.6	88.4
#100	1.5	1.6	6.9	3.7	7.9	96.3
LBW	1.3	1.4	0.8	1.1	2.6	98.9

*Maximum % Retained must be above the 3/8" sieve.
 *Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 4% for the 3/4" sieve when a 1.5" max. size (nom. Max. 1.0") aggregate is used.

Production Gradation Batch Plant Gradations Aggregate Supplier Gradations

Coarseness Factor:	67	Workability Factor:	33
---------------------------	-----------	----------------------------	-----------

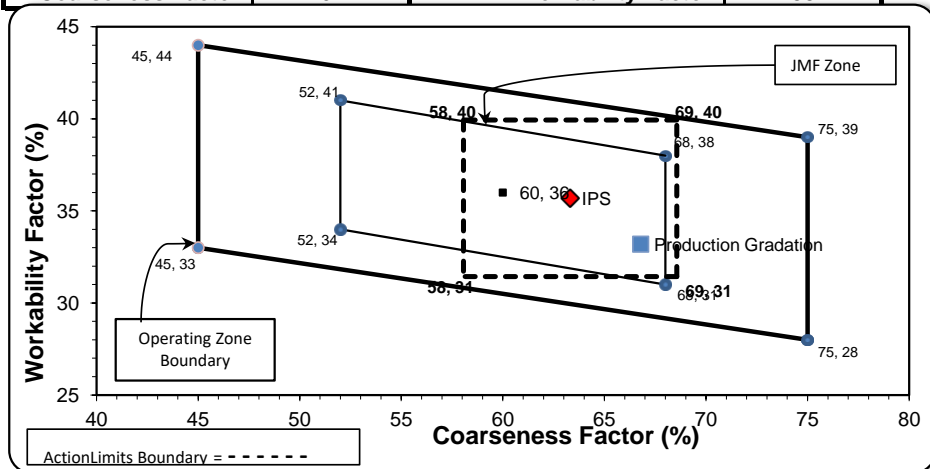

Intial Production Sample (IPS)

Coarseness Factor:	63		
Workability Factor:	36		
Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	100.0	0.0	0.0
3/4"	95.6	4.4	4.4
1/2"	73.1	22.6	26.9
3/8"	59.3	13.8	40.7
#4	42.8	16.5	57.2
#8	35.7	7.1	64.3
#16	28.9	6.8	71.1
#30	20.7	8.2	79.3
#50	9.9	10.8	90.1
#100	2.1	7.8	97.9
LBW	0.9	1.2	99.1

PREPARED BY:
 SM, LLC Technical Service

Approved By:
