

# Aggregate Optimization Chart

# Production Gradation Report

**PLANT #:** P-102

Sample Date: 10/7/24

Concrete Grade: DM, 4500HP

Contractor: \_\_\_\_\_

Dates Test Represents: 10/8/2024 through 10/14/2024

MDOT No.: \_\_\_\_\_

Agg. Class	Pit #	Source	Weight (SSD)	ft <sup>3</sup>	Specific Gravity	% Contribution
6AA	58-003	Stoneco	1450	8.64	2.69	49.2
26A	58-003	Stoneco	350	2.09	2.69	11.9
2NS	63-114	Highland	1150	6.95	2.65	39.0
<b>Total Wt</b>			<b>2950</b>	<b>17.68</b>		<b>100.0</b>

<----- Verify this number is 100%



**Superior Materials, LLC**  
 30701 W. 10 Mile Rd.  
 Suite 500  
 Farmington Hills, MI 48336


Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	99.7	100.0	100.0	99.9	0.1	0.1
3/4"	86.3	100.0	100.0	93.3	6.6	6.7
1/2"	46.5	100.0	100.0	73.7	19.6	26.3
3/8"	20.7	89.5	100.0	59.8	13.9	40.2
#4	3.0	6.7	99.4	41.0	18.8	59.0
#8	1.3	1.5	85.5	34.1	6.9	65.9
#16	1.2	1.2	66.6	26.7	7.5	73.3
#30	1.0	1.0	45.8	18.5	8.2	81.5
#50	1.0	1.0	21.3	8.9	9.6	91.1
#100	1.0	0.9	4.5	2.4	6.6	97.6
LBW	0.8	0.8	0.5	0.7	1.7	99.3

\*Maximum % Retained must be above the 3/8" sieve.  
 \*Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 4% for the 3/4" sieve when a 1.5" max. size (nom. Max. 1.0") aggregate is used.

Production Gradation  Batch Plant Gradations  Aggregate Supplier Gradations  Adjusted WF Initial Production Sample (IPS)

<b>Coarseness Factor:</b>	<b>61</b>	<b>Workability Factor:</b>	<b>34</b>	<b>36.6</b>
---------------------------	-----------	----------------------------	-----------	-------------

<b>Coarseness Factor:</b>	<b>61</b>
<b>Workability Factor:</b>	<b>36</b>

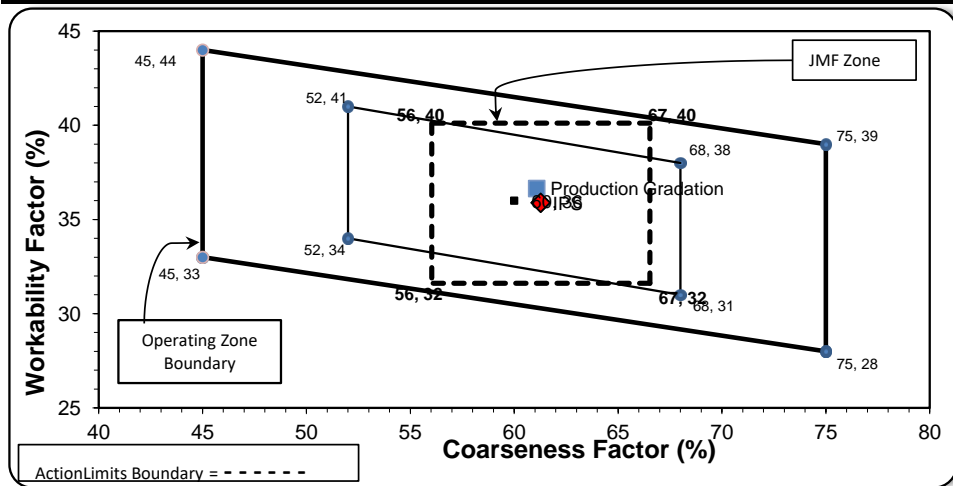

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	99.3	0.7	0.7
3/4"	89.2	10.1	10.8
1/2"	70.7	18.5	29.3
3/8"	60.7	10.0	39.3
#4	44.4	16.3	55.6
#8	35.9	8.5	64.1
#16	27.3	8.6	72.7
#30	19.1	8.2	80.9
#50	7.4	11.7	92.6
#100	1.9	5.6	98.1
LBW	0.7	1.2	99.3

PREPARED BY:  
 SM, LLC Technical Service

Approved By:

# Aggregate Optimization Chart

# Production Gradation Report

**PLANT #:** P-103

Sample Date: 10/7/24

Concrete Grade: DM, 4500HP

Contractor: \_\_\_\_\_

Dates Test Represents: 10/8/2024 through 10/14/2024

MDOT No.: \_\_\_\_\_

Agg. Class	Pit #	Source	Weight (SSD)	ft <sup>3</sup>	Specific Gravity	% Contribution
6AA	58-003	Stoneco	1450	8.64	2.69	49.2
26A	58-003	Stoneco	350	2.09	2.69	11.9
2NS	63-114	Highland	1150	6.95	2.65	39.0
<b>Total Wt</b>			<b>2950</b>	<b>17.68</b>		<b>100.0</b>

<----- Verify this number is 100%



**Superior Materials, LLC**  
 30701 W. 10 Mile Rd.  
 Suite 500  
 Farmington Hills, MI 48336

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	99.7	100.0	100.0	99.9	0.1	0.1
3/4"	86.3	100.0	100.0	93.3	6.6	6.7
1/2"	46.5	100.0	100.0	73.7	19.6	26.3
3/8"	20.7	89.5	100.0	59.8	13.9	40.2
#4	3.0	6.7	99.4	41.0	18.8	59.0
#8	1.3	1.5	85.5	34.1	6.9	65.9
#16	1.2	1.2	66.6	26.7	7.5	73.3
#30	1.0	1.0	45.8	18.5	8.2	81.5
#50	1.0	1.0	21.3	8.9	9.6	91.1
#100	1.0	0.9	4.5	2.4	6.6	97.6
LBW	0.8	0.8	0.5	0.7	1.7	99.3

\*Maximum % Retained must be above the 3/8" sieve.

\*Any two adjacent sieves must equal 10% except max.,

nom. max., #100 and #200 sieves.

\*% Retained must be at least 4% for each sieve except max.,

nom. max., #100 and #200 sieves.

\*% Retained must be at least 4% for the 3/4" sieve when

a 1.5" max. size (nom. Max. 1.0") aggregate is used.

Production Gradation  Batch Plant Gradations  Aggregate Supplier Gradations


Adjusted WF Initial Production Sample (IPS)

<b>Coarseness Factor:</b>	<b>61</b>	<b>Workability Factor:</b>	<b>34</b>	<b>36.6</b>
---------------------------	-----------	----------------------------	-----------	-------------

<b>Coarseness Factor:</b>	<b>61</b>
---------------------------	-----------

<b>Workability Factor:</b>	<b>36</b>
----------------------------	-----------

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	99.3	0.7	0.7
3/4"	89.2	10.1	10.8
1/2"	70.7	18.5	29.3
3/8"	60.7	10.0	39.3
#4	44.4	16.3	55.6
#8	35.9	8.5	64.1
#16	27.3	8.6	72.7
#30	19.1	8.2	80.9
#50	7.4	11.7	92.6
#100	1.9	5.6	98.1
LBW	0.7	1.2	99.3

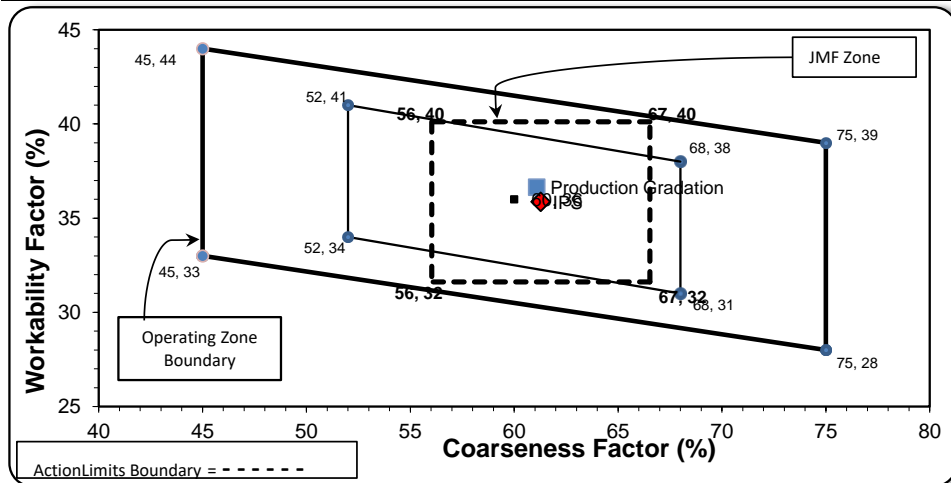

PREPARED BY:  
 SM, LLC Technical Service

Approved BY:

# Aggregate Optimization Chart

**PLANT #:** 12

Sample Date: 10/7/24

Dates Test Represents: 10/8/2024 through 10/14/2024

Concrete Grade: DM, 4500HP

Contractor: \_\_\_\_\_

MDOT No.: \_\_\_\_\_

Agg. Class	Pit #	Source	Weight (SSD)	ft <sup>3</sup>	Specific Gravity	% Contribution
6AA	71-47	Presque Isle	1350	8.26	2.62	46.5
26A	71-47	Presque Isle	405	2.48	2.62	13.9
2NS	63-115	Ray Rd	1150	6.95	2.65	39.6
<b>Total Wt</b>			<b>2905</b>	<b>17.69</b>		<b>100.0</b>

<----- Verify this number is 100%



**Superior Materials, LLC**  
 30701 W. 10 Mile Rd.  
 Suite 500  
 Farmington Hills, MI 48336


Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	97.9	100.0	100.0	99.0	1.0	1.0
3/4"	71.8	100.0	100.0	86.9	12.1	13.1
1/2"	30.4	94.2	100.0	66.8	20.0	33.2
3/8"	14.6	83.6	100.0	58.0	8.8	42.0
#4	2.6	19.6	96.9	42.3	15.7	57.7
#8	2.0	5.2	81.5	33.9	8.4	66.1
#16	1.8	2.6	65.2	27.0	6.9	73.0
#30	1.8	2.0	49.8	20.8	6.2	79.2
#50	1.6	1.9	26.7	11.6	9.3	88.4
#100	1.6	1.8	6.6	3.6	8.0	96.4
LBW	1.4	1.6	0.8	1.2	2.4	98.8

\*Maximum % Retained must be above the 3/8" sieve.  
 \*Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 4% for the 3/4" sieve when a 1.5" max. size (nom. Max. 1.0") aggregate is used.

Production Gradation  Batch Plant Gradations  Aggregate Supplier Gradations

Adjusted WF Initial Production Sample (IPS)

<b>Coarseness Factor:</b>	<b>64</b>	<b>Workability Factor:</b>	<b>34</b>	<b>Adjusted WF</b>	<b>36.4</b>	<b>Coarseness Factor:</b>	<b>63</b>
---------------------------	-----------	----------------------------	-----------	--------------------	-------------	---------------------------	-----------

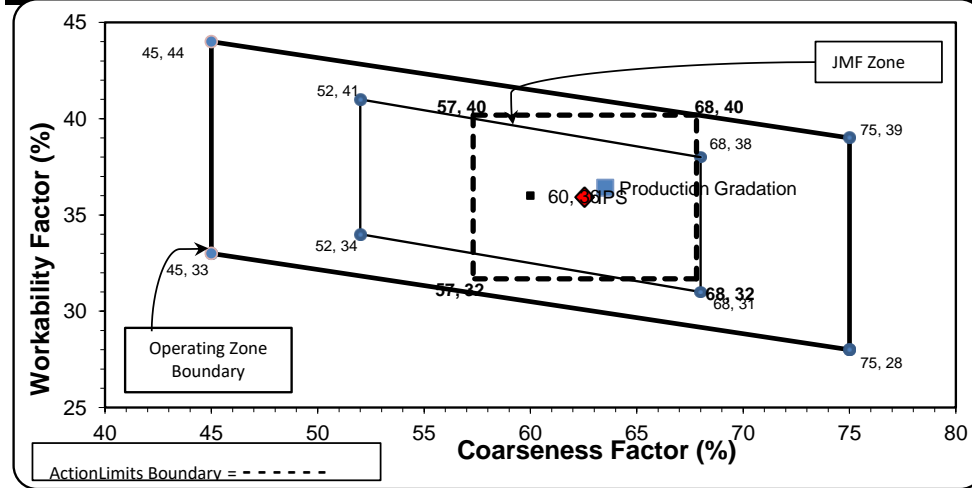

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	99.3	0.7	0.7
3/4"	89.0	10.3	11.0
1/2"	70.3	18.7	29.7
3/8"	59.9	10.4	40.1
#4	41.9	18.0	58.1
#8	35.9	6.0	64.1
#16	27.8	8.2	72.2
#30	18.9	8.8	81.1
#50	6.3	12.6	93.7
#100	1.7	4.6	98.3
LBW	1.0	0.7	99.0

PREPARED BY:  
 SM, LLC Technical Service

Approved By:

# Aggregate Optimization Chart

**PLANT #:** p11

Contractor: \_\_\_\_\_

Sample Date: 10/7/24

Concrete Grade: DM, 4500HP

Dates Test Represents: 10/8/2024 through 10/14/2024

MDOT No.: \_\_\_\_\_

Agg. Class	Pit #	Source	Weight (SSD)	ft <sup>3</sup>	Specific Gravity	% Contribution
6AA	71-47	Presque Isle	1355	8.29	2.62	46.6
26A	71-47	Presque Isle	400	2.45	2.62	13.8
2NS	63-115	Ray Rd	1150	6.95	2.65	39.6
<b>Total Wt</b>			<b>2905</b>	<b>17.69</b>		<b>100.0</b>

<----- Verify this number is 100%



**Superior Materials, LLC**  
 30701 W. 10 Mile Rd.  
 Suite 500  
 Farmington Hills, MI 48336


Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	97.9	100.0	100.0	99.0	1.0	1.0
3/4"	71.8	100.0	100.0	86.8	12.2	13.2
1/2"	30.4	94.2	100.0	66.7	20.1	33.3
3/8"	14.6	83.6	100.0	57.9	8.8	42.1
#4	2.6	19.6	96.9	42.3	15.6	57.7
#8	2.0	5.2	81.5	33.9	8.4	66.1
#16	1.8	2.6	65.2	27.0	6.9	73.0
#30	1.8	2.0	49.8	20.8	6.2	79.2
#50	1.6	1.9	26.7	11.6	9.3	88.4
#100	1.6	1.8	6.6	3.6	8.0	96.4
LBW	1.4	1.6	0.8	1.2	2.4	98.8

\*Maximum % Retained must be above the 3/8" sieve.  
 \*Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 4% for the 3/4" sieve when a 1.5" max. size (nom. Max. 1.0") aggregate is used.

Production Gradation  Batch Plant Gradations  Aggregate Supplier Gradations

Adjusted WF Initial Production Sample (IPS)

<b>Coarseness Factor:</b>	<b>64</b>	<b>Workability Factor:</b>	<b>34</b>	<b>Adjusted WF</b>	<b>36.4</b>	<b>Coarseness Factor:</b>	<b>62</b>
---------------------------	-----------	----------------------------	-----------	--------------------	-------------	---------------------------	-----------

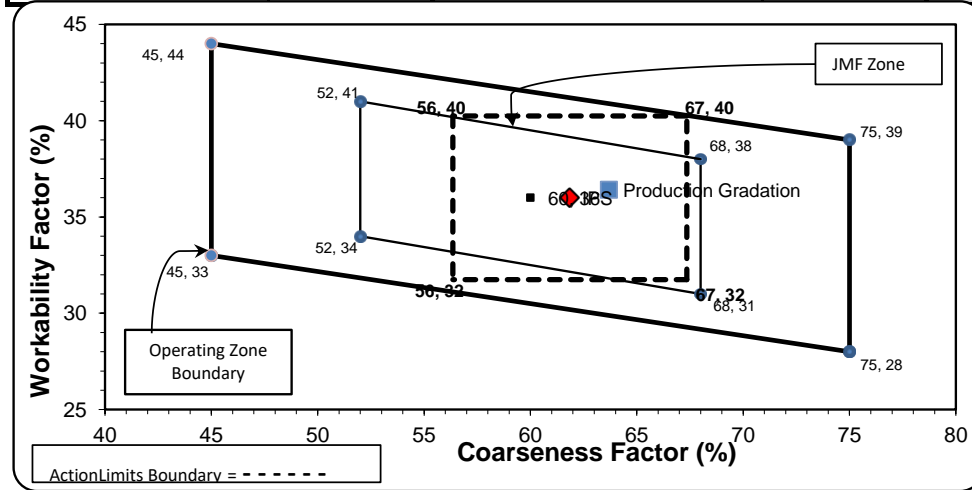

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	100.0	0.0	0.0
3/4"	95.0	5.0	5.0
1/2"	72.3	22.8	27.7
3/8"	60.4	11.8	39.6
#4	42.6	17.8	57.4
#8	36.0	6.6	64.0
#16	29.5	6.5	70.5
#30	20.3	9.2	79.7
#50	9.5	10.8	90.5
#100	3.4	6.1	96.6
LBW	1.3	2.1	98.7

PREPARED BY:  
 SM, LLC Technical Service

Approved By:

# Aggregate Optimization Chart

# Production Gradation Report

**PLANT #:** **P-35**

Sample Date: 10/7/24

Concrete Grade: DM, 4500HP

Contractor: \_\_\_\_\_

Dates Test Represents: 10/8/2024 through 10/14/2024

MDOT No.: \_\_\_\_\_

Agg. Class	Pit #	Source	Weight (SSD)	ft <sup>3</sup>	Specific Gravity	% Contribution
6AA	58-003	Stoneco	1475	8.79	2.69	50.0
26A	58-003	Stoneco	325	1.94	2.69	11.0
2NS	81-019	Pleasant Lake	1150	6.95	2.65	39.0
<b>Total Wt</b>			<b>2950</b>	<b>17.68</b>		<b>100.0</b>

<----- Verify this number is 100%



**Superior Materials, LLC**  
 30701 W. 10 Mile Rd.  
 Suite 500  
 Farmington Hills, MI 48336

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	99.7	100.0	100.0	99.9	0.2	0.2
3/4"	86.3	100.0	100.0	93.2	6.7	6.8
1/2"	46.5	100.0	100.0	73.3	19.9	26.8
3/8"	20.7	89.5	100.0	59.2	14.1	40.8
#4	3.0	6.7	97.6	40.3	18.9	59.7
#8	1.3	1.5	85.3	34.1	6.2	65.9
#16	1.2	1.2	67.4	27.0	7.1	73.0
#30	1.0	1.0	47.1	19.0	8.0	81.0
#50	1.0	1.0	23.2	9.7	9.3	90.3
#100	1.0	0.9	4.9	2.5	7.1	97.5
LBW	0.8	0.8	0.6	0.7	1.8	99.3

\*Maximum % Retained must be above the 3/8" sieve.

\*Any two adjacent sieves must equal 10% except max.,

nom. max., #100 and #200 sieves.

\*% Retained must be at least 4% for each sieve except max.,

nom. max., #100 and #200 sieves.

\*% Retained must be at least 4% for the 3/4" sieve when

a 1.5" max. size (nom. Max. 1.0") aggregate is used.


Production Gradation  Batch Plant Gradations  Aggregate Supplier Gradations

Adjusted WF Initial Production Sample (IPS)

<b>Coarseness Factor:</b>	<b>62</b>	<b>Workability Factor:</b>	<b>34</b>	<b>36.6</b>
---------------------------	-----------	----------------------------	-----------	-------------

<b>Coarseness Factor:</b>	<b>61</b>
---------------------------	-----------

<b>Workability Factor:</b>	<b>36</b>
----------------------------	-----------

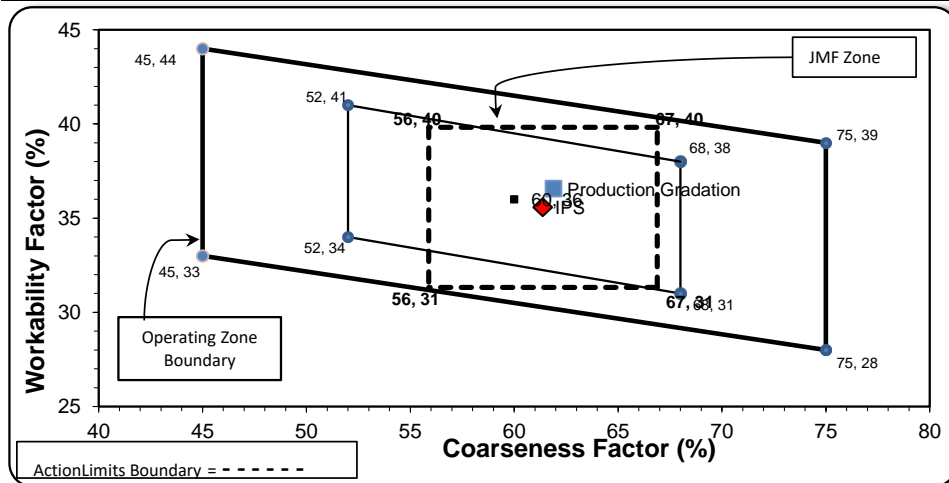

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	99.3	0.7	0.7
3/4"	89.1	10.2	10.9
1/2"	70.5	18.6	29.5
3/8"	60.5	10.0	39.5
#4	44.1	16.4	55.9
#8	35.6	8.5	64.4
#16	27.7	7.9	72.3
#30	20.6	7.1	79.4
#50	8.7	11.8	91.3
#100	1.6	7.1	98.4
LBW	1.1	0.6	98.9

PREPARED BY:  
 SM, LLC Technical Service

Approved By:

# Aggregate Optimization Chart

# Production Gradation Report

**PLANT #:** **P-38**

Sample Date: 10/7/24

Concrete Grade: DM, 4500HP

Contractor: \_\_\_\_\_

Dates Test Represents: 10/8/2024 through 10/14/2024

MDOT No.: \_\_\_\_\_

Agg. Class	Pit #	Source	Weight (SSD)	ft <sup>3</sup>	Specific Gravity	% Contribution
6AA	58-003	Stoneco	1475	8.79	2.69	50.0
26A	58-003	Stoneco	325	1.94	2.69	11.0
2NS	81-019	Pleasant Lake	1150	6.95	2.65	39.0
<b>Total Wt</b>			<b>2950</b>	<b>17.68</b>		<b>100.0</b>

<----- Verify this number is 100%



**Superior Materials, LLC**  
 30701 W. 10 Mile Rd.  
 Suite 500  
 Farmington Hills, MI 48336

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	99.7	100.0	100.0	99.9	0.2	0.2
3/4"	86.3	100.0	100.0	93.2	6.7	6.8
1/2"	46.5	100.0	100.0	73.3	19.9	26.8
3/8"	20.7	89.5	100.0	59.2	14.1	40.8
#4	3.0	6.7	97.6	40.3	18.9	59.7
#8	1.3	1.5	85.3	34.1	6.2	65.9
#16	1.2	1.2	67.4	27.0	7.1	73.0
#30	1.0	1.0	47.1	19.0	8.0	81.0
#50	1.0	1.0	23.2	9.7	9.3	90.3
#100	1.0	0.9	4.9	2.5	7.1	97.5
LBW	0.8	0.8	0.6	0.7	1.8	99.3

\*Maximum % Retained must be above the 3/8" sieve.

\*Any two adjacent sieves must equal 10% except max.,

nom. max., #100 and #200 sieves.

\*% Retained must be at least 4% for each sieve except max.,

nom. max., #100 and #200 sieves.

\*% Retained must be at least 4% for the 3/4" sieve when

a 1.5" max. size (nom. Max. 1.0") aggregate is used.


Production Gradation  Batch Plant Gradations  Aggregate Supplier Gradations

Adjusted WF Initial Production Sample (IPS)

<b>Coarseness Factor:</b>	<b>62</b>	<b>Workability Factor:</b>	<b>34</b>	<b>36.6</b>
---------------------------	-----------	----------------------------	-----------	-------------

<b>Coarseness Factor:</b>	<b>61</b>
---------------------------	-----------

<b>Workability Factor:</b>	<b>36</b>
----------------------------	-----------

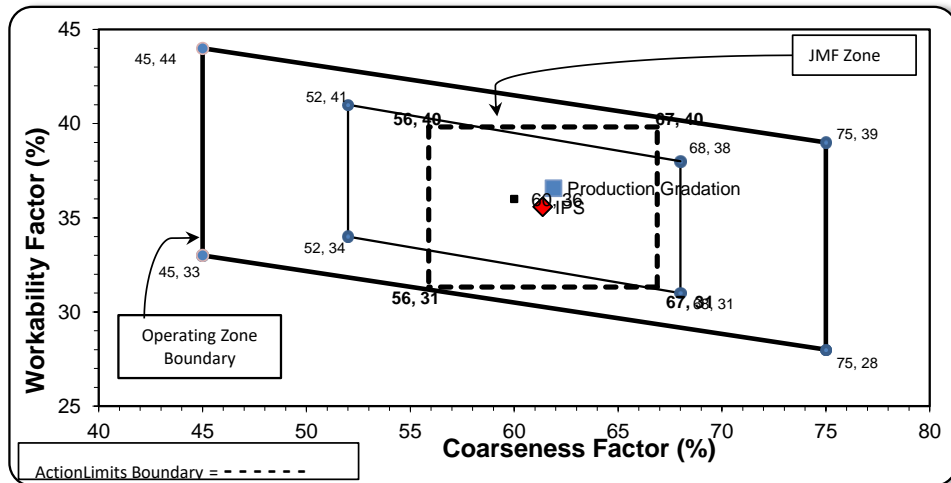

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	99.3	0.7	0.7
3/4"	89.1	10.2	10.9
1/2"	70.5	18.6	29.5
3/8"	60.5	10.0	39.5
#4	44.1	16.4	55.9
#8	35.6	8.5	64.4
#16	27.7	7.9	72.3
#30	20.6	7.1	79.4
#50	8.7	11.8	91.3
#100	1.6	7.1	98.4
LBW	1.1	0.6	98.9

PREPARED BY:  
 SM, LLC Technical Service

Approved By:

# Aggregate Optimization Chart

# Production Gradation Report

**PLANT #:** **P-02**

Sample Date: 10/7/24

Concrete Grade: DM, 4500HP

Contractor: \_\_\_\_\_

Dates Test Represents: 10/8/2024 through 10/14/2024

MDOT No.: \_\_\_\_\_

Agg. Class	Pit #	Source	Weight (SSD)	ft <sup>3</sup>	Specific Gravity	% Contribution
6AA	71-47	Presque Isle	1350	8.26	2.62	46.5
26A	71-47	Presque Isle	405	2.48	2.62	13.9
2NS	63-115	Ray Rd	1150	6.95	2.65	39.6
<b>Total Wt</b>			<b>2905</b>	<b>17.69</b>		<b>100.0</b>

<----- Verify this number is 100%



**Superior Materials, LLC**  
 30701 W. 10 Mile Rd.  
 Suite 500  
 Farmington Hills, MI 48336

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	97.9	100.0	100.0	99.0	1.0	1.0
3/4"	71.8	100.0	100.0	86.9	12.1	13.1
1/2"	30.4	94.2	100.0	66.8	20.0	33.2
3/8"	14.6	83.6	100.0	58.0	8.8	42.0
#4	2.6	19.6	96.9	42.3	15.7	57.7
#8	2.0	5.2	81.5	33.9	8.4	66.1
#16	1.8	2.6	65.2	27.0	6.9	73.0
#30	1.8	2.0	49.8	20.8	6.2	79.2
#50	1.6	1.9	26.7	11.6	9.3	88.4
#100	1.6	1.8	6.6	3.6	8.0	96.4
LBW	1.4	1.6	0.8	1.2	2.4	98.8


\*Maximum % Retained must be above the 3/8" sieve.  
 \*Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.  
 \*% Retained must be at least 4% for the 3/4" sieve when a 1.5" max. size (nom. Max. 1.0") aggregate is used.

Production Gradation  Batch Plant Gradations  Aggregate Supplier Gradations  Adjusted WF Initial Production Sample (IPS)

<b>Coarseness Factor:</b>	<b>64</b>	<b>Workability Factor:</b>	<b>34</b>	<b>Adjusted WF</b>	<b>36.4</b>
---------------------------	-----------	----------------------------	-----------	--------------------	-------------

<b>Coarseness Factor:</b>	<b>63</b>
---------------------------	-----------

<b>Workability Factor:</b>	<b>35</b>
----------------------------	-----------

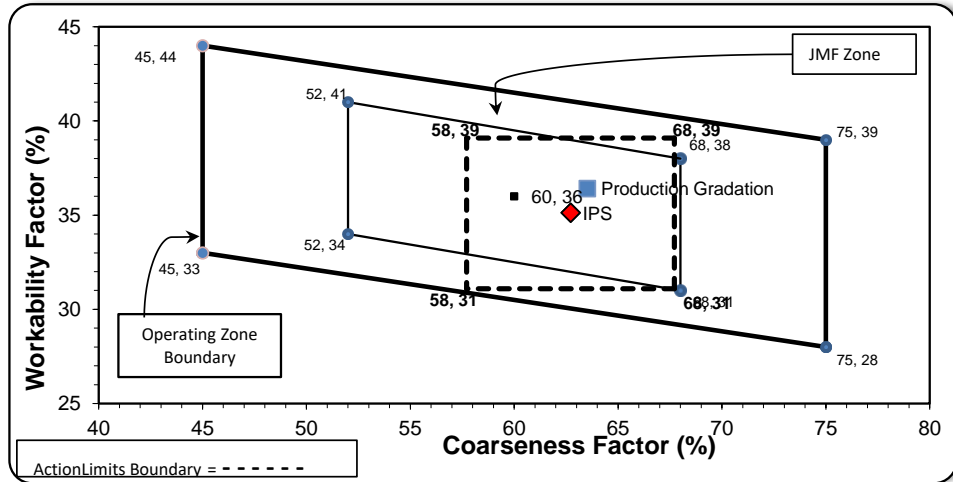

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	100.0	0.0	0.0
3/4"	95.1	4.9	4.9
1/2"	74.6	20.5	25.4
3/8"	59.3	15.3	40.7
#4	42.1	17.2	57.9
#8	35.1	7.1	64.9
#16	29.2	5.9	70.8
#30	21.9	7.3	78.1
#50	9.6	12.4	90.4
#100	2.4	7.2	97.6
LBW	0.9	1.5	99.1

PREPARED BY:  
 SM, LLC Technical Service

Approved By:
