

Aggregate Optimization Chart

PLANT #: **P-102**

Sample Date: 11/18/24

Concrete Grade: **S2M, 3500HP**

Dates Test Represents: 11/19/2024 through 11/25/2024

Contractor: _____

MDOT No.: _____

Agg. Class	Pit #	Source	Weight (SSD)	ft ³	Specific Gravity	% Contribution
6AA	58-003	Stoneco	1550	9.23	2.69	50.0
26A	58-003	Stoneco	350	2.09	2.69	11.3
2NS	63-114	Highland	1200	7.26	2.65	38.7
Total Wt			3100	18.58		100.0

<----- Verify this number is 100%




Superior Materials, LLC
 30701 W. 10 Mile Rd.
 Suite 500
 Farmington Hills, MI 48336

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	100.0	100.0	100.0	100.0	0.0	0.0
3/4"	79.5	100.0	100.0	89.8	10.3	10.3
1/2"	35.7	100.0	100.0	67.9	21.9	32.2
3/8"	14.2	87.8	100.0	55.7	12.1	44.3
#4	1.9	13.4	99.1	40.8	14.9	59.2
#8	1.2	3.7	85.6	34.2	6.7	65.8
#16	1.0	2.0	68.0	27.0	7.1	73.0
#30	0.9	1.5	48.5	19.4	7.7	80.6
#50	0.9	1.3	23.8	9.8	9.6	90.2
#100	0.8	1.2	5.1	2.5	7.3	97.5
LBW	0.8	1.1	0.2	0.6	1.9	99.4

*Maximum % Retained must be above the 3/8" sieve.
 *Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 4% for the 3/4" sieve when a 1.5" max. size (nom. Max. 1.0") aggregate is used.

Production Gradation Batch Plant Gradations Aggregate Supplier Gradations

Coarseness Factor:	67	Workability Factor:	34
---------------------------	-----------	----------------------------	-----------

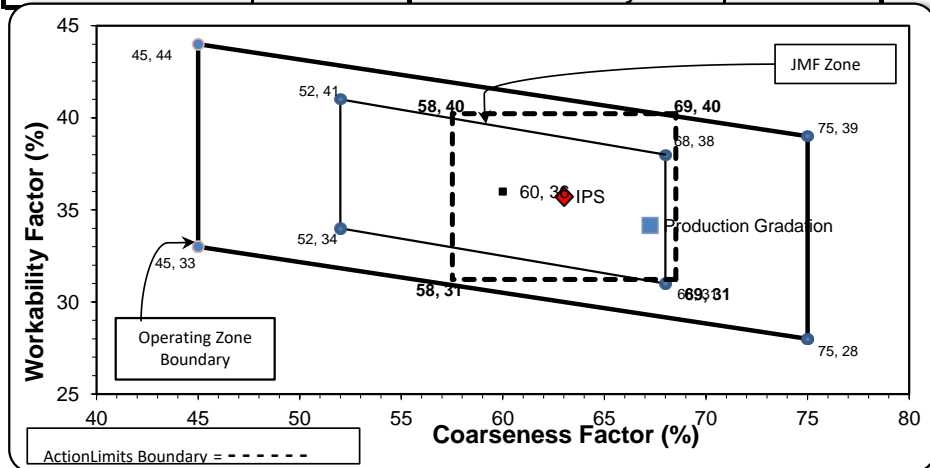

Initial Production Sample (IPS)

Coarseness Factor:	63		
Workability Factor:	36		
Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	99.2	0.8	0.8
3/4"	90.9	8.3	9.1
1/2"	71.3	19.6	28.7
3/8"	59.5	11.8	40.5
#4	43.8	15.7	56.2
#8	35.7	8.1	64.3
#16	27.0	8.7	73.0
#30	18.6	8.4	81.4
#50	6.8	11.8	93.2
#100	1.4	5.4	98.6
LBW	0.6	0.8	99.4

PREPARED BY:
 SM, LLC Technical Service

Approved By:

Aggregate Optimization Chart

PLANT #: **P-103**

Sample Date: 11/18/24

Concrete Grade: **S2M, 3500HP**

Dates Test Represents: 11/19/2024 through 11/25/2024

Contractor: _____

MDOT No.: _____

Agg. Class	Pit #	Source	Weight (SSD)	ft ³	Specific Gravity	% Contribution
6AA	58-003	Stoneco	1550	9.23	2.69	50.0
26A	58-003	Stoneco	350	2.09	2.69	11.3
2NS	63-114	Highland	1200	7.26	2.65	38.7
Total Wt			3100	18.58		100.0

<----- Verify this number is 100%




Superior Materials, LLC
 30701 W. 10 Mile Rd.
 Suite 500
 Farmington Hills, MI 48336

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	100.0	100.0	100.0	100.0	0.0	0.0
3/4"	79.5	100.0	100.0	89.8	10.3	10.3
1/2"	35.7	100.0	100.0	67.9	21.9	32.2
3/8"	14.2	87.8	100.0	55.7	12.1	44.3
#4	1.9	13.4	99.1	40.8	14.9	59.2
#8	1.2	3.7	85.6	34.2	6.7	65.8
#16	1.0	2.0	68.0	27.0	7.1	73.0
#30	0.9	1.5	48.5	19.4	7.7	80.6
#50	0.9	1.3	23.8	9.8	9.6	90.2
#100	0.8	1.2	5.1	2.5	7.3	97.5
LBW	0.8	1.1	0.2	0.6	1.9	99.4

*Maximum % Retained must be above the 3/8" sieve.
 *Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 4% for the 3/4" sieve when a 1.5" max. size (nom. Max. 1.0") aggregate is used.

Production Gradation Batch Plant Gradations Aggregate Supplier Gradations

Coarseness Factor: 67 **Workability Factor:** 34

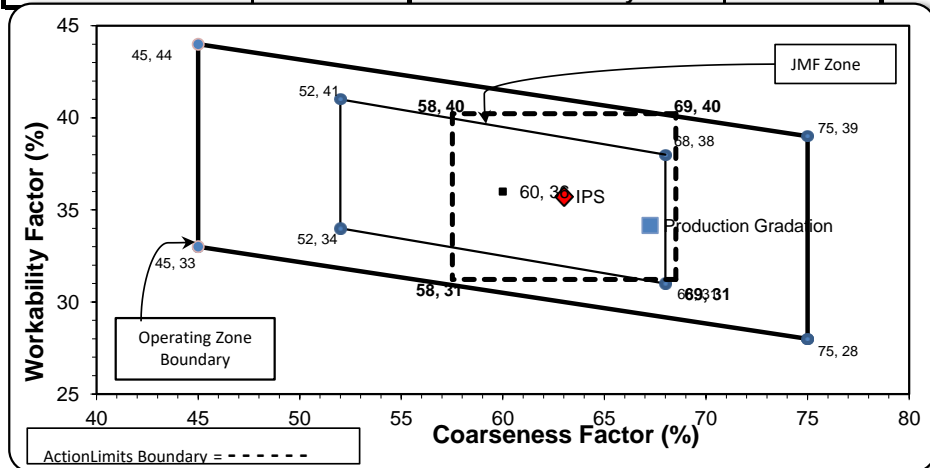

Initial Production Sample (IPS)

Coarseness Factor: 63
Workability Factor: 36

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	99.2	0.8	0.8
3/4"	90.9	8.3	9.1
1/2"	71.3	19.6	28.7
3/8"	59.5	11.8	40.5
#4	43.8	15.7	56.2
#8	35.7	8.1	64.3
#16	27.0	8.7	73.0
#30	18.6	8.4	81.4
#50	6.8	11.8	93.2
#100	1.4	5.4	98.6
LBW	0.6	0.8	99.4

PREPARED BY:
 SM, LLC Technical Service

Approved BY:

Aggregate Optimization Chart

PLANT #: 12

Sample Date: 11/18/24

Concrete Grade: **S2M, 3500HP**

Dates Test Represents: 11/19/2024 through 11/25/2024

Contractor: _____

MDOT No.: _____

Agg. Class	Pit #	Source	Weight (SSD)	ft ³	Specific Gravity	% Contribution
6AA	71-47	Presque Isle	1670	10.21	2.62	54.8
26A	71-47	Presque Isle	150	0.92	2.62	4.9
2NS	63-115	Ray Rd	1230	7.44	2.65	40.3
Total Wt			3050	18.57		100.0

<----- Verify this number is 100%




Superior Materials, LLC
 30701 W. 10 Mile Rd.
 Suite 500
 Farmington Hills, MI 48336

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	99.4	100.0	100.0	99.7	0.3	0.3
3/4"	87.1	100.0	100.0	92.9	6.7	7.1
1/2"	48.8	95.4	100.0	71.7	21.2	28.3
3/8"	30.3	83.4	100.0	61.0	10.7	39.0
#4	6.1	18.9	97.8	43.7	17.3	56.3
#8	2.6	5.0	79.5	33.7	10.0	66.3
#16	2.2	2.9	63.0	26.8	7.0	73.2
#30	2.2	2.5	48.1	20.7	6.0	79.3
#50	2.1	2.3	26.5	11.9	8.8	88.1
#100	2.1	2.2	6.0	3.7	8.3	96.3
LBW	1.9	2.1	1.0	1.5	2.1	98.5

*Maximum % Retained must be above the 3/8" sieve.
 *Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 4% for the 3/4" sieve when a 1.5" max. size (nom. Max. 1.0") aggregate is used.

Production Gradation Batch Plant Gradations Aggregate Supplier Gradations

Coarseness Factor: 59 **Workability Factor:** 34

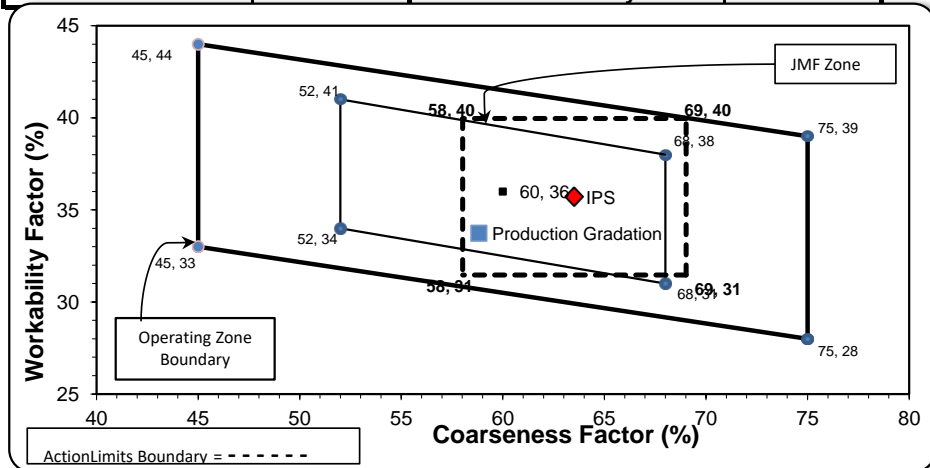

Initial Production Sample (IPS)

Coarseness Factor: 64
Workability Factor: 36

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	99.2	0.8	0.8
3/4"	90.9	8.3	9.1
1/2"	71.3	19.6	28.7
3/8"	59.2	12.1	40.8
#4	41.5	17.7	58.5
#8	35.7	5.8	64.3
#16	27.9	7.9	72.1
#30	18.3	9.5	81.7
#50	7.3	11.0	92.7
#100	2.0	5.3	98.0
LBW	0.9	1.1	99.1

PREPARED BY:
 SM, LLC Technical Service

Approved By:

Aggregate Optimization Chart

PLANT #: p11

Sample Date: 11/18/24

Concrete Grade: **S2M, 3500HP**

Dates Test Represents: 11/19/2024 through 11/25/2024

Contractor: _____

MDOT No.: _____

Agg. Class	Pit #	Source	Weight (SSD)	ft ³	Specific Gravity	% Contribution
6AA	71-47	Presque Isle	1670	10.21	2.62	54.8
26A	71-47	Presque Isle	150	0.92	2.62	4.9
2NS	63-115	Ray Rd	1230	7.44	2.65	40.3
Total Wt			3050	18.57		100.0

<----- Verify this number is 100%




Superior Materials, LLC
 30701 W. 10 Mile Rd.
 Suite 500
 Farmington Hills, MI 48336

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	99.4	100.0	100.0	99.7	0.3	0.3
3/4"	87.1	100.0	100.0	92.9	6.7	7.1
1/2"	48.8	95.4	100.0	71.7	21.2	28.3
3/8"	30.3	83.4	100.0	61.0	10.7	39.0
#4	6.1	18.9	97.8	43.7	17.3	56.3
#8	2.6	5.0	79.5	33.7	10.0	66.3
#16	2.2	2.9	63.0	26.8	7.0	73.2
#30	2.2	2.5	48.1	20.7	6.0	79.3
#50	2.1	2.3	26.5	11.9	8.8	88.1
#100	2.1	2.2	6.0	3.7	8.3	96.3
LBW	1.9	2.1	1.0	1.5	2.1	98.5

*Maximum % Retained must be above the 3/8" sieve.
 *Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 4% for the 3/4" sieve when a 1.5" max. size (nom. Max. 1.0") aggregate is used.

Production Gradation Batch Plant Gradations Aggregate Supplier Gradations

Coarseness Factor: 59 **Workability Factor:** 34

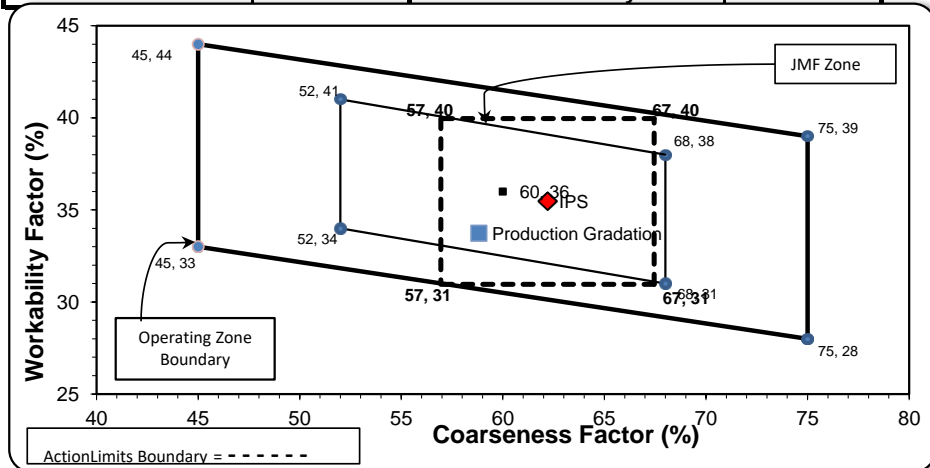

Initial Production Sample (IPS)

Coarseness Factor: 62
Workability Factor: 35

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	100.0	0.0	0.0
3/4"	94.0	6.0	6.0
1/2"	70.2	23.7	29.8
3/8"	59.9	10.4	40.1
#4	42.7	17.2	57.3
#8	35.5	7.2	64.5
#16	28.4	7.0	71.6
#30	19.2	9.2	80.8
#50	8.9	10.3	91.1
#100	3.1	5.9	96.9
LBW	1.4	1.7	98.6

PREPARED BY:
 SM, LLC Technical Service

Approved By:

Aggregate Optimization Chart

PLANT #: **P-02**

Sample Date: 11/18/24

Concrete Grade: **S2M, 3500HP**

Dates Test Represents: 11/19/2024 through 11/25/2024

Contractor: _____

MDOT No.: _____

Agg. Class	Pit #	Source	Weight (SSD)	ft ³	Specific Gravity	% Contribution
6AA	71-47	Presque Isle	1670	10.21	2.62	54.8
26A	71-47	Presque Isle	150	0.92	2.62	4.9
2NS	63-115	Ray Rd	1230	7.44	2.65	40.3
Total Wt			3050	18.57		100.0

<----- Verify this number is 100%




Superior Materials, LLC
 30701 W. 10 Mile Rd.
 Suite 500
 Farmington Hills, MI 48336

Sieve	6AA	26A	2NS	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	100.0	100.0	100.0	0.0	0.0
1.5"	100.0	100.0	100.0	100.0	0.0	0.0
1"	99.4	100.0	100.0	99.7	0.3	0.3
3/4"	87.1	100.0	100.0	92.9	6.7	7.1
1/2"	48.8	95.4	100.0	71.7	21.2	28.3
3/8"	30.3	83.4	100.0	61.0	10.7	39.0
#4	6.1	18.9	97.8	43.7	17.3	56.3
#8	2.6	5.0	79.5	33.7	10.0	66.3
#16	2.2	2.9	63.0	26.8	7.0	73.2
#30	2.2	2.5	48.1	20.7	6.0	79.3
#50	2.1	2.3	26.5	11.9	8.8	88.1
#100	2.1	2.2	6.0	3.7	8.3	96.3
LBW	1.9	2.1	1.0	1.5	2.1	98.5

*Maximum % Retained must be above the 3/8" sieve.
 *Any two adjacent sieves must equal 10% except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 4% for each sieve except max., nom. max., #100 and #200 sieves.
 *% Retained must be at least 4% for the 3/4" sieve when a 1.5" max. size (nom. Max. 1.0") aggregate is used.

Production Gradation Batch Plant Gradations Aggregate Supplier Gradations

Coarseness Factor: 59 **Workability Factor:** 34

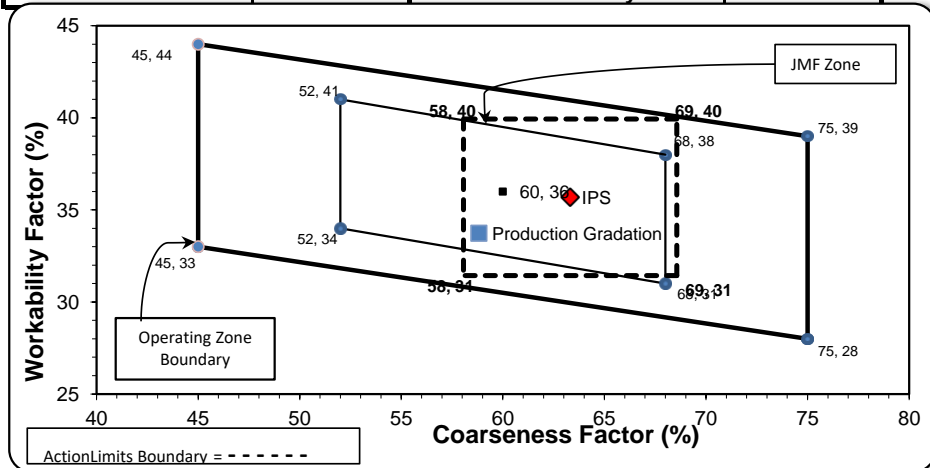

Initial Production Sample (IPS)

Coarseness Factor: 63
Workability Factor: 36

Sieve	Cumulative % Passing	% Retained	Cumulative % Retained
2"	100.0	0.0	0.0
1.5"	100.0	0.0	0.0
1"	100.0	0.0	0.0
3/4"	95.6	4.4	4.4
1/2"	73.1	22.6	26.9
3/8"	59.3	13.8	40.7
#4	42.8	16.5	57.2
#8	35.7	7.1	64.3
#16	28.9	6.8	71.1
#30	20.7	8.2	79.3
#50	9.9	10.8	90.1
#100	2.1	7.8	97.9
LBW	0.9	1.2	99.1

PREPARED BY:
 SM, LLC Technical Service

Approved By:
